Request for Quotation (RFQ) – PEB Storage Shed at Hattar Industrial Estate

From Muhammad Akram <muhammadakram99@gmail.com>
To <info@acco.com.pk>
Date 2025-11-20 23:07

for quote.rar (~536 KB)

Ahmed Construction Company (ACCO Pakistan)
office 2, 3rd Floor, BigCity Plaza, Block E2 Block E Gulberg III, Lahore, 54000
Dear Sir

My name is **M. Akram**, Project Manager at **Lyceum Engineering, Lahore**. We are initiating the construction of a **Pre-Engineered Building (PEB) Storage Shed** located at **Hattar Industrial Estate**.

We are sharing with you the **basic conceptual reference drawings/plans** along with the **Bill of Quantities (BOQ)** for your review. You are requested to kindly provide your **best possible quotation** for the complete scope of work as per the attached BOQ.

In case any information is missing or unclear in the provided documents, you may please **assume standard industrial practices, specifications, or typical design values** to complete your quotation. For any additional clarification, feel free to contact us.

We will appreciate receiving your proposal at your earliest convenience.

Thank you, and we look forward to your competitive quote.

Warm Regards

M. Akram
Project Manager
Lyceum Engineering, Lahore

+923064110220
muhammadakram99@gmail.com

NEW SHED FOR ROP/GP STORAGE					
S.No	**Item Description**	**Quantity**	**Unit**	**Unit Price**	**Amount**
	Demolitioning				
1	Demolition of existing rainwater channels at GP and ROP stores, including dismantling /removal of channel sections, debris disposal, and cleaning of site, complete in all respects.	200	M		
2	Demolition of existing brick work at GP and ROP stores, including dismantling /removal of masonry, debris disposal, and cleaning of site, complete in all respects.	3	M3		
3	Demolition of existing RCC at GP and ROP stores, including dismantling /removal of RCC wall/floor/slab, debris disposal, and cleaning of site, complete in all respects.	3	M3		
	Steel structure				
4	Providing, fabrication, transportation, preparation, and erection of PEB (Pre-Engineered Building) steel members including steel columns, rafters, purlins, girts, bracings, base plates, end plates, anchor bolts, nut & bolts, welding, and all associated accessories, complete in all respects, including one coat of anti-rust primer.	268004	kg		
5	Providing, supplying, and fixing galvanized, proprietary pre-painted corrugated steel sheets of 0.70 mm thickness for roof and wall cladding, including all necessary accessories. Sheets shall be factory-finished, corrosion-resistant, pre-painted GI corrugated steel panels with zinc coating as per ASTM/AISI standards, fixed in position as per manufacturer's recommendations, Including Cutting, bending, and shaping sheets to the required size, Fixing with self-drilling screws, washers, EPDM seals, and overlaps as specified. Providing all flashings, ridges, corner trims, drip trims, and related accessories.	2000	M^2		

S.No	Item Description	Quantity	Unit	Unit Price	Amount
6	Providing, fabricating, and fixing GI (Galvanized Iron) sheet gutter and spout, including complete rainwater downpipe system, manufactured from heavy-duty, corrosion-resistant, galvanized steel sheet of approved gauge (minimum 22–24 SWG), formed to required profile. Work includes all fittings, supports, and accessories necessary to ensure a leak-proof and durable installation.	200	M		
	Civil Works				
7	Providing, supplying, and laying of Plain Cement Concrete (PCC) in foundation works, mix ratio 1:4:8 (Cement: Sand: Coarse Aggregate) with minimum compressive strength of 1500 psi, including necessary formwork, compaction, curing, and finishing, complete in all respects.	26	M3		
8	Providing, supplying, and laying of Reinforced Cement Concrete (RCC) footings for Pedestals with a design compressive strength of 3000 psi (20.7 MPa), including necessary formwork, compaction, and curing, excluding reinforcement, complete in all respects.	53	M3		
9	Providing, supplying, and laying of Reinforced Cement Concrete (RCC) pedestals with a design compressive strength of 3000 psi (20.7 MPa), including necessary formwork, compaction, and curing, excluding reinforcement, complete in all respects	45	M3		
10	Supply, placement, and compaction of suitable soil for filling under floor slabs, in layers not exceeding 150 mm compacted thickness, including watering, mechanical compaction, and all necessary works to achieve maximum dry density as per specifications, complete in all respects.	2200	M3		
11	Supply, placement, and compaction of sand 76.2 mm / 3” for filling under floor slabs, including watering, mechanical compaction, and all necessary works to achieve maximum dry density of filled sand, complete in all respects.	152	M3		

S.No	Item Description	Quantity	Unit	Unit Price	Amount
12	Providing, supplying, and laying of Plain Cement Concrete (PCC) 101.6 mm (4”) thick under RCC flooring, mix ratio 1:4:8 (Cement: Sand: Coarse Aggregate) with minimum compressive strength of 1500 psi, including necessary levelling, compaction, finishing, and curing, complete in all respects.	200	M3		
13	Providing, supplying, and laying of Reinforced Cement Concrete (RCC) 101.6 mm (4”) thick in panels with a design compressive strength of 3000 psi (20.7 MPa), including necessary formwork, compaction, finishing, and curing, excluding the cost of reinforcement, complete in all respects.	200	M3		
14	Providing, supplying, and laying of Reinforced Cement Concrete (RCC) Wall 304.8 mm (12”) thick, 3 meter high with a design compressive strength of 3000 psi (20.7 MPa), including necessary formwork, compaction, finishing, and curing, excluding the cost of reinforcement, complete in all respects.	26	M3		
15	Providing, supplying, and laying of Reinforced Cement Concrete (RCC) Columns 600 mmx600mm (23.622”x23.622") thick, 6 meter high with a design compressive strength of 4500 psi (20.7 MPa), including necessary formwork, compaction, finishing, and curing, excluding the cost of reinforcement, complete in all respects.	9	M3		
16	Providing, supplying, cutting, bending, and fixing of 60-grade steel reinforcement bars conforming to ASTM A615 / A615M Grade 60 or equivalent approved standards for RCC footings, pedestals, beams, slabs, and floors, including all binding, supports, spacers, and necessary accessories, complete in all respects.	21500	KG		
17	Providing, fabricating, and fixing of 6 m × 6 m metal gates, including 14 SWG MS sheet panels, suitable MS angles and flats for frame, heavy-duty hinges, tower bolts, lock arrangements, and all necessary accessories, complete with one coat of anti-corrosive primer.	72	M^2		

S.No	Item Description	Quantity	Unit	Unit Price	Amount
18	Providing, supplying, and fixing of transparent sheets (UV-stabilized transparent sheets, Fixing on roof framing with appropriate fasteners and supports. Sealing joints to ensure watertight performance.) Cutting, trimming, and alignment as per roof profile. for skylights in roof, including supports, fasteners, sealing, and accessories, complete with proper alignment and watertight installation.	20	M^2		
19	**Anti-Corrosive & Acid-Resistant Protective Coating on PEB Steel Structure** Providing and applying a complete anti-corrosive and chemical-resistant protective coating system on all exposed PEB steel structural members, including columns, rafters, bracings, purlins, girts, base plates, and associated steel components. Work includes surface preparation removal of rust, dust, oil, and contaminants. Coating system to comprise the following: Primer Coat: One coat of Zinc-Rich Epoxy Primer, DFT 50–75 microns. Intermediate Coat: One coat of High-Build Epoxy MIO (Micaceous Iron Oxide), DFT 100–150 microns. Finish Coat: One coat of Epoxy Novolac Chemical-Resistant Coating, DFT 150–200 microns, suitable for environments containing sulphuric acid (H_2SO_4) fumes. Total minimum dry film thickness (DFT): 300–400 microns.	425	M^2		
20	**Electrical** Providing, supplying, installing, testing, and commissioning of 100W LED light fixtures, complete with high-efficiency LED driver, housing, mounting brackets, wiring connections, and all necessary accessories, complete in all respects.	20	EA		

S.No	Item Description	Quantity	Unit	Unit Price	Amount
21	Providing, supplying, installing, testing, and commissioning of Main Distribution Board (DB) including all circuit breakers, protective devices, voltmeter, ammeter with selector switches, indicating lights, busbars, internal wiring, earthing connections, labels, and all necessary accessories, complete in all respects.	1	EA		
22	Providing, supplying, installing, testing, and commissioning of heavy-duty industrial exhaust fans (3-phase)1.5kw , complete with motor, blades, protective casing, shutters/louvers, mounting frame, vibration isolators, wiring connections, and all necessary accessories, complete in all respects.	4	EA		
23	Providing, supplying, laying, and installation of main electrical cables and general internal wiring, including conduits, back boxes, junction boxes, supports, and all associated accessories, complete in all respects.	2000	M^2		
24	Providing, supplying, laying, and installation of main electrical cables 4 × 16 mm^2, including conduits, back boxes, junction boxes, supports, and all associated accessories, complete in all respects.	50	M		
25	Providing, supplying, laying, and installation of main electrical cables 4 × 4 mm^2, including conduits, back boxes, junction boxes, supports, and all associated accessories, complete in all respects.	100	M		
26	Providing, supplying, laying, and installation of main electrical Armored cables 3× 2.5 mm^2, including conduits, back boxes, junction boxes, supports, and all associated accessories, complete in all respects.	100	M		
27	Providing, supplying, laying, and installation of main electrical armored cables 2× 2.5 mm^2, including conduits, back boxes, junction boxes, supports, and all associated accessories, complete in all respects.	100	M		

S.No	Item Description	Quantity	Unit	Unit Price	Amount
28	Providing, supplying, and installation of GI cable trays 6"x2" (perforated or ladder type) along walls, including all supports, brackets, fixing accessories, and necessary hardware, complete in all respects, with a minimum thickness of 1.6 mm (16 SWG)	150	M		
29	Providing, supplying, and installation of industrial switch sockets,IP66 class DB, 3Phase 5pin, 32amp including all associated components, mounting accessories, and testing, complete in all respects.	4	EA		
30	Providing, supplying, and installation of industrial switch sockets,IP66, class DB, 1Phase 3pin, 32amp including all associated components, mounting accessories, and testing, complete in all respects.	4	EA		
31	Providing, supplying, and installation of electrical earthing system, including earth rods/plates, backfill materials, connecting conductors, clamps, and all accessories, complete in all respects.	1	LS		
	Total				

NEW SHED FOR ROP/GP STORAGE					
S.No	**Item Description**	**Quantity**	**Unit**	**Unit Price**	**Amount**
	Demolitioning				
1	Demolition of existing rainwater channels at GP and ROP stores, including dismantling /removal of channel sections, debris disposal, and cleaning of site, complete in all respects.	200	M	2,000	400,000
2	Demolition of existing brick work at GP and ROP stores, including dismantling /removal of masonry, debris disposal, and cleaning of site, complete in all respects.	3	M3	3,000	9,000
3	Demolition of existing RCC at GP and ROP stores, including dismantling /removal of RCC wall/floor/slab, debris disposal, and cleaning of site, complete in all respects.	3	M3	5,298	15,894
	Steel structure				
4	Providing, fabrication, transportation, preparation, and erection of PEB (Pre-Engineered Building) steel members including steel columns, rafters, purlins, girts, bracings, base plates, end plates, anchor bolts, nut & bolts, welding, and all associated accessories, complete in all respects, including one coat of anti-rust primer.	268004	kg	450	120,601,800
5	Providing, supplying, and fixing galvanized, proprietary pre-painted corrugated steel sheets of 0.70 mm thickness for roof and wall cladding, including all necessary accessories. Sheets shall be factory-finished, corrosion-resistant, pre-painted GI corrugated steel panels with zinc coating as per ASTM/AISI standards, fixed in position as per manufacturer's recommendations, Including Cutting, bending, and shaping sheets to the required size, Fixing with self-drilling screws, washers, EPDM seals, and overlaps as specified. Providing all flashings, ridges, corner trims, drip trims, and related accessories.	2000	M^2	4,550	9,100,000

S.No	Item Description	Quantity	Unit	Unit Price	Amount
6	Providing, fabricating, and fixing GI (Galvanized Iron) sheet gutter and spout, including complete rainwater downpipe system, manufactured from heavy-duty, corrosion-resistant, galvanized steel sheet of approved gauge (minimum 22–24 SWG), formed to required profile. Work includes all fittings, supports, and accessories necessary to ensure a leak-proof and durable installation.	200	M	1,250	250,000
	Civil Works				
7	Providing, supplying, and laying of Plain Cement Concrete (PCC) in foundation works, mix ratio 1:4:8 (Cement: Sand: Coarse Aggregate) with minimum compressive strength of 1500 psi, including necessary formwork, compaction, curing, and finishing, complete in all respects.	26	M3	16,175	424,594
8	Providing, supplying, and laying of Reinforced Cement Concrete (RCC) footings for Pedestals with a design compressive strength of 3000 psi (20.7 MPa), including necessary formwork, compaction, and curing, excluding reinforcement, complete in all respects.	53	M3	36,000	1,913,625
9	Providing, supplying, and laying of Reinforced Cement Concrete (RCC) pedestals with a design compressive strength of 3000 psi (20.7 MPa), including necessary formwork, compaction, and curing, excluding reinforcement, complete in all respects	45	M3	37,500	1,701,000
10	Supply, placement, and compaction of suitable soil for filling under floor slabs, in layers not exceeding 150 mm compacted thickness, including watering, mechanical compaction, and all necessary works to achieve maximum dry density as per specifications, complete in all respects.	2200	M3	31,788	69,933,600
11	Supply, placement, and compaction of sand 76.2 mm / 3” for filling under floor slabs, including watering, mechanical compaction, and all necessary works to achieve maximum dry density of filled sand, complete in all respects.	152	M3	2,825	430,530

S.No	Item Description	Quantity	Unit	Unit Price	Amount
12	Providing, supplying, and laying of Plain Cement Concrete (PCC) 101.6 mm (4”) thick under RCC flooring, mix ratio 1:4:8 (Cement: Sand: Coarse Aggregate) with minimum compressive strength of 1500 psi, including necessary levelling, compaction, finishing, and curing, complete in all respects.	200	M3	16,953	3,390,600
13	Providing, supplying, and laying of Reinforced Cement Concrete (RCC) 101.6 mm (4”) thick in panels with a design compressive strength of 3000 psi (20.7 MPa), including necessary formwork, compaction, finishing, and curing, excluding the cost of reinforcement, complete in all respects.	200	M3	37,000	7,400,000
14	Providing, supplying, and laying of Reinforced Cement Concrete (RCC) Wall 304.8 mm (12”) thick, 3 meter high with a design compressive strength of 3000 psi (20.7 MPa), including necessary formwork, compaction, finishing, and curing, excluding the cost of reinforcement, complete in all respects.	26	M3	52,000	1,331,366
15	Providing, supplying, and laying of Reinforced Cement Concrete (RCC) Columns 600 mmx600mm (23.622”x23.622") thick, 6 meter high with a design compressive strength of 4500 psi (20.7 MPa), including necessary formwork, compaction, finishing, and curing, excluding the cost of reinforcement, complete in all respects.	9	M3	56,000	483,840
16	Providing, supplying, cutting, bending, and fixing of 60-grade steel reinforcement bars conforming to ASTM A615 / A615M Grade 60 or equivalent approved standards for RCC footings, pedestals, beams, slabs, and floors, including all binding, supports, spacers, and necessary accessories, complete in all respects.	21500	KG	330	7,095,000
17	Providing, fabricating, and fixing of 6 m × 6 m metal gates, including 14 SWG MS sheet panels, suitable MS angles and flats for frame, heavy-duty hinges, tower bolts, lock arrangements, and all necessary accessories, complete with one coat of anti-corrosive primer.	72	M^2	15,602	1,123,344


S.No	Item Description	Quantity	Unit	Unit Price	Amount
18	Providing, supplying, and fixing of transparent sheets (UV-stabilized transparent sheets, Fixing on roof framing with appropriate fasteners and supports. Sealing joints to ensure watertight performance.) Cutting, trimming, and alignment as per roof profile. for skylights in roof, including supports, fasteners, sealing, and accessories, complete with proper alignment and watertight installation.	20	M^2	6,000	120,000
19	**Anti-Corrosive & Acid-Resistant Protective Coating on PEB Steel Structure** Providing and applying a complete anti-corrosive and chemical-resistant protective coating system on all exposed PEB steel structural members, including columns, rafters, bracings, purlins, girts, base plates, and associated steel components. Work includes surface preparation removal of rust, dust, oil, and contaminants. Coating system to comprise the following:	425	M^2	1,291	548,675
	Primer Coat: One coat of Zinc-Rich Epoxy Primer, DFT 50–75 microns. Intermediate Coat: One coat of High-Build Epoxy MIO (Micaceous Iron Oxide), DFT 100–150 microns. Finish Coat: One coat of Epoxy Novolac Chemical-Resistant Coating, DFT 150–200 microns, suitable for environments containing sulphuric acid (H_2SO_4) fumes. Total minimum dry film thickness (DFT): 300–400 microns.				
	Electrical				
20	Providing, supplying, installing, testing, and commissioning of 100W LED light fixtures, complete with high-efficiency LED driver, housing, mounting brackets, wiring connections, and all necessary accessories, complete in all respects.	20	EA	20,000	400,000


S.No	Item Description	Quantity	Unit	Unit Price	Amount
21	Providing, supplying, installing, testing, and commissioning of Main Distribution Board (DB) including all circuit breakers, protective devices, voltmeter, ammeter with selector switches, indicating lights, busbars, internal wiring, earthing connections, labels, and all necessary accessories, complete in all respects.	1	EA	114,000	114,000
22	Providing, supplying, installing, testing, and commissioning of heavy-duty industrial exhaust fans (3-phase)1.5kw , complete with motor, blades, protective casing, shutters/louvers, mounting frame, vibration isolators, wiring connections, and all necessary accessories, complete in all respects.	4	EA	220,000	880,000
23	Providing, supplying, laying, and installation of main electrical cables and general internal wiring, including conduits, back boxes, junction boxes, supports, and all associated accessories, complete in all respects.	2000	M^2	2,500	5,000,000
24	Providing, supplying, laying, and installation of main electrical cables 4 × 16 mm^2, including conduits, back boxes, junction boxes, supports, and all associated accessories, complete in all respects.	50	M	153,000	7,650,000
25	Providing, supplying, laying, and installation of main electrical cables 4 × 4 mm^2, including conduits, back boxes, junction boxes, supports, and all associated accessories, complete in all respects.	100	M	85,200	8,520,000
26	Providing, supplying, laying, and installation of main electrical Armored cables 3× 2.5 mm^2, including conduits, back boxes, junction boxes, supports, and all associated accessories, complete in all respects.	100	M	51,000	5,100,000
27	Providing, supplying, laying, and installation of main electrical armored cables 2× 2.5 mm^2, including conduits, back boxes, junction boxes, supports, and all associated accessories, complete in all respects.	100	M	36,000	3,600,000


S.No	Item Description	Quantity	Unit	Unit Price	Amount
28	Providing, supplying, and installation of GI cable trays 6"x2" (perforated or ladder type) along walls, including all supports, brackets, fixing accessories, and necessary hardware, complete in all respects, with a minimum thickness of 1.6 mm (16 SWG)	150	M	5,500	825,000
29	Providing, supplying, and installation of industrial switch sockets,IP66 class DB, 3Phase 5pin, 32amp including all associated components, mounting accessories, and testing, complete in all respects.	4	EA	18,000	72,000
30	Providing, supplying, and installation of industrial switch sockets,IP66, class DB, 1Phase 3pin, 32amp including all associated components, mounting accessories, and testing, complete in all respects.	4	EA	8,400	33,600
31	Providing, supplying, and installation of electrical earthing system, including earth rods/plates, backfill materials, connecting conductors, clamps, and all accessories, complete in all respects.	1	LS	350,000	350,000
	Total				**258,817,468**




			MUHAMMAD FAHAD (ELECTRICAL ENGINEER)	QURBAN ALI (SENIOR MANAGER)
REV	DATE	DESCRIPTION OF REVISION	DRAWN BY	APPROVED BY
AGRI TECH - HPFP ALL OVER AND BEYOND			CREATION DATE	1-Nov-25
			VIEW TYPE	TOP VIEW
			CALCULATIONS	
NEW GP ROP STORE			TOTAL WIDTH OF STORE	22.864 meter
POWER & LIGHTING CIRCUIT LAYOUT			TOTAL LENGTH OF STORE	97.700 meter

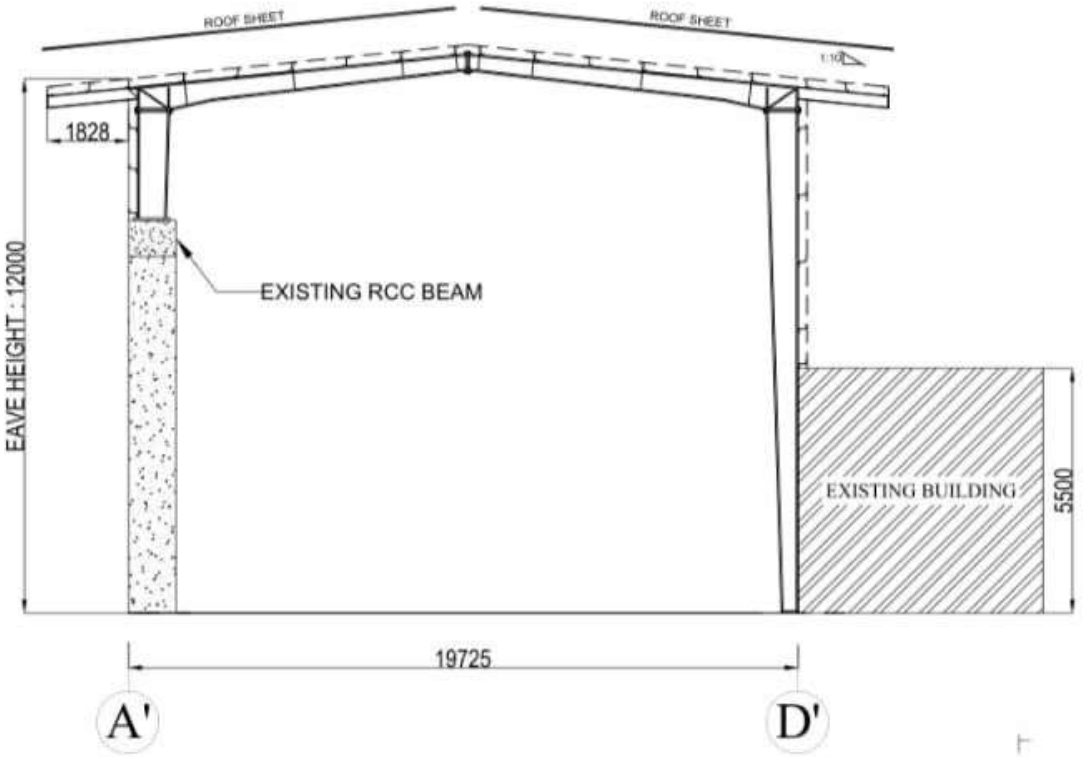
ROOF SHEET
ROOF SHEET
1:10
1828
EAVE HEIGHT : 12000
EXISTING RCC BEAM
EXISTING BUILDING
5500
19725
A'
D'

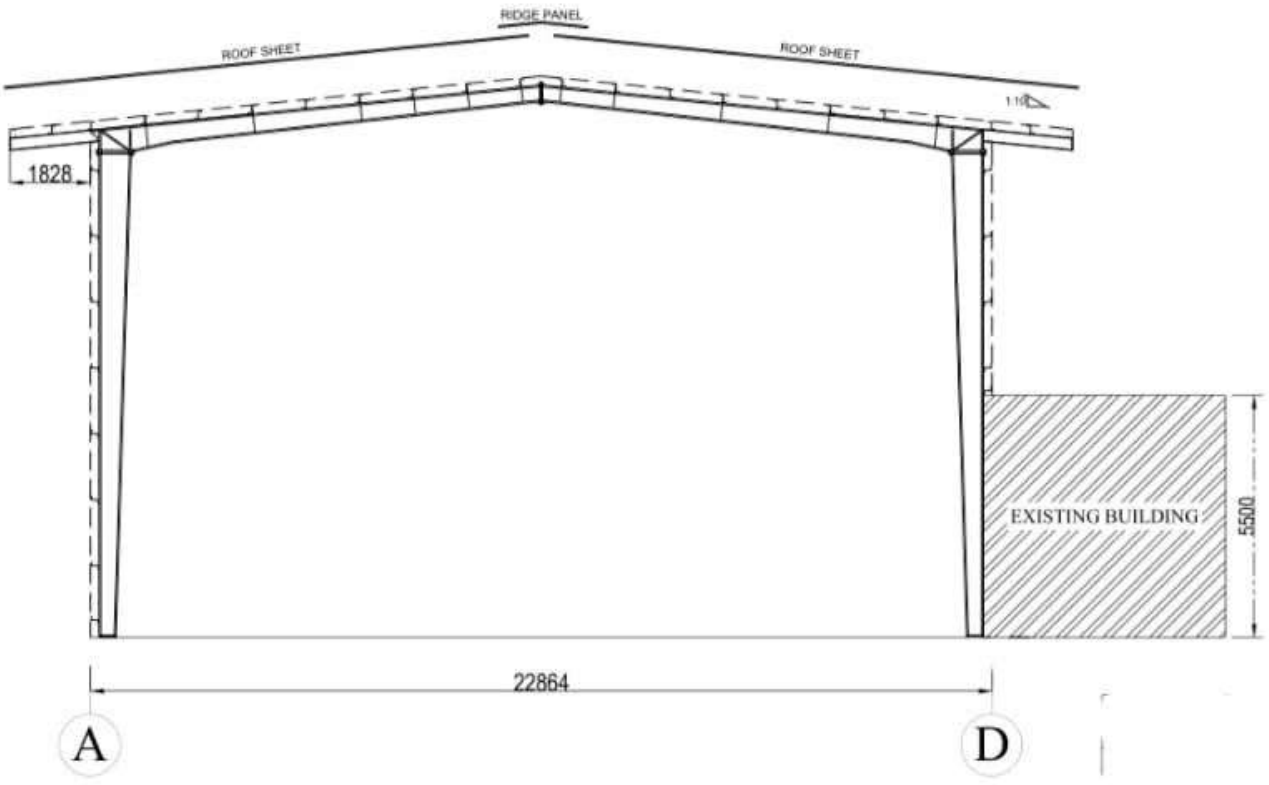
RIDGE PANEL
ROOF SHEET
ROOF SHEET
1:10
1828
EXISTING BUILDING
5500
22864
A
D

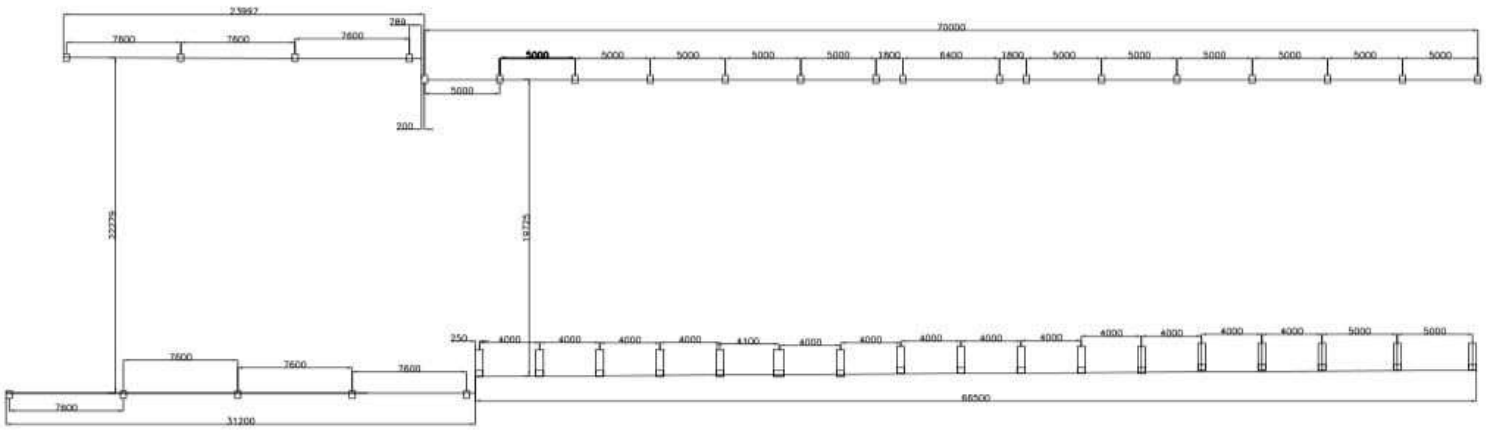

EXISTING PLAN

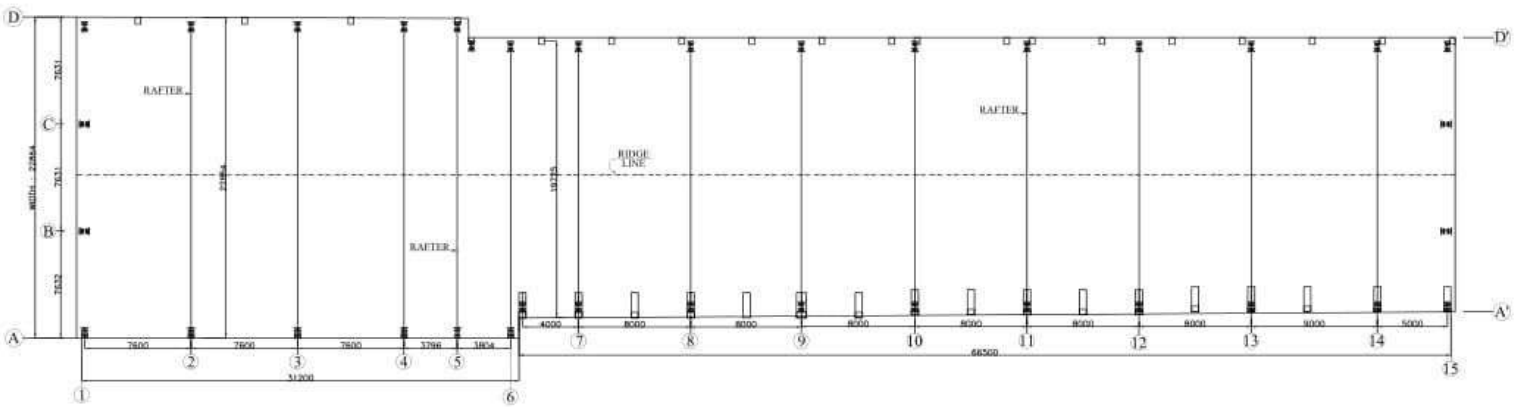

ANCHOR BOLT LAYOUT PLAN
