To,
Hassan butt

Date: July 21, 2025
Ref No: ACCO/QTSN/379

SUBJECT: QUOTATION FOR CONSTRUCTION OF PEB WAREHOUSE AT PADEL COURT, LAHORE (AREA 9,188.00 SFT. APPROX HEIGHTS 36'00")

Dear Sir,

We are pleased to submit the requisite Technical & Commercial document for the contractual agreement in accordance with your inquiry and input. The detailed parameters for this particular job have been mentioned in the sections below.

SR	SCOPE OF WORK	AREA	RATE	AMOUNT (Rs.)	REMARKS
1	1- Fabrication & supply of complete pre-engineered steel Building system incl. steel columns and rafters, wall and roof purlins, wall and roof pre-painted 50 mm thick Glass wool 2- Sides' walls & roof sheeting.	9,188.00	1350	12,403,800.00	
				12,403,800.00	

TERMS & CONDITIONS: -

MODE OF PAYMENT (Without Taxes):

1. 60% on the time of start the work.
2. 20% on the Dispatch time of Pre-Engineering Framework.
3. 15% on the erection time.
4. 5% on the Completion time.
5. Civil works not including in this quotation.
6. Bills shall be paid within 7 days the after the submission.
7. The prices are based on mentioned items in BOQ. Any additional items from BOQ shall be claim separately.
8. Cordon off Area and Debris removal from site shall be paid by Client.
9. Provision of all accessibility to working area, Provision of storage facilities for our goods and equipment, where necessary, water & Electricity shall be provided the d by the client.


We will be obliged for your Cooperation in this regard.

With best regards,

Tanveer Ahmed
DIRECTOR

Product description

1. Building System

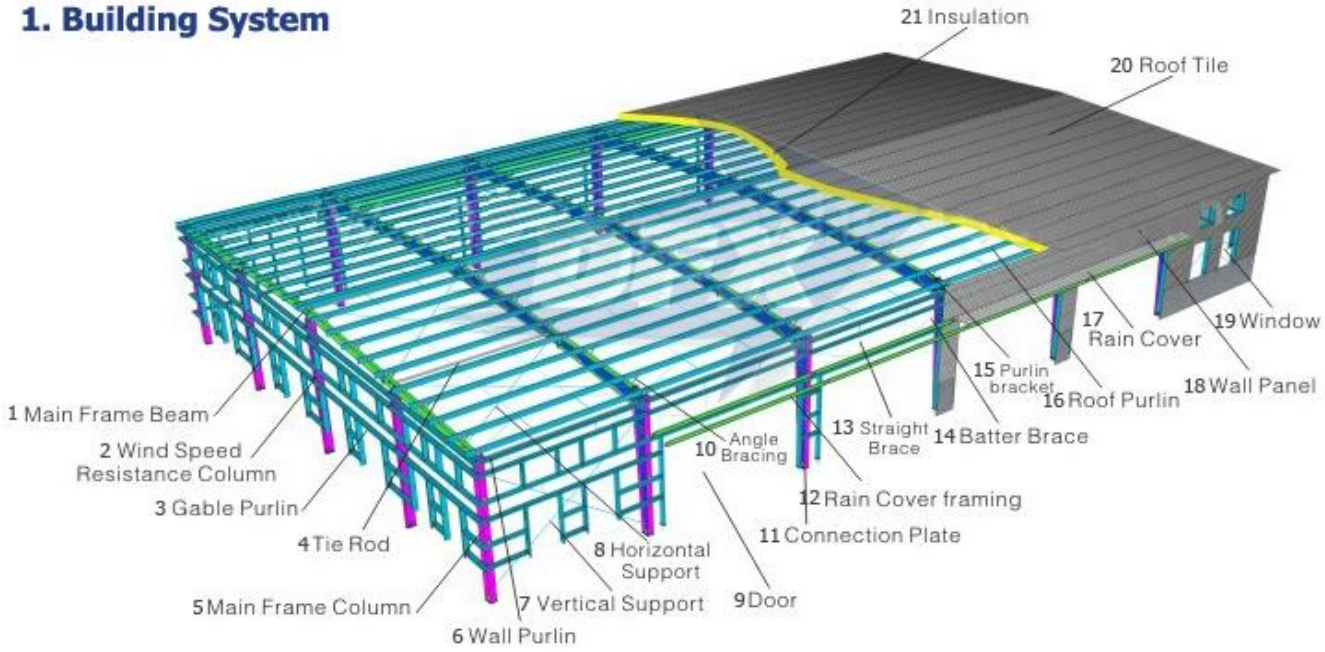

2. Specification

Items		Specification
Main Steel Frame	Flanges	5-6-8-10 mm
	Anchor Bolts	24 mm
	Purlin	1.5mm 8" (150 microns)
	Base plate	20-25mm
	Connection plates	16-20mm
	Wire Bracing	12mm
	Sheet	0.5mm
Maintenance system	Roof Panel	50mm Glass Wool Panel / Corrugated Steel Sheet
	Wall Panel	Corrugated Steel Sheet 0.50 mm thick average
Accessories	Window	Nill
	Door	Sliding Door / Rolling Metal Door / Personal Door 16 g
	Rainspout	Nill
Live load on Roof		0.57 (kN/m2) (Color steel panel surrounded)
Live load on Frame		0.57 (kN/m2)
Wind Resistance (km/hr)		16 (Exposure C)
Seismic Zone		2-B
Structure Usage		Up to 50 years
Finishing Options		Vast array of colors and textures available

Paint Options	Alkyd painting, two primary painting, two finish painting (gray paint, red paint, white paint etc.) Or Galvanized.

3. Detailed Images



RELATED PRODUCTS

