To,
AD Junaid

Date: August 16, 2025
Ref No: ACCO/QTSN/428

**SUBJECT: QUOTATION FOR CONSTRUCTION OF PEB WAREHOUSE AT DHA QUETTA (AREA 7,500.00 SFT. APPROX HEIGHTS 18'00")**

Dear Sir,

We are pleased to submit the requisite Technical & Commercial document for the contractual agreement in accordance with your inquiry and input. The detailed parameters for this particular job have been mentioned in the sections below.

| SR | SCOPE OF WORK | AREA | RATE | AMOUNT (Rs.) | REMARKS |
|---|---|---|---|---|---|
| 1 | 1- Fabrication & supply of complete pre-engineered steel Building system incl. steel columns and rafters, wall and roof purlins, wall and roof pre-painted 50 mm thick Glass wool<br><br>Shade height center 18'-00"<br>Side walls heights 18'-00"<br>2- Sides' walls & roof sheeting. | 7,500.00 | 1500 | 10,500,000.00 | |
| | | | | **10,500,000.00** | |

**TERMS & CONDITIONS: -**

**MODE OF PAYMENT (Without Taxes):**

1. 60% on the time of start the work.
2. 20% on the Dispatch time of Pre-Engineering Framework.
3. 15% on the erection time.
4. 5% on the Completion time.
5. Civil works not including in this quotation.
6. Bills shall be paid within 7 days the after the submission.
7. The prices are based on mentioned items in BOQ. Any additional items from BOQ shall be claim separately.
8. Cordon off Area and Debris removal from site shall be paid by Client.
9. Provision of all accessibility to working area, Provision of storage facilities for our goods and equipment, where necessary, water & Electricity shall be provided the d by the client.


We will be obliged for your Cooperation in this regard.

With best regards,

**Tanveer Ahmed**
**DIRECTOR**

## Product description

### 1. Building System

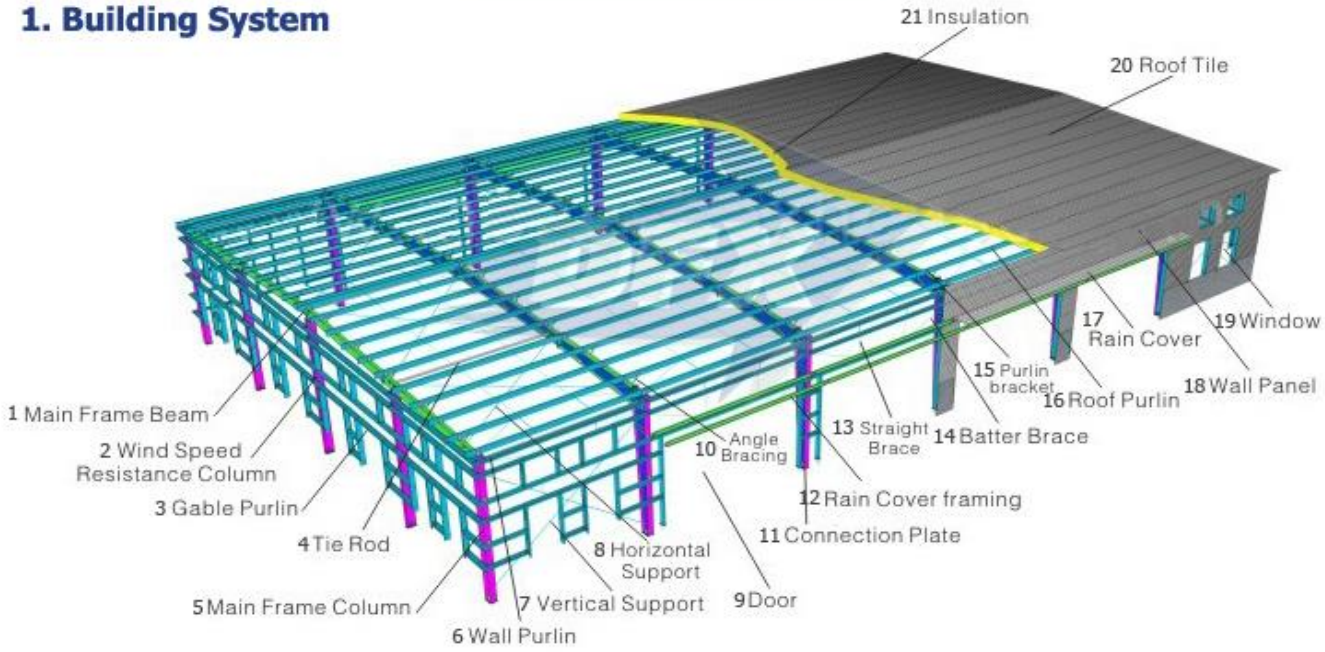


## 2. Specification

| Items | | Specification |
|---|---|---|
| Main Steel Frame | Flanges | 5-6-8-10 mm |
| | Anchor Bolts | 24 mm |
| | Purlin | 1.5mm 8" (150 microns) |
| | Base plate | 20-25mm |
| | Connection plates | 16-20mm |
| | Wire Bracing | 12mm |
| | Sheet | 0.5mm |
| Maintenance system | Roof Panel | 50mm Glass Wool Panel / Corrugated Steel Sheet |
| | Wall Panel | Corrugated Steel Sheet 0.50 mm thick average |
| Accessories | Window | Nill |
| | Door | Sliding Door / Rolling Metal Door / Personal Door 16 g |
| | Rainspout | Nill |
| Live load on Roof | | 0.57 (kN/m2) (Color steel panel surrounded) |
| Live load on Frame | | 0.57 (kN/m2) |
| Wind Resistance (km/hr) | | 16 (Exposure C) |
| Seismic Zone | | 2-B |
| Structure Usage | | Up to 50 years |
| Finishing Options | | Vast array of colors and textures available |

| | |
|---|---|
| Paint Options | Alkyd painting, two primary painting, two finish painting (gray paint, red paint, white paint etc.) Or Galvanized. |

## 3. Detailed Images



## RELATED PRODUCTS

