To,
Muhammad Usman
1-P, Gulberg III, Lahore

Date: Sep 16, 2025
Ref No: ACCO/QTSN/22

SUBJECT: QUOTATION FOR CONSTRUCTION OF PRE-ENGINEERED BUILDING AT LAHORE (AREA 7770 .00SFT. APPROX HEIGHTS 39 '00") Three Floors G/F +F/F+S/F

Dear Sir,

We are pleased to submit the requisite Technical & Commercial document for the contractual agreement in accordance with your inquiry and input. The detailed parameters for this particular job have been mentioned in the sections below.

SR	SCOPE OF WORK	AREA	RATE	AMOUNT (Rs.)	REMARKS
A	1- Fabrication & supply of complete pre-engineered steel Building system incl. steel columns and rafters, wall and roof purlins, wall and roof pre-painted, Shade height center 13 '-00" X 3 =39'-00 ○ Side's walls & roof sheeting.	23310.00	2500.00	58275000.00	
B	Civil work ground floor foundation and PCC Flooring Only with 6 feet Bricks Walls 3 sides	7770 Sft	900.00	6993000.00	
C	Rcc Flooring 1:2:4 Concrete in F/F and S/F for slabe 3" thick	4000 Cft	900.00	3.600,000.00	
D	Steel 2" 12"X12" F/F and S/F	3500 Kg	310.00	1085000.00	
	Total			**6,995,3000.00**	

TERMS & CONDITIONS: -

MODE OF PAYMENT (Without Taxes):


1. 50% on the time of start the work.
2. 30% on the time of Pre-Engineering Framework.
3. 10% on the time of Purlin.
4. 10% on the time of Sheeting.
5. Civil works only foundation including in this quotation.
6. Bills shall be paid within 7 days the after the submission.
7. The prices are based on mentioned items in BOQ. Any additional items from BOQ shall be claim separately.
8. Cordon off Area and Debris removal from site shall be paid by Client.

9. Provision of all accessibility to working area, Provision of storage facilities for our goods and equipment, where necessary, water & Electricity shall be provided the d by the client.
10. Civil Work is not included.

We will be obliged for your Cooperation in this regard.
With best regards,
Tanveer Ahmed
DIRECTOR

Product description

1. Building System

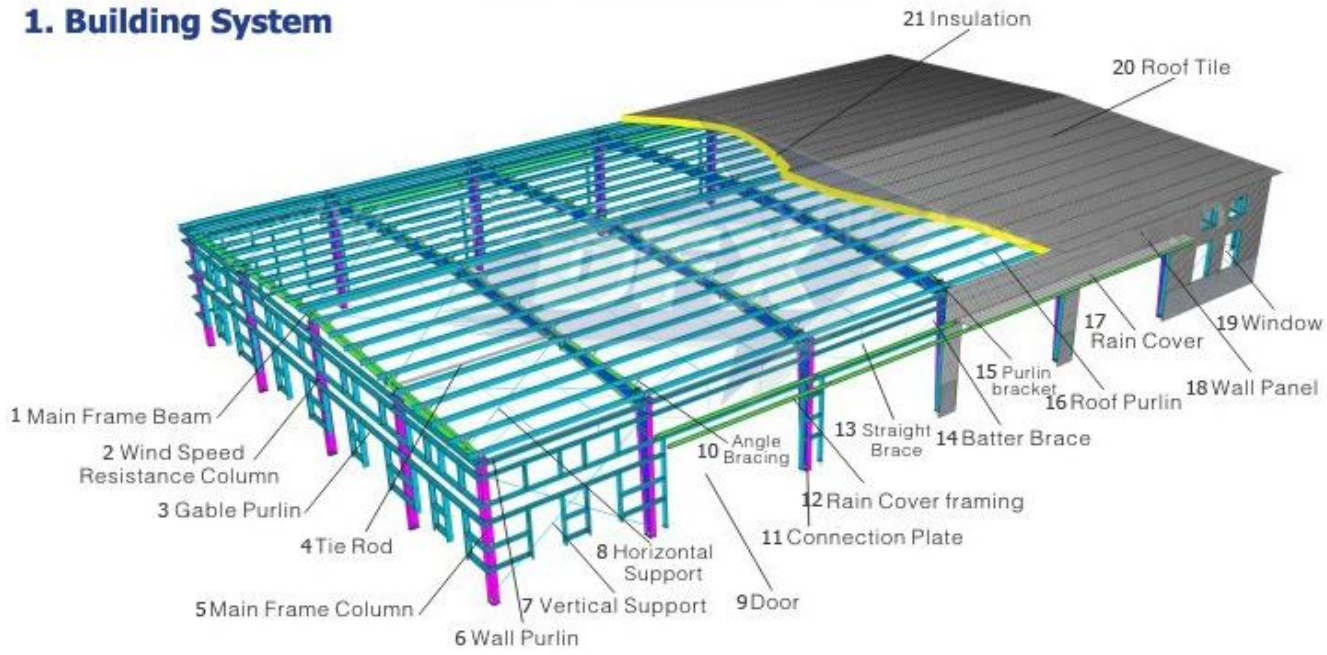

2. Specification

Items		Specification
Main Steel Frame	Column (6 & 8mm)	Q235, Q345 Welded H Section Steel
	Beam (6 & 8mm)	Q235, Q345 Welded H Section Steel
Secondary Frame	Purlin	Q235 C and Z purlin
	Knee brace	Q235 Angle Steel
	Tie Rod	Q235 Circular Steel Pipe
	Brace	Q235 Round Bar
	Vertical and Horizontal Support	Q235 Angle Steel, Round Bar or Steel Pipe
Maintenance system	Roof Panel	50mm Glass Wool Panel / Corrugated Steel Sheet 0.45 mm thick


	Wall Panel	Corrugated Steel Sheet 0.50 mm thick average
Accessories	Window	Nill
	Door	Sliding Door / Rolling Metal Door / Personal Door 16 g
	Rainspout	Nill
Live load on Roof		0.57 (kN/m2) (Color steel panel surrounded)
Live load on Frame		0.57 (kN/m2)
Wind Resistance (km/hr)		16 (Exposure C)
Seismic Zone		2-B
Structure Usage		Up to 50 years
Finishing Options		Vast array of colors and textures available
Paint Options		Alkyd painting, two primary painting, two finish painting (gray paint, red paint, white paint etc.) Or Galvanized.


3. Detailed Images

COMPOSITE MATERIALS

Qingdao Director Steel Structure Co., Ltd.


Galvanized H Beam





H Beam


I Beam





Box Column

Steel Tube



Steel Bar






Turnbuckle


Anchor Bolt







Casing

C and Z Purlin




Steel Deck





Steel Sheet


EPS Sandwich Panel





Rock Wool Sandwich Panel

PU Sandwich Panel



RELATED PRODUCTS



To,
Muhammad Usman
1-P, Gulberg III, Lahore

Date: Sep 16, 2025
Ref No: ACCO/QTSN/22

SUBJECT: QUOTATION FOR CONSTRUCTION OF PRE-ENGINEERED BUILDING AT LAHORE (AREA 7770 .00SFT. APPROX HEIGHTS 13 '00")

Dear Sir,

We are pleased to submit the requisite Technical & Commercial document for the contractual agreement in accordance with your inquiry and input. The detailed parameters for this particular job have been mentioned in the sections below.

SR	SCOPE OF WORK	AREA	RATE	AMOUNT (Rs.)	REMARKS
A	1- Fabrication & supply of complete pre-engineered steel Building system incl. steel columns and rafters, wall and roof purlins, wall and roof pre-painted, Shade height center 13 '-00" ○ Side's walls & roof sheeting.	7770.00	1450	11,266,500.00	
B	CIVIL WORK FOR SHED FOUNDATION ONLY	7770	230	1,787,100.00	
				13,053,600.00	

TERMS & CONDITIONS: -

MODE OF PAYMENT (Without Taxes):


1. 50% on the time of start the work.
2. 30% on the time of Pre-Engineering Framework.
3. 10% on the time of Purlin.
4. 10% on the time of Sheeting.
5. Civil works only foundation including in this quotation.
6. Bills shall be paid within 7 days the after the submission.
7. The prices are based on mentioned items in BOQ. Any additional items from BOQ shall be claim separately.
8. Cordon off Area and Debris removal from site shall be paid by Client.
9. Provision of all accessibility to working area, Provision of storage facilities for our goods and equipment, where necessary, water & Electricity shall be provided the d by the client.
10. Civil Work is not included.

We will be obliged for your Cooperation in this regard.
With best regards,
Tanveer Ahmed

DIRECTOR

Product description

1. Building System

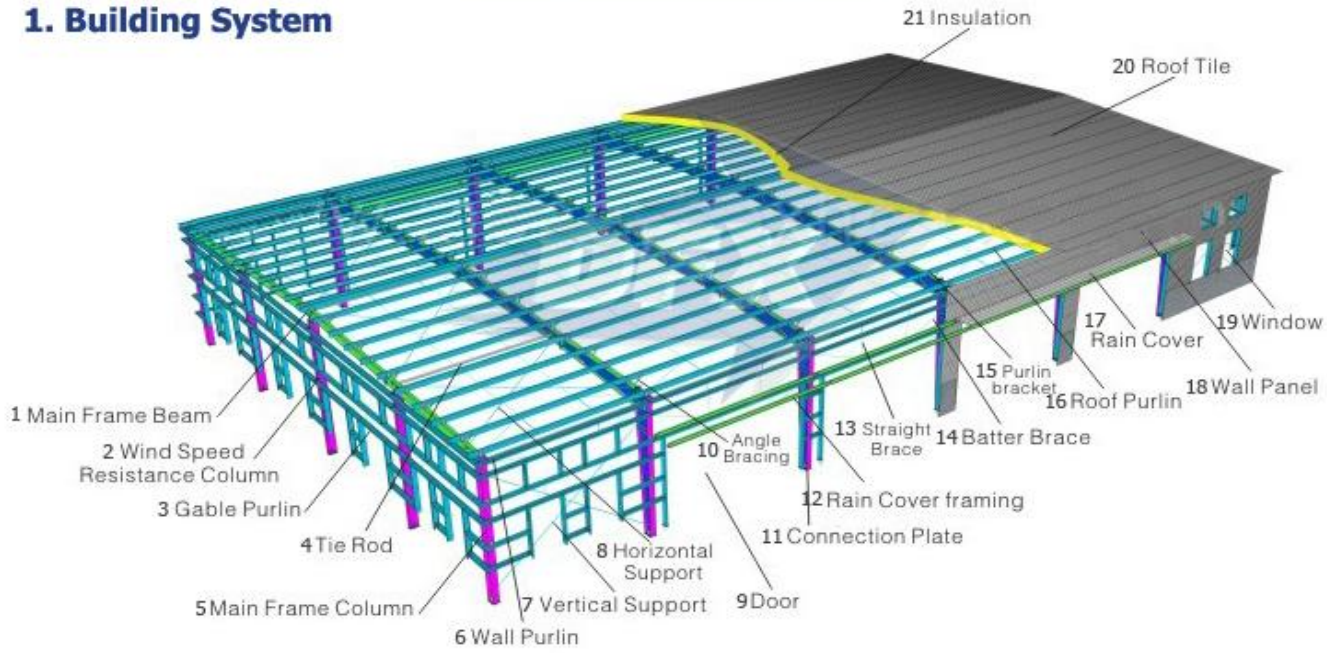


2. Specification

Items		Specification
Main Steel Frame	Column (6 & 8mm)	Q235, Q345 Welded H Section Steel
	Beam (6 & 8mm)	Q235, Q345 Welded H Section Steel
Secondary Frame	Purlin	Q235 C and Z purlin
	Knee brace	Q235 Angle Steel
	Tie Rod	Q235 Circular Steel Pipe
	Brace	Q235 Round Bar
	Vertical and Horizontal Support	Q235 Angle Steel, Round Bar or Steel Pipe
Maintenance system	Roof Panel	50mm Glass Wool Panel / Corrugated Steel Sheet 0.45 mm thick
	Wall Panel	Corrugated Steel Sheet 0.50 mm thick average
Accessories	Window	Nill
	Door	Sliding Door / Rolling Metal Door / Personal Door 16 g
	Rainspout	Nill
Live load on Roof		0.57 (kN/m2) (Color steel panel surrounded)

Live load on Frame	0.57 (kN/m2)
Wind Resistance (km/hr)	16 (Exposure C)
Seismic Zone	2-B
Structure Usage	Up to 50 years
Finishing Options	Vast array of colors and textures available
Paint Options	Alkyd painting, two primary painting, two finish painting (gray paint, red paint, white paint etc.) Or Galvanized.

3. Detailed Images

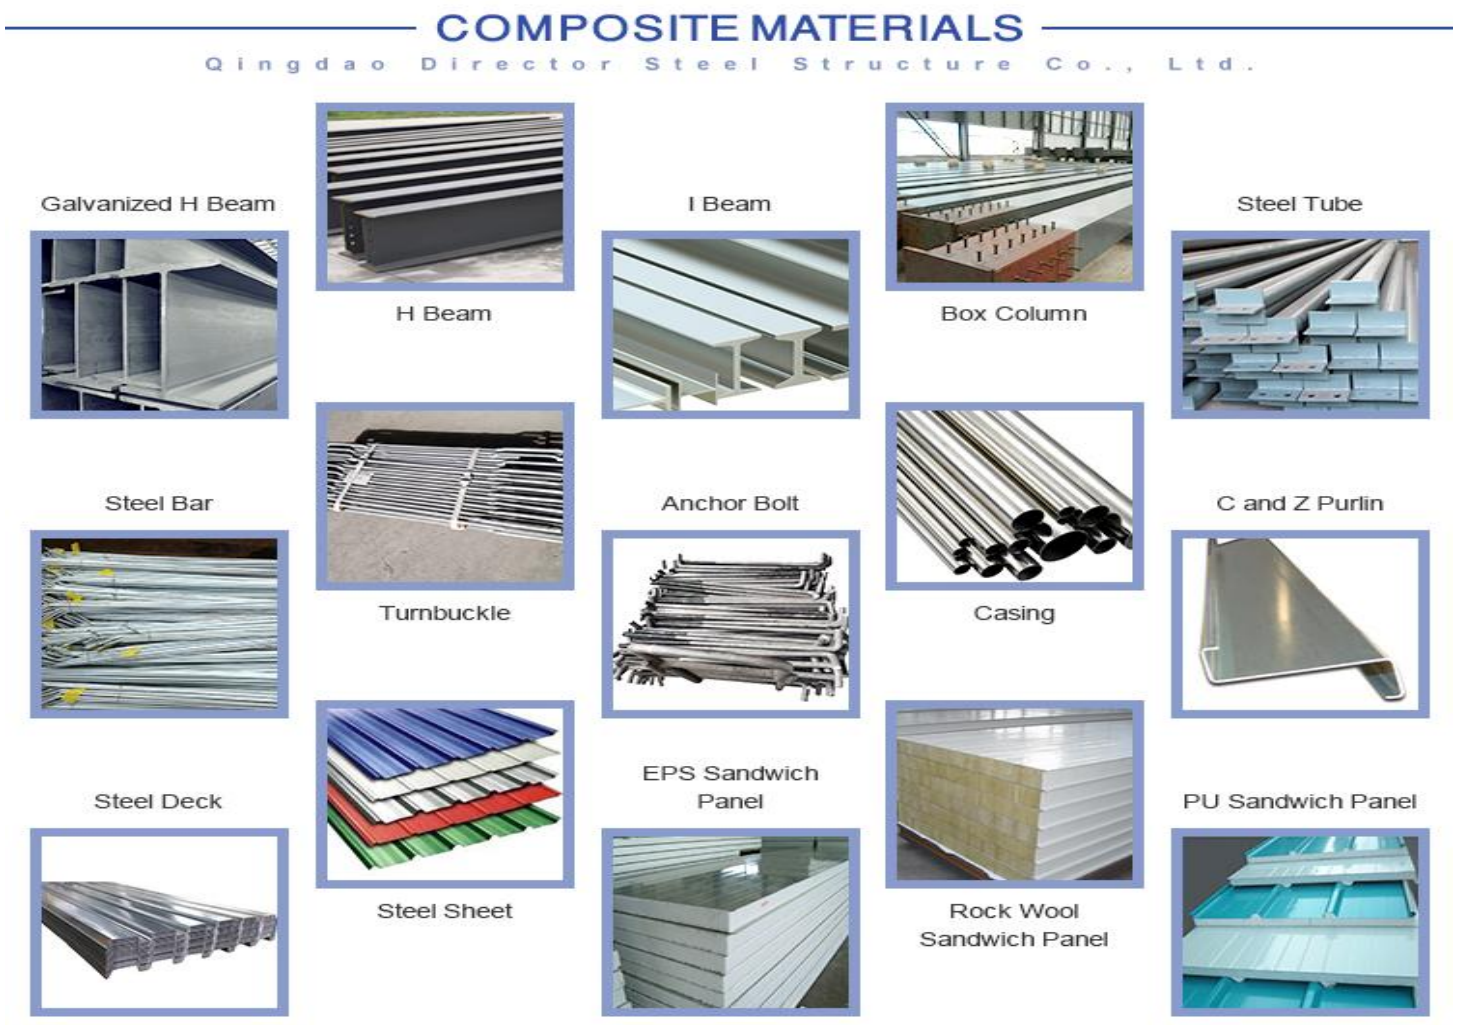

RELATED PRODUCTS

