To,

Date: November 11, 2025
Ref#: ACCO/PEB/896

SUBJECT: - **QUOTATION FOR INSTALLATION OF PRE-ENGINEERED SOLAR SYSTEM**

السلام علیکم
We are pleased to submit our best quote for subject work as follows: -

Sr.#	Item Description	Area (SFT)	Rate (Rs.)	Amount
1	Construction, supply and installation of a prefabricated steel system for solar installation Complete in all respect. Heights Approx. 37', 21' and 15'	6,800	1,000/-	6,800,000/-
2	Construction, supply and installation of a prefabricated steel system for solar installation Complete in all respect. Heights Approx. 37' and 40'	8,000	1,100/-	8,800,000/-
	Total Amount			**15,600,000/-**

Terms & Conditions:


1. This quotation excludes all taxes.
2. Complication Time 3 Month
3. 50% Advance before starting the Project other balance Payment according to percentage of Work
4. Provision of storage facilities for our goods and equipment, where necessary, shall be client responsibility.
5. Electricity & water supply will be provided by the client.
6. This quotation is valid for 30 days from above mentioned date.
7. Civil Work is not included.

We will be obliged for your cooperation in this regard.
Thanks & Regards.
Truly yours,

Tanveer Ahmed
Director
+92-322-8000190

Product description

1. Building System

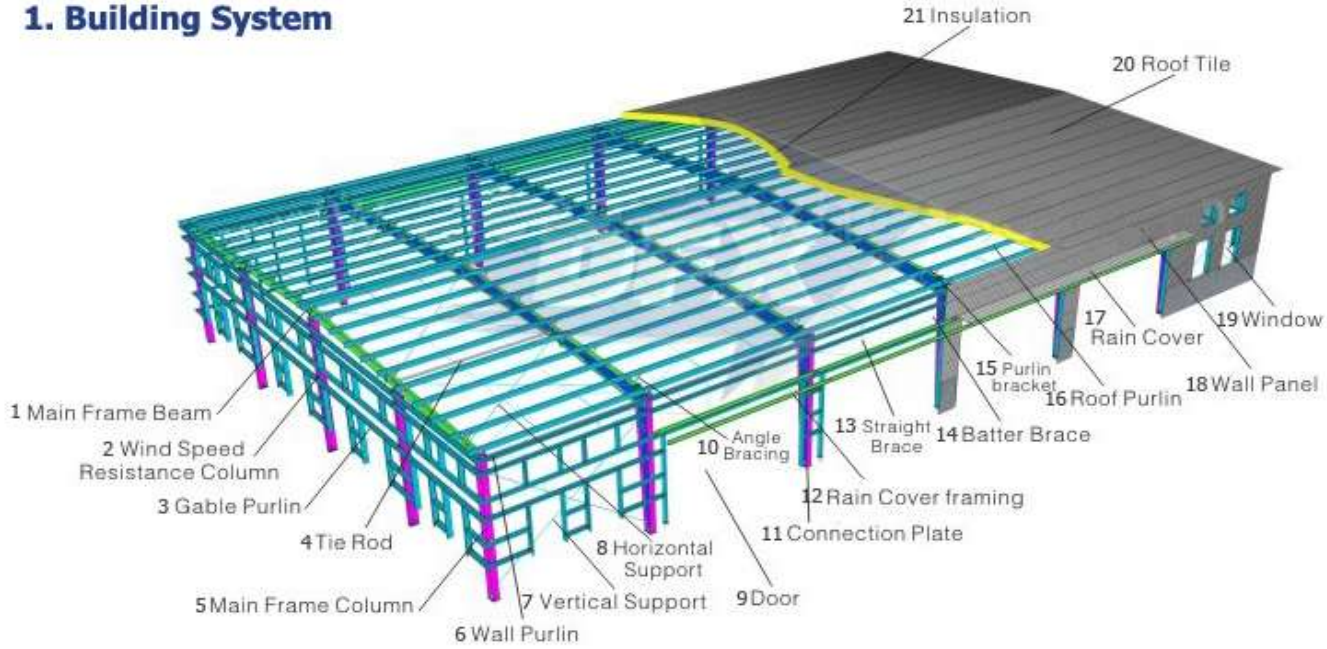

2. Specification

Items		Specification
Main Steel Frame	Column	Q235, Q345 Welded H Section Steel
	Beam	Q235, Q345 Welded H Section Steel
Secondary Frame	Purlin	Q235 C and Z purlin
	Knee brace	Q235 Angle Steel
	Tie Rod	Q235 Circular Steel Pipe
	Brace	Q235 Round Bar
	Vertical and Horizontal Support	Q235 Angle Steel, Round Bar or Steel Pipe
Maintenance system	Roof Panel	50mm thick sandwich panel
	Wall Panel	50mm thick sandwich panel
Accessories	Window	Nil
	Door	Nil
	Rainspout	PVC
Live load on Roof		0.57 (kN/m2) (Color steel panel surrounded)
Live load on Frame		0.57 (kN/m2)

Wind Resistance (km/hr)	160 (Exposure C)
Seismic Zone	2-B
Structure Usage	Up to 50 years
Finishing Options	Vast array of colors and textures available
Paint Options	Alkyd painting, two primary painting, two finish painting (gray paint, red paint, white paint, epoxy zinc etc.) Or Galvanized.

3. Detailed Images



RELATED PRODUCTS









