To,
Dr. Bilal
Samundri, Punjab Pakistan

Date: November 20, 2025
Ref#: ACCO/PEB/935-1

SUBJECT: - **REVISED QUOTATION FOR CONSTRUCTION OF PRE-ENGINEERED POULTRY FARM**

السلام علیکم
We are pleased to submit our best quote for subject work as follows: -

Sr.#	Item Description	Area (SFT)	Rate (Rs.)	Amount
1	Complete Design Package for Pre-Engineered Building (including Architectural Planning, Structural Design, GA Drawings, Fabrication Drawings, MEP Coordination & 3D Concept)	2	100,000/-	200,000/-
	Total Amount			**200,000/-**

Sr.#	Item Description	Area (SFT)	Rate (Rs.)	Amount
1	Construction, supply and installation of a prefabricated steel structure poultry farm for Layers Complete in all respect. Area: 400x60 feet Height Approx. 20 feet	24,000	2,175/-	42,000,000/-
2	Complete Civil works of the building	24,000	1,000/-	24,000,000/-
3	Electrical works including wire, switches, complete in all respect	24,000	200/-	4,800,000/-
4	Stainless steel doors (Main door and small door)	2	500,000/-	500,000/-
	Total Amount			**81,500,000/-**

Sr.#	Item Description	Area (SFT)	Rate (Rs.)	Amount
1	Construction, supply and installation of a prefabricated steel structure poultry farm for Broilers Complete in all respect. Area: 400x60 feet Height Approx. 7 feet	24,000	1,750/-	42,000,000/-
2	Complete Civil works of the building	24,000	700/-	16,800,000/-
3	Electrical works including wire, switches, complete in all respect	24,000	200/-	4,800,000/-
4	Stainless steel sliding doors (Main door and back door)	2	500,000/-	500,000/-
	Total Amount			**64,100,000/-**

Terms & Conditions:


1. This quotation excluding of all taxes.
2. Complication Time 45 days
3. 50% Advance before starting the Project other balance Payment according to percentage of Work
4. Provision of storage facilities for our goods and equipment, where necessary, shall be client responsibility.
5. Electricity & water supply will be provided by the client.
6. If the area of building increase or decreases then price will be increases or decreases accordingly.
7. This quotation is valid for 30 days from above mentioned date.

We will be obliged for your cooperation in this regard.
Thanks & Regards.
Truly yours,

Tanveer Ahmed
Director

Product description

1. Building System

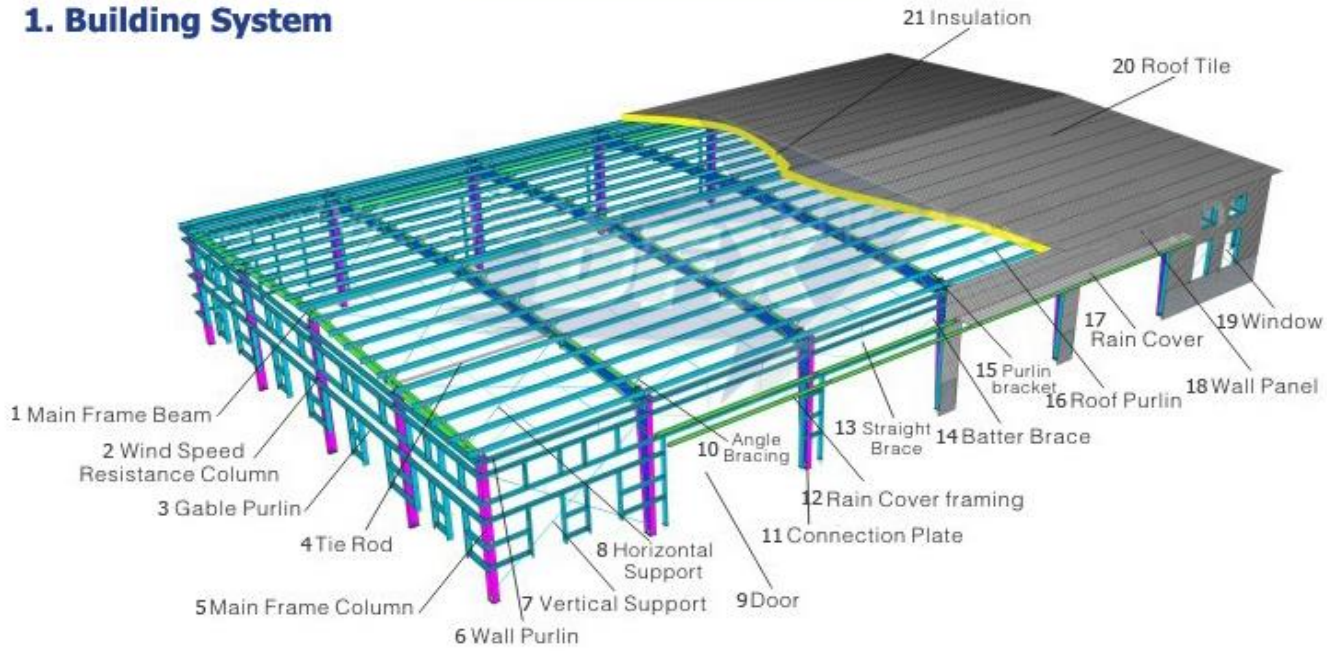

2. Specification

Items		Specification
Main Steel Frame	Column	5 mm and 6 mm
	Beam	5 mm and 6 mm
Secondary Frame	Purlin	1.5 mm
	Knee brace	12 mm
	Tie Rod	50 mm x 50 mm angle
	Brace	Sag Rod
	Vertical and Horizontal Support	Q235 Angle Steel, Round Bar or Steel Pipe
Maintenance system	Roof Panel	50 mm PU sandwich panel
	Wall Panel	50 mm PU sandwich panel
Accessories	Window	Nil
	Door	Stainless steel sliding doors 16 gauge
	Rainspout	MS Sheet
Live load on Roof		0.57 (kN/m2) (Color steel panel surrounded)
Live load on Frame		0.57 (kN/m2)

Wind Resistance (km/hr)	160 (Exposure C) / 140 km per hour
Seismic Zone	2-B
Structure Usage	Up to 50 years
Finishing Options	Vast array of colors and textures available
Paint Options	Alkyd painting, two primary painting, two finish painting (gray paint, red paint, white paint, epoxy zinc etc.) Or Galvanized.

3. Detailed Images



RELATED PRODUCTS



+92 322 8000 190 UAN: +923 111 749 849 info@acco.com.pk

Office 2nd, 3rd Floor, Bigcity Plaza, Gulberg-III, Lahore, Pakistan
