To,
Mr. Waqar Sahab
CMH, Gujranwala Punjab Pakistan

Date: December 16, 2025
Ref#: ACCO/PEB/1138

SUBJECT: - **QUOTATION FOR DESIGN & CONSTRUCTION OF PRE-ENGINEERED BUILDING IN GUJRANWALA**

السلام علیکم
We are pleased to submit our best quote for subject work as follows: -

Sr.#	Item Description	Area (SFT)	Rate (Rs.)	Amount
1	Design supply and installation of a pre-engineering building for stay room Complete in all respect. Area: 10,000 feet Height Approx. 13 feet	10,000	16/-	160,000/-
2	Construction, Gray and finish with foundation and side walls 10 feet height floor tile complete in all respects windows and doors	10,000	1,800/-	18,000,000 /-
3	Pre Engineered Building Male Night Stay Hall 3500 Female Night Stay Hall 3500 Canteen 2000 Bathrooms and Circulation & Entrances	10,000	1,500/-	15,000,000/-
4	Electric and Plumbing works	10,000	210	2,100,000/-
5	**Total Amount**			**35,260,000**/-

Terms & Conditions:


1. This quotation excludes all taxes.
2. Complication Time 30 days
3. 50% Advance before starting the Project other balance Payment according to percentage of Work
4. Provision of storage facilities for our goods and equipment, where necessary, shall be client responsibility.
5. Electricity & water supply will be provided by the client.
6. This quotation is valid for 30 days from above mentioned date.
7. Civil Work

We will be obliged for your cooperation in this regard.
Thanks & Regards.
Truly yours,

Tanveer Ahmed
Director

Product description

1. Building System

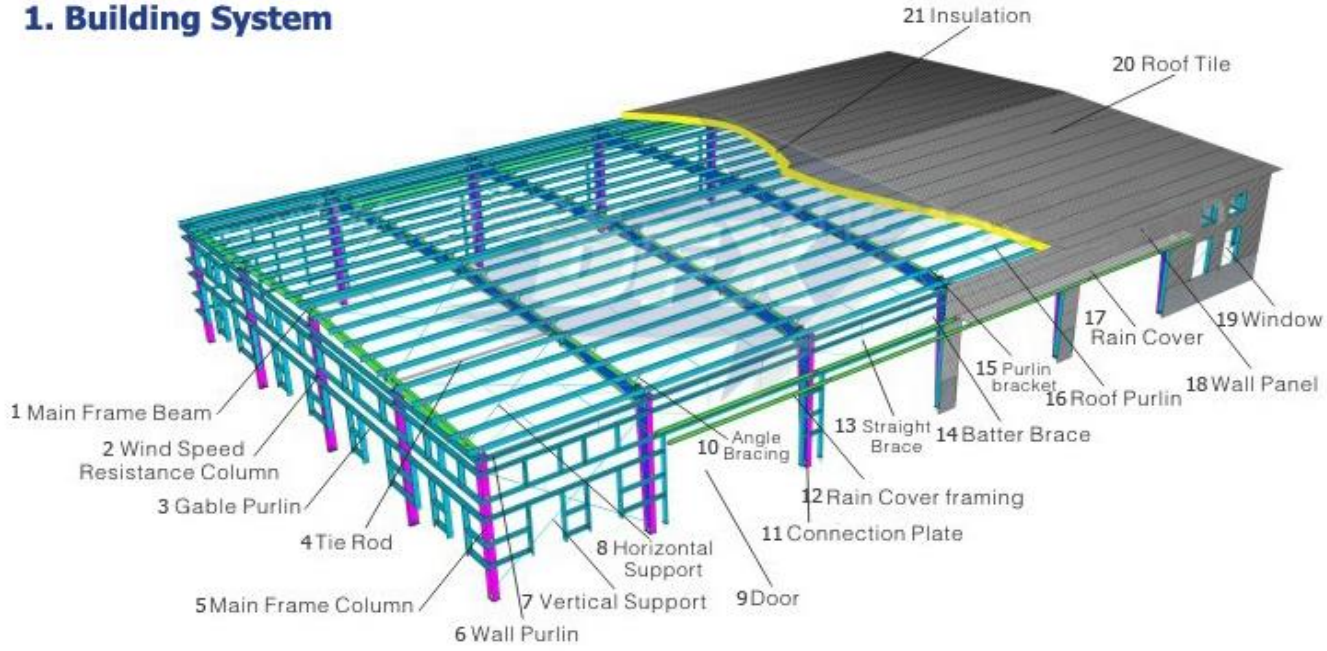

2. Specification

Items		Specification
Main Steel Frame	Column	5 mm and 6 mm
	Beam	5 mm and 6 mm
Secondary Frame	Purlin	1.5 mm
	Knee brace	12 mm
	Tie Rod	50 mm x 50 mm angle
	Brace	Sag Rod
	Vertical and Horizontal Support	Q235 Angle Steel, Round Bar or Steel Pipe
Maintenance system	Roof Panel	0.45 mm sheet PPGI (Pre-Painted Galvanized Iron) 50mm Glass Wool
	Wall Panel	0.45 mm sheet PPGI (Pre-Painted Galvanized Iron) 50mm Glass Wool

Accessories	Window	Nil
	Door	Nil
	Rainspout	MS Sheet
Live load on Roof		0.57 (kN/m2) (Color steel panel surrounded)
Live load on Frame		0.57 (kN/m2)
Wind Resistance (km/hr)		160 (Exposure C) / 140 km per hour
Seismic Zone		2-B
Structure Usage		Up to 50 years
Finishing Options		Vast array of colors and textures available
Paint Options		Alkyd painting, two primary painting, two finish painting (gray paint, red paint, white paint, epoxy zinc etc.) Or Galvanized.

3. Detailed Images



RELATED PRODUCTS



+92 322 8000 190 UAN: +923 111 749 849 info@acco.com.pk

Office 2nd, 3rd Floor, Bigcity Plaza, Gulberg-III, Lahore, Pakistan
