ACCO
AHMED CONSTRUCTION COMPANY

BJQ Hospital Gulberg Greens Islamabad

Tuesday, Feb 24, 2026
Ref No: ACCO/QTN/OT1440

Quotation

1. Glass Modular Operation Theater.
2. AM Clad Operation Theater.
3. Gi Powder Coated Penal Modular OperationTheater.
4. SS Penal Modular Operation Theater.

Dear Sir,
Ref. to your inquiry for subject cited item, please find enclosed herewith our best prices for your inquired item with the following terms & conditions. We hope you will find our prices very competitive and complete in all aspects.

Description	Area	Price/sq	Amount
Glass Modular Operation Theater. **Printed & Color Glass Panels for OT's:** i. 8 mm Clear Tempered Glass with side polish having 40 mm aluminum profile frame fixed with cement silicon on the back of the glass. ii. Prefabricated modular back Ceramic Painted USA/Italy Glass wall panels in any color of end-user choice. iii. Graphic or Image is with one panels. iv. Space Between Panels Filled with Removable Silicon Gasket **Sub-Structure:** 1.2 mm Galvanized steel Structure frame for OT's with all accessories. Made: Pakistan			
	OT # 1:25'-7 ½"X15'0" =385 SFT	Rs:3200 sqft	Rs: 1,232,000/-
	OT # 2:21'-0"X15'-0" =315 SFT	Rs:3200 sqft	Rs: 1,008,000/-



Ceramic Print color glass





OFFICE:
Office #2, 3rd Floor, Bigcity Plaza, Gulberg-III, Lahore

Web:
www.acco.com.pk

Contact:
+92-311-1749849, +92 322-8000190
Email: info@acco.com.pk

ACCO
AHMED CONSTRUCTION COMPANY

Description	Area	Price/sq	Amount
Pasted Color Glass Operation Theater. i. 8 mm Clear Tempered Glass with side polish Ceramic Color Painted (USA/Italy) Pasted with cement silicon on the back of the glass ii. Graphic or Image Ceramic Print with PVC Protection **Sub-Structure:** Gypsum Board Irish or Elephant 1.2 mm Galvanized steel Structure frame for OT's with all accessories. Made: Pakistan	OT # 1:25'-7 ½"X15'0" =385 SFT	Rs:2600 sqft	Rs: 1,001,000/-
	OT # 2:21'-0"X15'-0" =315 SFT	Rs:2600 sqft	Rs: 819,000/-



Digital Ceramic UV Digital Printed Pasted Glass Operation Theater. i. 8 mm Clear Tempered Glass with side polish Ceramic Color Painted (USA/Italy) Pasted with cement silicon on the back of the glass ii. Graphic or Image Ceramic Print with PVC Protection **Sub-Structure:** Gypsum Board Irish or Elephant 1.2 mm Galvanized steel Structure frame for OT's with all accessories. Made: Pakistan	OT # 1:25'-7 ½"X15'0" =385 SFT	Rs:2200 sqft	Rs: 847,000/-
	OT # 2:21'-0"X15'-0" =315 SFT	Rs:2200 sqft	Rs: 693,000/-

OFFICE:
Office #2, 3rd Floor, Bigcity Plaza, Gulberg-III, Lahore

Web:
www.acco.com.pk

Contact:
+92-311-1749849, +92-322- 8000190
Email: info@acco.com.pk

Description	Area	Price/sq	Amount
I Clad UK PVC wall cladding I. 2mm MM-Clad UK Original antimicrobial wall cladding ii. 8mm Tempered Printed Glass Wall **Sub-Structure:** Galvanized steel Structure frame for OT's with Ceramic Sheet Arish or Elephant Made: Pakistan	OT # 1:25'-7 ½"X15'0" =385 SFT	Rs:2500 sqft	Rs: 962,500/-
	OT # 2:21'-0"X15'-0" =315 SFT	Rs:2500 sqft	Rs: 787,500/-
 **Clad Local PVC wall cladding** I. 2mm MM- Local wall cladding ii. 8mm Tempered Printed Glass Wall **Sub-Structure:** Galvanized steel Structure frame for OT's with Ceramic Sheet Arish or Elephant Made: Pakistan			
Clad Local PVC wall cladding	OT # 1:25'-7 ½"X15'0" =385 SFT	Rs:2200 sqft	Rs: 847000/-
	OT # 2:21'-0"X15'-0" =315 SFT	Rs:2200 sqft	Rs: 693000/-

OFFICE:
Office #2, 3rd Floor, Bigcity Plaza, Gulberg-III, Lahore

Web:
www.acco.com.pk

Contact:
+92-311-1749849, +92-322- 8000190
Email: info@acco.com.pk

ACCO
AHMED CONSTRUCTION COMPANY

Description	QTY	Unit Price
Touch screen control panel • 24 inches Touch screen • Temp & humidity controlling (includes the humidity & temperature sensor). • Countdown Clock. • Clock. • Lights controlling. • Medical gas alarm. Imported components assembled locally	1 pcs	Rs: 550,000/-
Analog Control Panel	1 pcs	Rs: 188,000/-
S.S. Automatic Sliding doors ● Automaic Hermetically sealed Sliding Door Stainless Steel Grinded and having class 304 with German Motor compliianced with EN16005 ● Size: 1450 x 2100 mm. ● Door Frame is also made of Stainless Steel, thickness minimum 1 mm. ● Vertical Continuous Sealing of the door to avoid pressure loss. ● Duplex Sandwich construction of the Door leaf, impact proof, approximately thicknesses 40 mm. ● 2 x Door Opening Handles for the manual opening of door in case of power failure. ● 2 x touchless sensors for door opening. ● Complete with Fitting, Necessary components. **Inspect on Window** ● Inspection window 400/600 mm in door leaf as an addition to the earlier described door items with flush glazing. ● Dimensions: width x height = approx. 250 x 1200 mm.	1 pcs	Rs: 480,000/- China Drive
	1 pcs	Rs: 550,000/- Taiwan Drive
Manual Sliding doors		Rs: 380,000/-





OFFICE:
Office #2, 3rd Floor, Bigcity Plaza, Gulberg-III, Lahore

Web:
www.acco.com.pk

Contact:
+92-311-1749849, +92-322- 8000190
Email: info@acco.com.pk

ACCO
AHMED CONSTRUCTION COMPANY

Description	QTY	Unit Price
Manual Single leaf Door Double leaf Door Stainless steel frame included. Size: 900 mm x 2100 mm. Increase for window dim. 600 x 400 mm. 1mm SS 304 Grade for door leaf with Handle, door closer,Lock 	1 units SS Solid Door	Rs: 240,000/-
Manual Double leaf Door 	1 units SS Solid Door	Rs: 325,000/-
S.S Cabinet • Built-in Cabinet system integrated in the wall. • Size Approx 940 x 2100 x 455 mm (W x H x D). • Made of stainless steel (304) sheet 1 mm. • Tall cabinet with 2 leaf glass doors each, sealed all round with rubber seal. • The cabinet should have 4 stainless steel shelves. 	1 units	Rs: 310,000/-
X Ray Viewer • Dimension 900mm x 640mm x 95mm NO's • 2 plates With dimmer • Aluminum frame profile • Power 22 Watts Make: China 	1 units	**Rs: 80,000/-**
Ceiling (dampa type) for OT's • The false ceiling shall consist of metal ceiling tiles with clip in suspension system for easy access to the ceiling plenum. • The ceiling suspension system shall be made of galvanized steel U-profile attached to the concrete ceiling via threaded rod and clamping brackets with the flexibility of adjusting the ceiling height. • The clamping rails where the ceiling cassettes will be fixed in are attached to the suspension system via galvanized connectors. • The ceiling cassettes shall be 600 x 0.7 mm made of Aluminum. The visible part shall be powder coated with polyurethane in RAL 9010. Make: Imported 	Rs:520 sqft	

OFFICE:
Office #2, 3rd Floor, Bigcity Plaza, Gulberg-III, Lahore

Web:
www.acco.com.pk

Contact:
+92-311-1749849, +92-322-8000190
Email: info@acco.com.pk

ACCO
AHMED CONSTRUCTION COMPANY

Description	QTY	Unit Price
Provision/ fixing of lights/ fixture Combined clean room built in illuminator 48 W Visible surface of the lamp in PVC reflector. Without any extra cover profile. Installation flush with the ceiling. Make:Phillips	16 Pcs Phillips 16 Pcs China 	Rs:14,000/- Rs:8,000/-
Ceiling Edge • Aluminum powder coated 	1 Lenghts	Rs: 15,000/-
Anaesthesia Pendant • Friction braking system to prevent unintentional movement. • Swiveling arm with 340 degree rotation and with the radius of 750mm • Load capacity up to 110KGS • Electrical Sockets: 08 No's • Gas Outlet: 3 - 5 No's • Shelves: 2 No's (One with Drawer). • Lightweight and robust. • Integrated platforms and drawer unit for individual arrangement of devices of different sizes • Ergonomic control console for easy posi oning and maneuver. • Extensive modularity construction allows enough space for future expansion.	Pak Assembled 1 Pcs Motorized China 1 Pcs Pak Assembled  	Rs: 400,000/- Rs: 900,000/-
Surgeon Pendant • Fric on braking system to prevent uninten onal movement. • Swiveling arm with 340 degree rota on and with the radius of 750mm • Load capacity up to 110KGS • Electrical Sockets: 08 No's • Gas Outlet: 3 - 5 No's • Shelves: 2 No's (One with Drawer). • Lightweight and robust. • Integrated pla orms and drawer unit for individual arrangement of devices of different sizes • Ergonomic control console for easy positioning and maneuver. • Extensive modularity construc on allows enough space for future expansion. Make: Imported Components Assembled Locally	1 Pcs Pak Assembled Pak Assembled China  	Pak Assembled Rs: 400,000/- China Rs: 680,000/-

OFFICE:
Office #2, 3rd Floor, Bigcity Plaza, Gulberg-III, Lahore

Web:
www.acco.com.pk

Contact:
+92-311-1749849, +92-322-8000190
Email: info@acco.com.pk

ACCO
AHMED CONSTRUCTION COMPANY

Description	Unit Price

Vinyl Flooring

Rs:800 sqft

Homogenous Floor with self-leveling in OT in 2 mtr wide rolls with 2 mm thickness, with a total weight of 3.0 kg/m2 and includes an IQPUR treatment (polyurethane). Installation with an inverted flaw, hot-welded with the same material.
Make: Topfloor / TK Floor





S.S Scrub

- Double bay automa c stainless steel scrub Unit.
- Touchless operated lever with sensor operation.
- 3 x taps.
- 3 x Arm operated soap dispenser.
- 2 x brush dispenser.
- Dim: 2450 x 1200 x 625 mm Imported components assembled locally 304 Grade

Sensor Taps
3 x taps — Rs: 415,000/-

Manual Taps
3 x taps — Rs: 375,000/-

Sensor Taps
2 x taps — Rs: 340,000/-

Manual Taps
2 x taps — Rs: 330,000/-



S.S. power/Gas service panel

1 set — Rs: 120,000/-

Connect Panel for Gases - 1 meter Connect Panel for Electrical Sockets - 1 meter



OFFICE:
Office #2, 3rd Floor, Bigcity Plaza, Gulberg-III, Lahore

Web:
www.acco.com.pk

Contact:
+92-311-1749849, +92-322-8000190
Email: info@acco.com.pk


ACCO
AHMED CONSTRUCTION COMPANY

Description	QTY	Unit Price

SUS304 Stainless Steel Pass Window with Electronic Interlock Pass Box With CE Certificate For Hospital
SUS304 stainless steel
Interior and exterior product body and the two doors.
The thickness of the stainless steel is 1.0mm.
ultraviolet lamp with the power of 10W and the wavelength of 254nm.
It can get the ideal sterilization effect.
ensure safe use.
Interlockingsystem

Rs: 180,000/-

It can bear the load of 60kg.
The two doors of the product are set with transparent visible observation windows with round corners.

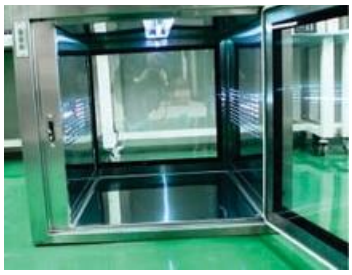



LED Medical OT Lights

Illumination (LUX): 160000
Color temperature (Kelvin): 3800-4800
Operator's Head Temperature Rise) (°C): ≤1
Surgical Field Temperature Rise (°C): ≤2
Effective Working Depth of Focus(mm): ≥800
Spot Size Adjustment Range (mm): 120-230
Average Life of Light Bulb (h): 100,000
Bulb Power (W): 1W/pc
Light adjustment: 1-8
Power Input: 100-240VAC 50/60Hz
Min Installation Height (mm) 2700mm

Make : China

Double Doom
1 unit

Rs: 1,100,000/-

Single Doom
1 unit

Rs: 600,000/-



Laminar Air Flow. Size: 2 x 2 Mtr

Laminar Air Flow Fabricated Fabricated With 1 mm G.I Sheet Finished With Electrostatic Powder Coating & Perforated Mesh Sheets Finished With Electrostatic Powder Coated. Hepa Filters. Make: APCS, Korea.



Rs: 650,000/-

OFFICE:
Office #2, 3rd Floor, Bigcity Plaza, Gulberg-III, Lahore

Web:
www.acco.com.pk

Contact:
+92-311-1749849, +92-22-8000190
Email: info@acco.com.pk

ACCO
AHMED CONSTRUCTION COMPANY

Terms & Conditons:

Validity:
Offered prices are valid for 15 Days.
Delivery: Within 45~60 days after receipt of your confirmed written order & payment transfer in advance.
Payment:
70% Payment advance with Confirm P.O.
20% Payment on delivery of the product at the site.
10% Payment after installation of the complete project.

*The Offered prices are on a DDP basis & exclusive of all kinds of taxes.
Installation: Installation will be provided free of charge. However, all pre-requisites will be provided by the consignee/institute.

Transportation charges will be paid separately and are not included in this quotation.
warranty: One year comprehensive warranty from the date of install on.

Looking forward to hear you soon in this connection.

Muhammad Emraan
For ACCO

0300-2358853
