To,
Mr. Hamza Riaz Sahab
Procurement Executive, Fauji Foods Limited
DHA Phase 8 Lahore,Pakistan

Date: April 22, 2026
Ref#: ACCO/PEB/1663

SUBJECT: - **QUOTATION FOR FILLING MACHINE PU PANEL ROOM AND VENTILATION (FOR HYGIENE AIR SUPPLY) IN SAHIWAL**

السلام علیکم
We are pleased to submit our best quote for subject work as follows: -

Sr.#	Item Description	Area (SFT)	Rate (Rs.)	Amount
1	Scope of Work – Filling Machine PU Panel Room and Ventilation (for Hygiene Air Supply)	1	14,265,525/-	14,265,525/-
	Total Amount			**14,265,525/-**

Terms & Conditions:

1. This quotation excludes all taxes.
2. Complication Time 35 days
3. 50% Advance before starting the Project, 35% on material on site and remaining 15% on completion.
4. Provision of storage facilities for our goods and equipment, where necessary, shall be client responsibility.
5. Electricity & water supply will be provided by the client.
6. This quotation is valid for 30 days from above mentioned date.


We will be obliged for your cooperation in this regard.
Thanks & Regards.
Truly yours,

Tanveer Ahmed
Director
+92-322-8000190

Sr.	Description	UOM	Qty	Amount	Total Amount
1	Polyurethane Sandwich Panel 4" (100mm), CFC-Free foamed in-place. Internal and external surface of hot-dip galvanized steel sheet, pre-painted polyester coating.	SFT	8,943	930	8,316,990
2	Assembling of panels 4" (100 mm), inclusive of fitment of profiles, filling and caulking of silicon and pressure relief ports.	SFT	8,943	345	3,085,335
3	Supply and installation of sliding door for the opening size of: 2.5M x 2.4M (high) complete with door frame, door hardware, side rail, & gasket with one hinged door (900x1900) and double glazed sight window (1' x 1.5') (Thickness 4") Provision for door frame heater	Nos.	2	250,000	500,000
4	Supply and installation of sliding door for the opening size of: 1.8M x 2.4M (high) complete with door frame, door hardware, side rail, & gasket with one hinged door (900x1900) and double glazed sight window (1' x 1.5') (Thickness 4") Provision for door frame heater	Nos.	1	190,000	190,000
5	Supply and installation of hinged doors and door frame 818.5 mm x 1930 mm equipped with heavy duty hinges, lock with internal safety release & panic bar etc (Thickness 4") Emergency Exit Door	Nos.	1	150,000	150,000
6	Supply and installation of window of the size of: 836.6 mm x 836.6 mm	Nos.	2	20,000	40,000
7	Supply and installation of window of the size of: 350 mm x 350 mm	Nos.	2	15,000	30,000
8	SS 304L angle (6" x 6" x 1.5 mm thickness) to be installed all around at the bottom of all PU panels. (700 RFT)	KG	788	1,400	1,103,200
9	Labor and Transportation Charges	Nos.	1	600,000	600,000
10	Dismantling of Insulated Panels Total ft² = 1798 ft² & 20 lights	Nos.	1	150,000	150,000
11	Supply and installation of hard area barricading before start of work, including complete end-to-end sealing using parachute material. Folding for Removal of already installed panels. All height arrangements and material rigging.	Units	1	100,000	100,000
	Total Amount				**14,265,525**

Product description

1. Building System

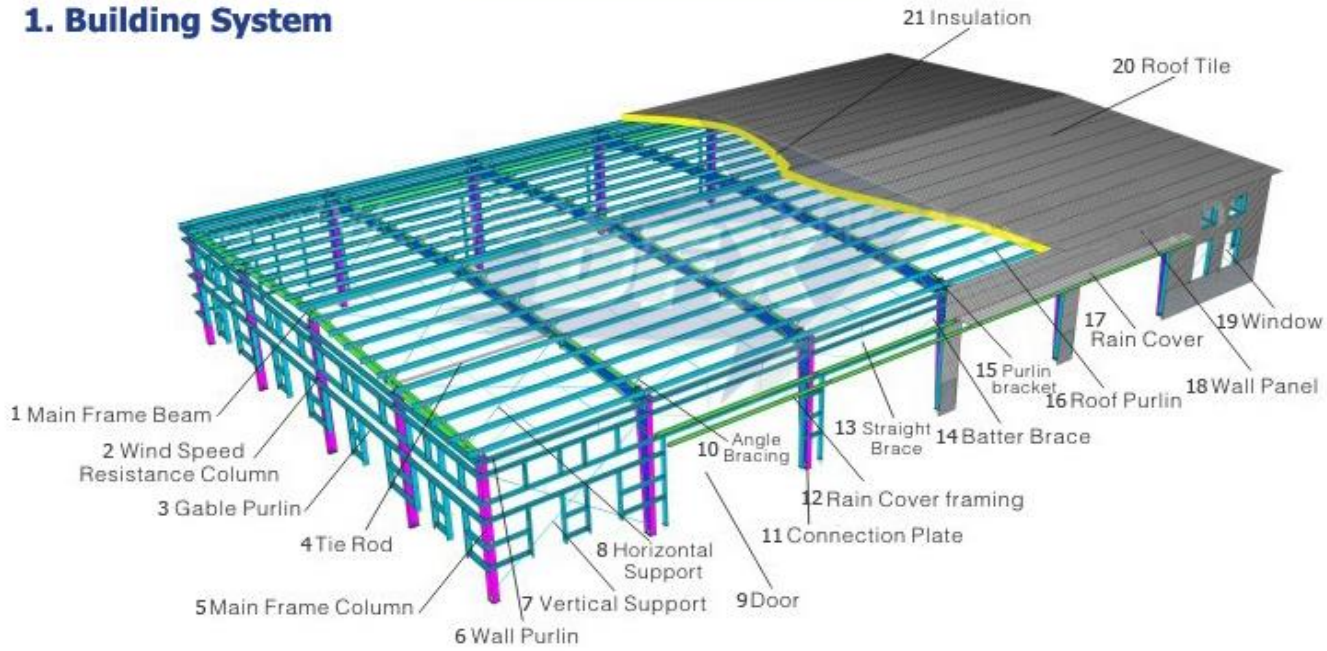

2. Specification

Items		Specification
Main Steel Frame	Column	5 mm and 6 mm
	Beam	5 mm and 6 mm
Secondary Frame	Purlin	1.5 mm
	Knee brace	12 mm
	Tie Rod	50 mm x 50 mm angle
	Brace	Sag Rod
	Vertical and Horizontal Support	Q235 Angle Steel, Round Bar or Steel Pipe
Maintenance system	Roof Panel	100mm PU Sandwich Panel
	Wall Panel	100mm PU Sandwich Panel
Accessories	Window	Nil
	Door	Sliding Door
	Rainspout	MS Sheet
Live load on Roof		0.57 (kN/m2) (Color steel panel surrounded)
Live load on Frame		0.57 (kN/m2)

Wind Resistance (km/hr)	160 (Exposure C) / 140 km per hour
Seismic Zone	2-B
Structure Usage	Up to 50 years
Finishing Options	Vast array of colors and textures available
Paint Options	Alkyd painting, two primary painting, two finish painting (gray paint, red paint, white paint, epoxy zinc etc.) Or Galvanized.

3. Detailed Images



RELATED PRODUCTS



+92 322 8000 190 UAN: +923 111 749 849 info@acco.com.pk

Office 2nd, 3rd Floor, Bigcity Plaza, Gulberg-III, Lahore, Pakistan
