To,
Mr. Sadaan Peerzada Sahab
Lahore, Punjab Pakistan

Date: May 7, 2026
Ref#: ACCO/PEB/1708

SUBJECT: - **QUOTATION FOR CONSTRUCTION OF PRE-ENGINEERED COMMERCIAL BUILDING**

السلام علیکم
We are pleased to submit our best quote for subject work as follows: -

Sr.#	Item Description	Area (SFT)	Rate (Rs.)	Amount
1	Construction, supply and installation of a prefabricated steel structure Building for **Commercial Art Presentation** Complete in all respect. Height Approx. 14 & 18 Feet Dimension: 54 x 56 feet Floors: 2	7,128	4,353/-	31,025,120/-
	Total Amount			31,025,120/-

Terms & Conditions:


1. This quotation excludes all taxes.
2. Completion Time 45 days
3. 50% Advance before starting the Project, 35% on material on site and remaining 15% on completion.
4. Provision of storage facilities for our goods and equipment, where necessary, shall be client responsibility.
5. Electricity & water supply will be provided by the client.
6. This quotation is valid for 30 days from above mentioned date.

We will be obliged for your cooperation in this regard.
Thanks & Regards.
Truly yours,

Tanveer Ahmed
Director
+92-322-8000190

Product description

1. Building System

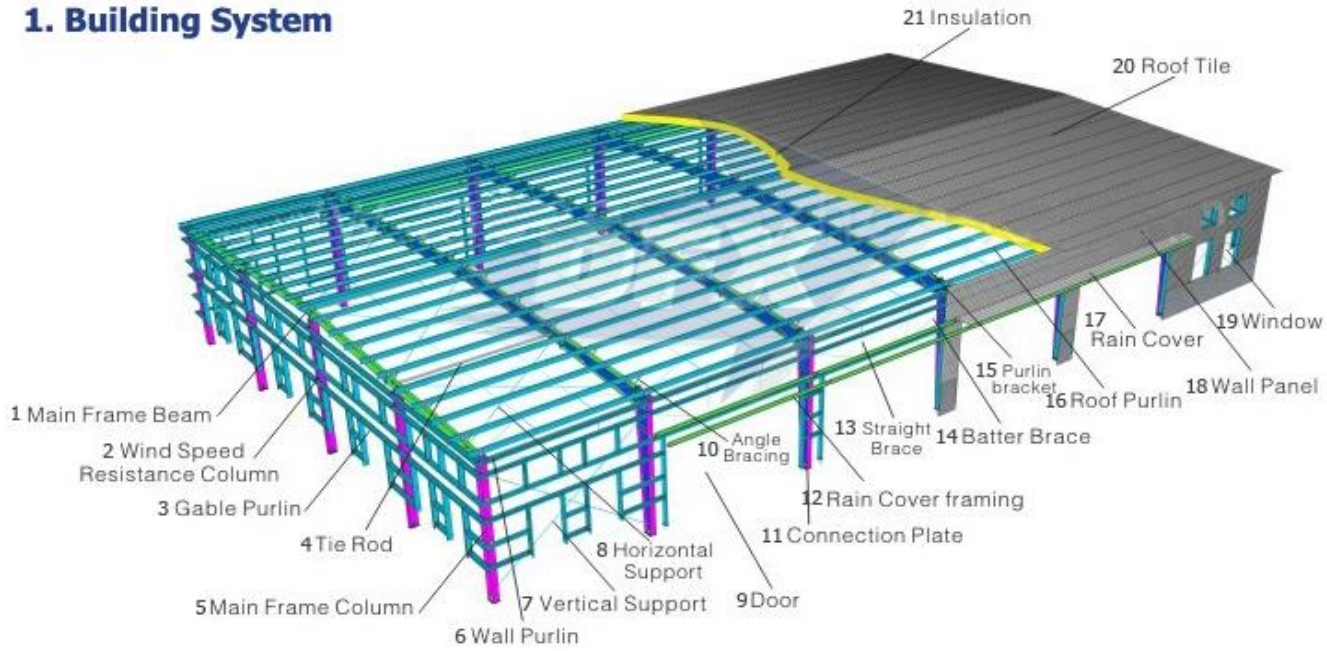

2. Specification

Items		Specification
Main Steel Frame	Column	5 mm and 6 mm
	Beam	5 mm and 6 mm
Secondary Frame	Purlin	1.5 mm
	Knee brace	12 mm
	Tie Rod	50 mm x 50 mm angle
	Brace	Sag Rod
	Vertical and Horizontal Support	Q235 Angle Steel, Round Bar or Steel Pipe
Maintenance system	Roof Panel	PU Sandwich Panel 50mm / Corrugated sheet 2mm
	Wall Panel	PU Sandwich Panel 50mm
Accessories	Window	As per design
	Door	As per design
	Rainspout	MS Sheet
Live load on Roof		0.57 (kN/m2) (Color steel panel surrounded)
Live load on Frame		0.57 (kN/m2)

Wind Resistance (km/hr)	160 (Exposure C) / 140 km per hour
Seismic Zone	2-B
Structure Usage	Up to 50 years
Finishing Options	Vast array of colors and textures available
Paint Options	Alkyd painting, two primary painting, two finish painting (gray paint, red paint, white paint, epoxy zinc etc.) Or Galvanized.

3. Detailed Images



RELATED PRODUCTS



+92 322 8000 190 UAN: +923 111 749 849 info@acco.com.pk

Office 2nd, 3rd Floor, Bigcity Plaza, Gulberg-III, Lahore, Pakistan
www.acco.com.pk

BILL OF QUANTITIES — PRE-ENGINEERED BUILDING

PEB Office / Commercial Shed · 54 × 66 ft · G+1 · Rev 2

A — CIVIL WORKS — Short Columns & Footings Only

#	Item Description	Specification	Qty	Unit	Rate (PKR)	Amount (PKR)	Notes
A.1	Isolated Pad Footings M-20 concrete, 5×5 ft, 2 ft deep, 12 nos grid	PCC 1:2:4 + RCC 1:1.5:3 Grade 60 steel @ 278/kg	12	nos	40,000	480,000	
A.2	Short RCC Columns 18"×18" up to plinth 2 ft, 12 nos	RCC 1:1.5:3, formwork, steel	12	nos	20,000	240,000	
A.3	Base Plate + Anchor Bolts MS plate 20mm, M24 bolts, 12 sets	Shop-fab, hot-dip galvanised	12	sets	12,500	150,000	
→ Civil Subtotal						**870,000**	

B — PEB STRUCTURAL STEEL — Primary + Secondary + Erection

#	Item Description	Specification	Qty	Unit	Rate (PKR)	Amount (PKR)	Notes
B.1	Primary Frames (Rigid Frames) Tapered I-section, 54 ft span, 5 bays @ 13.2 ft, 18 ft eave + ridge, Fe-345	IS 2062 Gr.B / ASTM A572 Gr.50 Fab @ ~5.8 kg/sft, ~20.7 MT total	20700	kg	540	11,178,000	
B.2	Secondary Members — Purlins / Girts Z/C-200×65×20 cold-formed, roof purlins + wall girts both floors	Galv or red-oxide coated ~2.1 kg/sft → ~7.5 MT	7500	kg	460	3,450,000	
B.3	Bracing System Rod X-bracing walls + roof wind bracing, sag rods	20mm dia rods + turnbuckles	1200	kg	480	576,000	
B.4	Eave Strut + Ridge Beam C-150 purlins at eave & ridge line	Cold-formed galvanised	450	kg	460	207,000	
B.5	Bolts, Cleats & Connections Gr 8.8 HSFG bolts, connection plates, gussets	Hot-dip galv, factory drilled	1	lot	420,000	420,000	
B.6	Surface Prep + Painting Shot blast Sa 2.5, 1 coat red-oxide 50µ + 1 coat finish 40µ	Alkyd primer + polyurethane topcoat	29850	kg	38	1,134,300	

BILL OF QUANTITIES — PRE-ENGINEERED BUILDING

PEB Office / Commercial Shed · 54 × 66 ft · G+1 · Rev 2

B.7	Fabrication & Erection Labour Factory fab + site erection, crane hire, safety gear	All-inclusive	7128	sft	135	962,280	
→ PEB Steel Subtotal						**17,927,580**	

C — CLADDING & ROOFING — 50mm Sandwich Panels + Checkered Sheet

#	Item Description	Specification	Qty	Unit	Rate (PKR)	Amount (PKR)	Notes
C.1	Wall Sandwich Panels — All 4 Walls 50mm PUF, 0.5mm PPGI both faces, total wall area ~4,320 sft	PIR 50mm U-value 0.38 W/m²K	4320	sft	650	2,808,000	
C.2	Roof Sandwich Panels — FF Roof 50mm PUF standing-seam roof panels, 3,564 sft + 5% laps	PIR 50mm, PPGI 0.5mm, slope ≥3°	3742	sft	650	2,432,300	
C.3	GF Inter-Floor Roof — Checkered Plate 3mm MS checkered sheet on C-purlin sub-frame, 3,564 sft	IS 3502 / BS EN 10025 ~23.6 kg/m², 3mm nominal	3564	sft	520	1,853,280	
C.4	Ridge Cap + Eave Flashing 0.6mm PPGI pre-formed flashings, ridge & eaves perimeter	Colour-matched PPGI	240	rft	380	91,200	
C.5	Corner Trims + Panel Accessories J-trims, corner pieces, neoprene tape, sealants	All-inclusive lot	1	lot	185,000	185,000	
C.6	Gutters & Downspouts 0.6mm GI half-round 6" gutter + 4" DWS, all 4 sides	Hot-dip galv, with leaf guards	240	rft	320	76,800	
→ Cladding Subtotal						**7,446,580**	

D — STAIRCASE — 6 ft Wide, GF to FF

#	Item Description	Specification	Qty	Unit	Rate (PKR)	Amount (PKR)	Notes

BILL OF QUANTITIES — PRE-ENGINEERED BUILDING

PEB Office / Commercial Shed · 54 × 66 ft · G+1 · Rev 2

D.1	MS Stringer Beams 2 nos ISMB 200, full flight GF to FF, 14 ft rise	Fe345, red-oxide painted	480	kg	540	259,200	
D.2	MS Checkered Plate Treads 6 ft × 10" per tread, 3mm checker, ~22 risers	Welded to stringers, anti-slip	22	nos	4,500	99,000	
D.3	SS/MS Handrail Both Sides 42" height, 2" sq tube top rail, vertical balusters @ 4"	MS painted or SS 304 option	60	rft	2,800	168,000	
D.4	Landing Platform (Mid + Top) 2 landings, 6×4 ft each, checker plate	3mm checker on RHS frame	48	sft	620	29,760	
→ Staircase Subtotal						**555,960**	

E — PASSENGER LIFT — 5-Person, 2-Stop (G+1)

#	Item Description	Specification	Qty	Unit	Rate (PKR)	Amount (PKR)	Notes
E.1	Lift Supply & Install — 5-Person 450 kg rated, 2-stop (G+1), 0.63 m/s, stainless cabin	SIGMA/Maison/Otis equiv 1000×1200mm car, 2-panel door	1	nos	2,800,000	2,800,000	
E.2	Lift Shaft Construction (PEB Hoistway) MS column + sandwich panel shaft enclosure, 2-stop pit + overhead	1.6m × 2.0m shaft, 4m OAH	1	lot	380,000	380,000	
E.3	Pit Construction (RCC) 1.2m deep pit, waterproofed, buffer & pit ladder	RCC 1:1.5:3	1	lot	95,000	95,000	
E.4	Lift Electrical & Control Panel 3-phase 415V supply, VVVF drive, ARD, intercom	Civil connection only	1	lot	85,000	85,000	
→ Lift Subtotal						**3,360,000**	

F — DOORS, WINDOWS, ACCESSORIES & MISCELLANEOUS

#	Item Description	Specification	Qty	Unit	Rate (PKR)	Amount (PKR)	Notes

BILL OF QUANTITIES — PRE-ENGINEERED BUILDING

PEB Office / Commercial Shed · 54 × 66 ft · G+1 · Rev 2

F.1	Industrial Sliding / Sectional Door 10×10 ft GI insulated, manual, main entrance	0.5mm PPGI panel, 2 nos	2	nos	145,000	290,000
F.2	Personnel Doors (Single Leaf) 3×7 ft, MS hollow section frame + sandwich panel infill	4 nos (2 GF, 2 FF)	4	nos	28,000	112,000
F.3	Fixed / Sliding Windows UPVC or aluminium fixed glazed 3×4 ft panels	6 nos (3 per floor)	6	nos	22,500	135,000
F.4	Turbo Ventilators 24" dia, GI, ridge-mounted, natural ventilation GF & FF	4 nos total	4	nos	12,000	48,000
F.5	External Drainage / Site Works PVC pipe 4", soakpits, site levelling, perimeter drain	Lumpsum	1	lot	280,000	280,000
→ Misc Subtotal						**865,000**

SUMMARY — COST SUMMARY — Rev 2

Section	Description	Amount (PKR)	% of Total
A	Civil Works — Footings & Short Columns Only	870,000	2.8%
B	PEB Structural Steel — Primary + Secondary + Erection	17,927,580	57.8%
C	Cladding & Roofing — Sandwich Panels + Checkered Sheet	7,446,580	24.0%
D	Staircase — 6 ft Wide, GF to FF	555,960	1.8%
E	Passenger Lift — 5-Person, 2-Stop	3,360,000	10.8%
F	Doors, Windows, Accessories & Drainage	865,000	2.8%
BASE COST (sum of A to F)		**31,025,120**	**100%**

RATES — PER SFT RATE ANALYSIS

BILL OF QUANTITIES — PRE-ENGINEERED BUILDING

PEB Office / Commercial Shed · 54 × 66 ft · G+1 · Rev 2

GF Covered Area	**3,564 sft**	*54 × 66 ft*
Total Covered Area	**7,128 sft**	*G + 1st floor*
Rate/sft (Excl. GST)	**PKR 4,353**	*on 7,128 sft total*
Steel-Only Rate/sft	**PKR 2,515**	*PEB structure portion*
Cladding Rate/sft	**PKR 1,045**	*sandwich + checkered*

BENCHMARK — MARKET BENCHMARK VALIDATION — Lahore, May 2026

#	Parameter	This Quotation	Market Range	Status
1	Structural steel (fab + erect)	**PKR 540/kg**	500–580 /kg	✓ **Within Range**
2	50mm PUF wall sandwich panel	**PKR 650/sft**	600–720 /sft	✓ **Within Range**
3	50mm PUF roof sandwich panel	**PKR 650/sft**	620–750 /sft	✓ **Within Range**
4	3mm checkered plate (supply+fix)	**PKR 520/sft**	490–560 /sft	✓ **Within Range**
5	5-person lift (2-stop, supply+install)	**PKR 28 lac**	25–35 lac	✓ **Within Range**
6	Overall rate per sft (excl. GST)	**PKR 4,684/sft**	3,500–6,000/sft	✓ **Mid-Premium**
7	Iron/rebar — Grade 60	**PKR 278/kg**	276–315 /kg	✓ **Current Market**

ITEMS EXCLUDED FROM THIS QUOTATION (Client's Scope)

Plinth filling, PCC sub-base & GF RCC slab · Internal partitions & false ceiling · Flooring finish · Plumbing · HVAC/Air conditioning · Electrical wiring & fixtures · Fire suppression & alarm · CCTV · Painting of interiors · External boundary wall · Approach road · Site survey / soil investigation · All solar panels, inverters, batteries & mounting

T&C — TERMS & CONDITIONS

1	**Payment Schedule**	30% mobilisation advance · 40% on delivery of steel to site · 20% on erection completion · 10% on final handover

BILL OF QUANTITIES — PRE-ENGINEERED BUILDING

PEB Office / Commercial Shed · 54 × 66 ft · G+1 · Rev 2

2	**Quotation Validity**	Rates valid 30 days from 07 May 2026, subject to steel market (Grade 60 @ PKR 278/kg base)
3	**Delivery Timeline**	Fabrication 6–8 weeks from drawing approval · Site erection 3–4 weeks
4	**Design Responsibility**	Structural drawings, anchor bolt plan & foundation reactions by PEB contractor. SBC ≥ 100 kN/m² assumed
5	**Wind & Seismic**	ASCE 7 / NBC Pakistan · Basic wind 120 km/h · Seismic zone 2A (Lahore)
6	**Warranty**	Structure 20 years · Panels 10 years · Lift per OEM warranty
7	**Client Obligations**	GST, NOC, town planning fees & site security are client's responsibility

Prepared by — Senior QS / PEB Engineer

Client Acceptance & Signature

Name / Designation / Date

Name / Company Stamp / Date
