To,
Mr. Abdullah Sharif Sahab
Lahore, Punjab Pakistan

Date: October 30, 2025
Ref#: ACCO/PEB/805

SUBJECT: - **QUOTATION FOR CONSTRUCTION OF PRE-ENGINEERED SHED WAREHOUSE**

السلام علیکم
We are pleased to submit our best quote for subject work as follows: -

Sr.#	Item Description	Area (SFT)	Rate (Rs.)	Amount
1	Construction, supply and installation of a prefabricated steel shed (100' x 16') Complete in all respect. Height Approx 40 feet	1,600	950/-	1,520,000/-
	Total Amount			**1,520,000/-**

Terms & Conditions:


1. This quotation excludes all taxes.
2. Complication Time 20 days
3. 50% Advance before starting the Project other balance Payment according to percentage of Work
4. Provision of storage facilities for our goods and equipment, where necessary, shall be client responsibility.
5. Electricity & water supply will be provided by the client.
6. This quotation is valid for 30 days from above mentioned date.
7. Civil Work is not included.

We will be obliged for your cooperation in this regard.
Thanks & Regards.
Truly yours,

Tanveer Ahmed
Director
+92-322-8000190

Product description

1. Building System

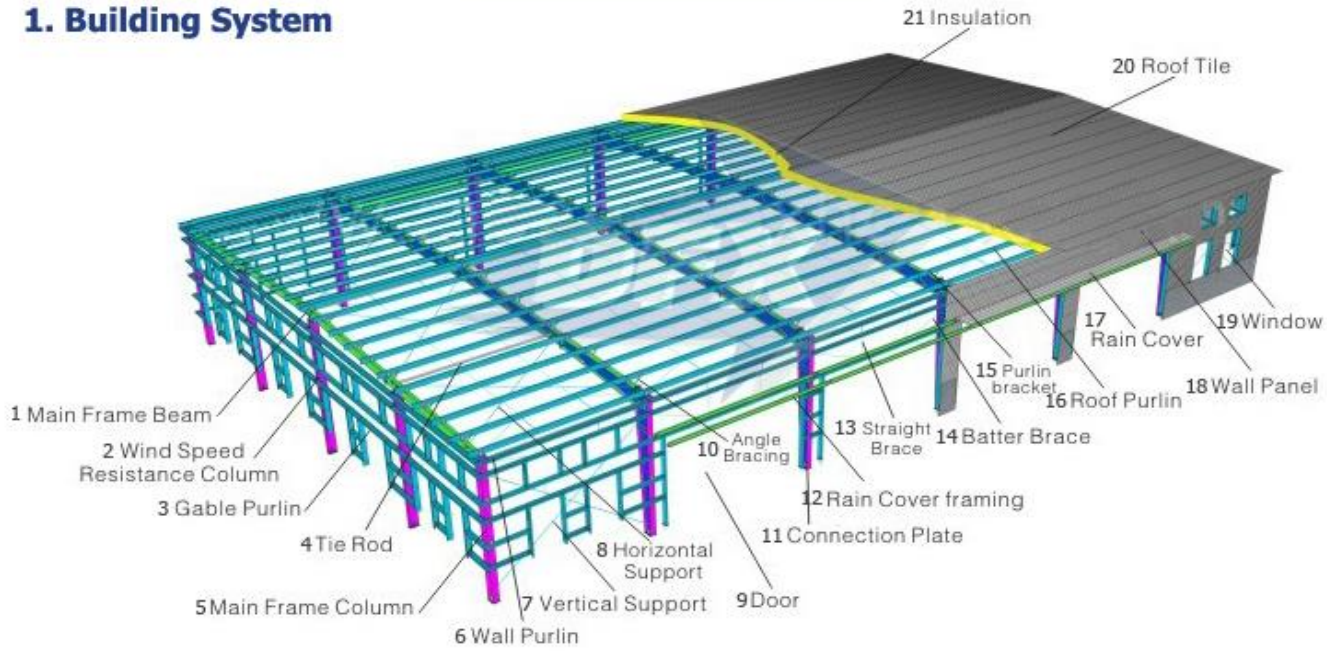

2. Specification

Items		Specification
Main Steel Frame	Column	Q235, Q345 Welded H Section Steel
	Beam	Q235, Q345 Welded H Section Steel
Secondary Frame	Purlin	Q235 C and Z purlin
	Knee brace	Q235 Angle Steel
	Tie Rod	Q235 Circular Steel Pipe
	Brace	Q235 Round Bar
	Vertical and Horizontal Support	Q235 Angle Steel, Round Bar or Steel Pipe
Maintenance system	Roof Panel	50mm Glass Wool Panel / Corrugated Steel Sheet 0.42 mm thick
	Wall Panel	50mm Glass Wool Panel / Corrugated Steel Sheet 0.42 mm thick
Accessories	Window	Aluminum Alloy Window / PVC Window / Sandwich Panel Window
	Door	Sliding Sandwich Panel Door / Rolling Metal Door / Personal Door
	Rainspout	PVC

Live load on Roof	0.57 (kN/m2) (Color steel panel surrounded)
Live load on Frame	0.57 (kN/m2)
Wind Resistance (km/hr)	160 (Exposure C)
Seismic Zone	2-B
Structure Usage	Up to 50 years
Finishing Options	Vast array of colors and textures available
Paint Options	Alkyd painting, two primary painting, two finish painting (gray paint, red paint, white paint, epoxy zinc etc.) Or Galvanized.

3. Detailed Images



RELATED PRODUCTS



+92 322 8000 190 UAN: +923 111 749 849 info@acco.com.pk

Office 2nd, 3rd Floor, Bigcity Plaza, Gulberg-III, Lahore, Pakistan
www.acco.com.pk
