To,
Mr. Shafiq Sahab
Lahore, Punjab Pakistan

Date: November 18, 2025
Ref#: ACCO/PEB/961

SUBJECT: - **QUOTATION FOR CONSTRUCTION OF PRE-ENGINEERED BUILDING IN LAHORE**

السلام علیکم
We are pleased to submit our best quote for subject work as follows: -

| Sr.# | Item Description | Area (SFT) | Rate (Rs.) | Amount |
|---|---|---|---|---|
| 1 | Construction, supply and installation of a prefabricated steel structure shed for warehouse Complete in all respect.<br>Area: 200x145 feet<br>Height Approx. 28 feet sides & 33 feet center | 29,000 | 1,450/- | 42,050,000/- |
| | **Total Amount** | | | **42,050,000/-** |

**Terms & Conditions:**


1. This quotation excludes all taxes.
2. Complication Time 90 days
3. 50% Advance before starting the Project other balance Payment according to percentage of Work
4. Provision of storage facilities for our goods and equipment, where necessary, shall be client responsibility.
5. Electricity & water supply will be provided by the client.
6. This quotation is valid for 30 days from above mentioned date.
7. Civil Work is not included.

We will be obliged for your cooperation in this regard.
Thanks & Regards.
Truly yours,

**Tanveer Ahmed**
**Director**
+92-322-8000190

## Product description

### 1. Building System

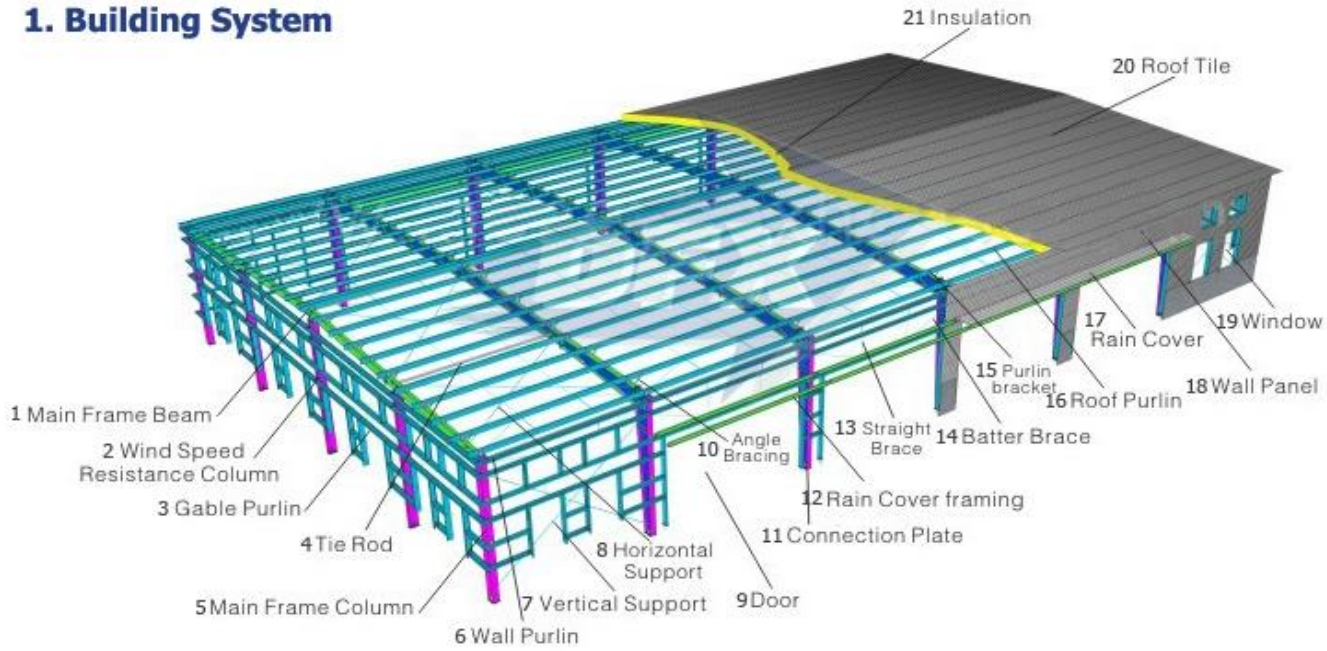


## 2. Specification

| Items | | Specification |
|---|---|---|
| Main Steel Frame | Column | 5 mm and 6 mm |
| | Beam | 5 mm and 6 mm |
| Secondary Frame | Purlin | 1.5 mm |
| | Knee brace | 12 mm |
| | Tie Rod | 50 mm x 50 mm angle |
| | Brace | Sag Rod |
| | Vertical and Horizontal Support | Q235 Angle Steel, Round Bar or Steel Pipe |
| Maintenance system | Roof Panel | 0.45 mm sheet PPGI (Pre-Painted Galvanized Iron) |
| | Wall Panel | 0.45 mm sheet PPGI (Pre-Painted Galvanized Iron) |
| Accessories | Window | Nil |
| | Door | Nil |
| | Rainspout | MS Sheet |
| Live load on Roof | | 0.57 (kN/m2) (Color steel panel surrounded) |
| Live load on Frame | | 0.57 (kN/m2) |

| | |
|---|---|
| Wind Resistance (km/hr) | 160 (Exposure C) / 140 km per hour |
| Seismic Zone | 2-B |
| Structure Usage | Up to 50 years |
| Finishing Options | Vast array of colors and textures available |
| Paint Options | Alkyd painting, two primary painting, two finish painting (gray paint, red paint, white paint, epoxy zinc etc.) Or Galvanized. |

## 3. Detailed Images



## RELATED PRODUCTS



+92 322 8000 190 UAN: +923 111 749 849 info@acco.com.pk



Office 2nd, 3rd Floor, Bigcity Plaza, Gulberg-III, Lahore, Pakistan
www.acco.com.pk
