To,
Mr. Zain Ul Abdeen Sahab
Layyah, Punjab Pakistan

Date: November 18, 2025
Ref#: ACCO/PEB/923

SUBJECT: - **QUOTATION FOR CONSTRUCTION OF PRE-ENGINEERED BANQUET HALL**

السلام علیکم
We are pleased to submit our best quote for subject work as follows: -

| Sr.# | Item Description | Area (SFT) | Rate (Rs.) | Amount |
|---|---|---|---|---|
| 1 | Construction, supply and installation of a prefabricated steel structure banquet hall for 1000 persons Complete in all respect.<br>Area: 15000 sft (15 sft per person)<br>Support areas: 4000 sft<br>Height Approx. 18 feet | 19,000 | 1,300/- | 24,700,000/- |
| | **Total Amount** | | | **24,700,000/-** |

**Terms & Conditions:**


1. This quotation excludes all taxes.
2. Complication Time 45 days
3. 50% Advance before starting the Project other balance Payment according to percentage of Work
4. Provision of storage facilities for our goods and equipment, where necessary, shall be client responsibility.
5. Electricity & water supply will be provided by the client.
6. This quotation is valid for 30 days from above mentioned date.
7. Civil Work is not included.

We will be obliged for your cooperation in this regard.
Thanks & Regards.
Truly yours,

**Tanveer Ahmed**
**Director**
+92-322-8000190

## Product description

### 1. Building System

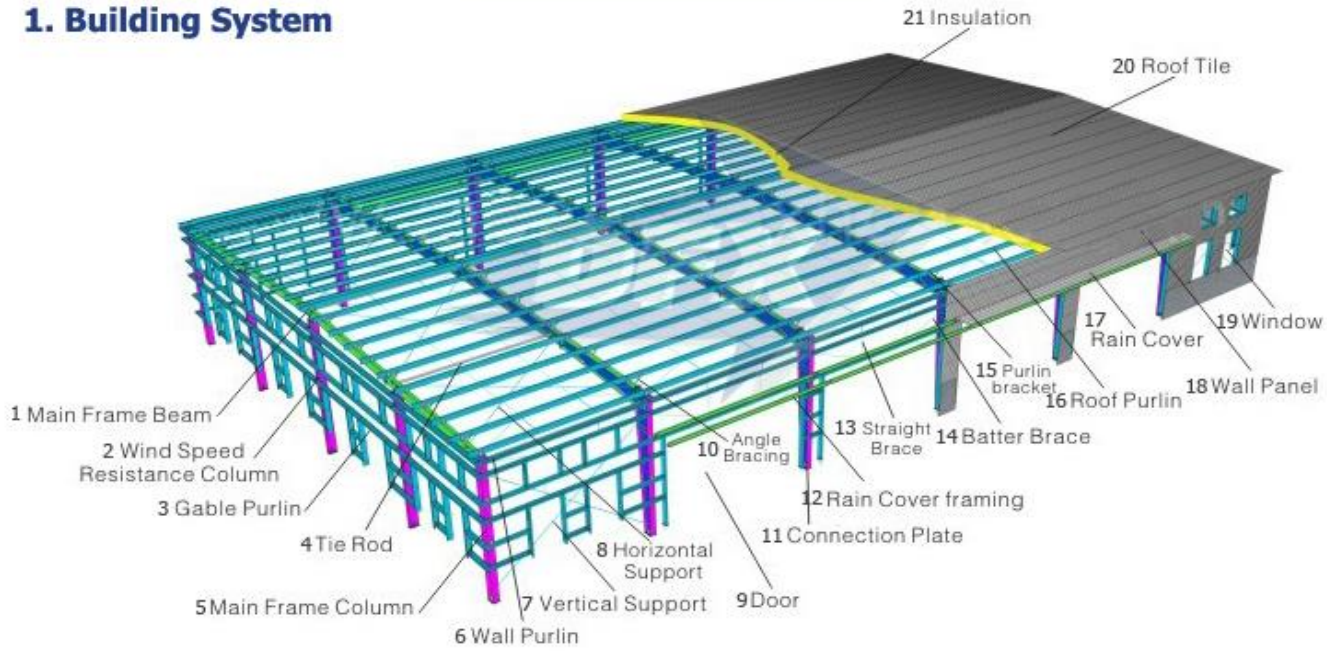


## 2. Specification

| Items | | Specification |
|---|---|---|
| Main Steel Frame | Column | Q235, Q345 Welded H Section Steel |
| | Beam | Q235, Q345 Welded H Section Steel |
| Secondary Frame | Purlin | Q235 C and Z purlin |
| | Knee brace | Q235 Angle Steel |
| | Tie Rod | Q235 Circular Steel Pipe |
| | Brace | Q235 Round Bar |
| | Vertical and Horizontal Support | Q235 Angle Steel, Round Bar or Steel Pipe |
| Maintenance system | Roof Panel | 0.42 mm thick PPGI Sheet |
| | Wall Panel | 0.42 mm thick PPGI Sheet |
| Accessories | Window | Nil |
| | Door | Nil |
| | Rainspout | PVC |
| Live load on Roof | | 0.57 (kN/m2) (Color steel panel surrounded) |
| Live load on Frame | | 0.57 (kN/m2) |

| | |
|---|---|
| Wind Resistance (km/hr) | 160 (Exposure C) |
| Seismic Zone | 2-B |
| Structure Usage | Up to 50 years |
| Finishing Options | Vast array of colors and textures available |
| Paint Options | Alkyd painting, two primary painting, two finish painting (gray paint, red paint, white paint, epoxy zinc etc.) Or Galvanized. |

## 3. Detailed Images



## RELATED PRODUCTS



+92 322 8000 190 UAN: +923 111 749 849 info@acco.com.pk



Office 2nd, 3rd Floor, Bigcity Plaza, Gulberg-III, Lahore, Pakistan
www.acco.com.pk
