To,
Mr. Mohsin Baig Sahab
Manager Procurement, Gharibwal Cement Limited

Date: November 20, 2025
Ref#: ACCO/PEB/932

SUBJECT: - **QUOTATION FOR CONSTRUCTION OF COAL PRE-ENGINEERED BUILDING**

السلام علیکم
We are pleased to submit our best quote for subject work as follows: -

Sr.#	Item Description	Area (SFT)	Rate (Rs.)	Amount
1	Construction, supply and installation of a prefabricated steel shed for coal warehouse Complete in all respect. Height Approx. 49 feet 6 inches	79,241	1,493/-	118,306,813/-
	GST 18%			21,295,226/-
	Total Amount			**139,602,039/-**

Terms & Conditions:


1. This quotation excludes all taxes.
2. Complication Time 30 days
3. 50% Advance before starting the Project other balance Payment according to percentage of Work
4. Provision of storage facilities for our goods and equipment, where necessary, shall be client responsibility.
5. Electricity & water supply will be provided by the client.
6. This quotation is valid for 30 days from above mentioned date.
7. Civil Work is not included.

We will be obliged for your cooperation in this regard.
Thanks & Regards.
Truly yours,

Tanveer Ahmed
Director
+92-322-8000190

Product description

1. Building System

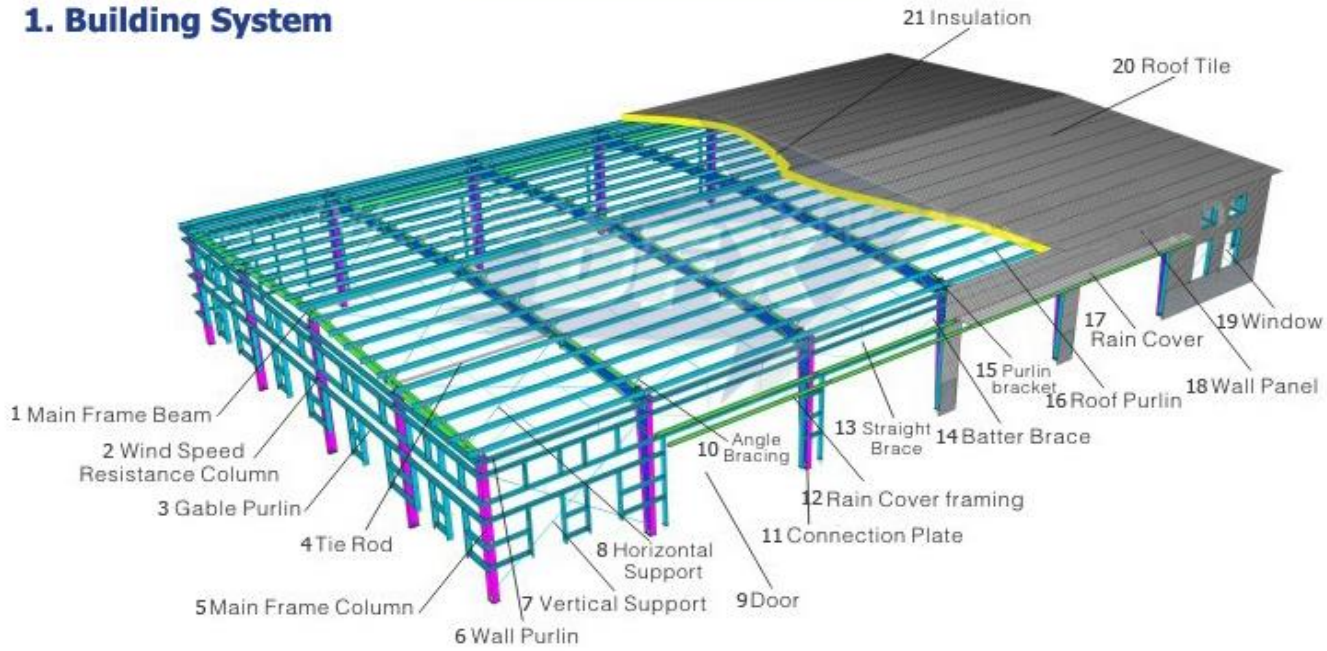

2. Specification

Items		Specification
Main Steel Frame	Column	5 mm and 6 mm
	Beam	5 mm and 6 mm
Secondary Frame	Purlin	1.5 mm
	Knee brace	12 mm
	Tie Rod	50 mm x 50 mm angle
	Brace	Sag Rod
	Vertical and Horizontal Support	Q235 Angle Steel, Round Bar or Steel Pipe
Maintenance system	Roof Panel	0.45 mm sheet PPGI (Pre-Painted Galvanized Iron)
	Wall Panel	0.45 mm sheet PPGI (Pre-Painted Galvanized Iron)
Accessories	Window	Nil
	Door	Nil
	Rainspout	MS Sheet
Live load on Roof		0.57 (kN/m2) (Color steel panel surrounded)
Live load on Frame		0.57 (kN/m2)

Wind Resistance (km/hr)	160 (Exposure C) / 140 km per hour
Seismic Zone	2-B
Structure Usage	Up to 50 years
Finishing Options	Vast array of colors and textures available
Paint Options	Alkyd painting, two primary painting, two finish painting (gray paint, red paint, white paint, epoxy zinc etc.) Or Galvanized.

3. Detailed Images




RELATED PRODUCTS



+92 322 8000 190 UAN: +923 111 749 849 info@acco.com.pk


Office 2nd, 3rd Floor, Bigcity Plaza, Gulberg-III, Lahore, Pakistan
www.acco.com.pk

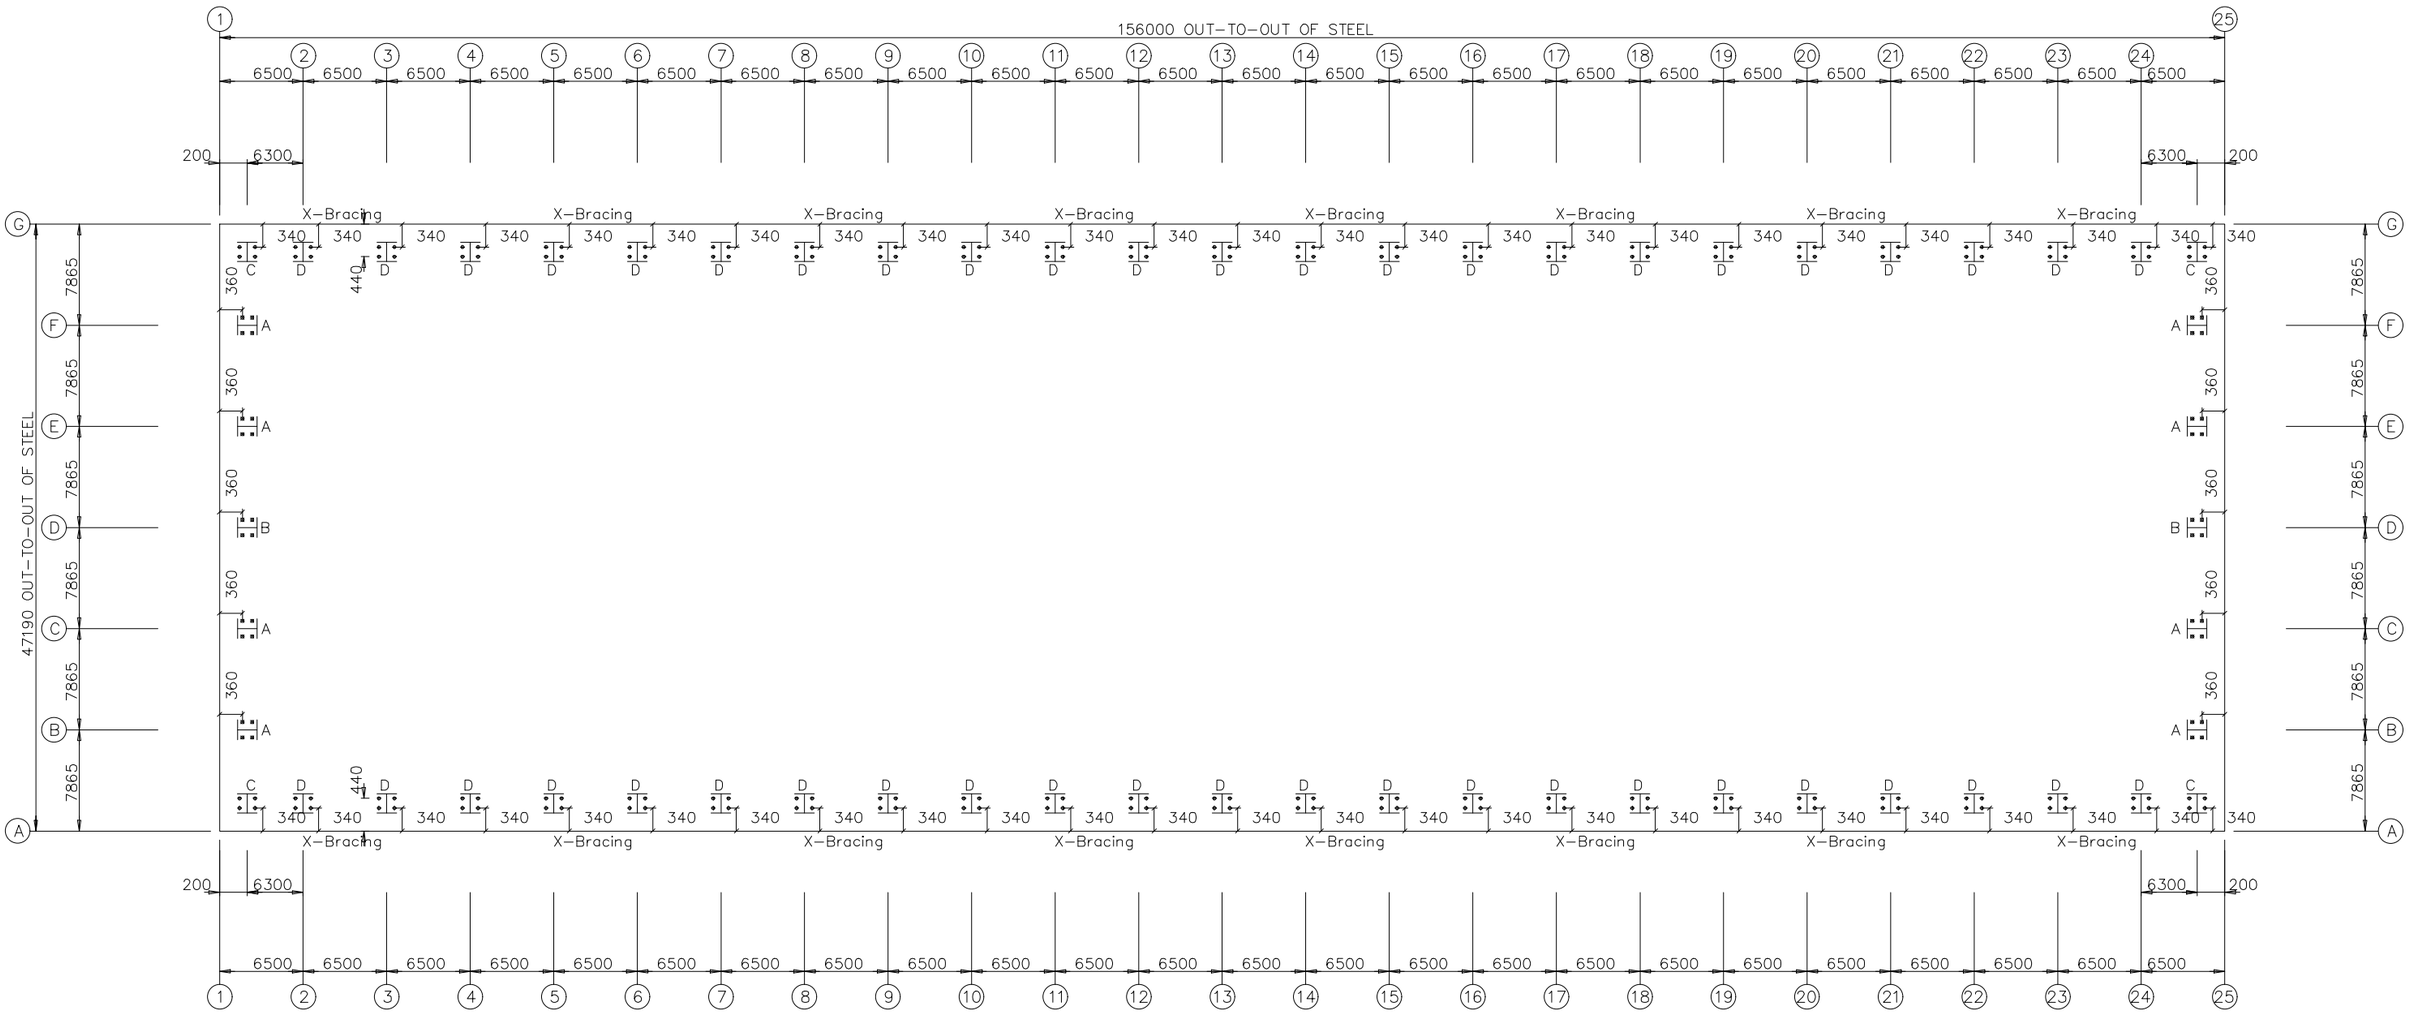

ARCHITECT ZUBAIR AHMED ZAFAR ALI	PROJECT MANAGER TANVEER AHMED	CLIENT _____	PROJECT CONSTRUCTION OF PRE-ENGINEERED CEMENT PLANT - COAL SHED
ADDRESS _____	No. / ISSUED / DATE 1. PROPOSED DRAWING	CONSULTANT : AHMED CONSTRUCTION COMPANY OFFICE NO.2,3RD FLOOR BIG CITY PLAZA, GULBERG-iii,Lahore 0322-8000190	DRAWING ANCHOR BOLT PLAN

DRAWN	MUHMMAD SAEED
PLOTTED DATE	18-November-2025
SCALE	SCALED TO FIT
DWG. NO.	01

ACCO
ARCHITECTURE & CONSTRUCTION

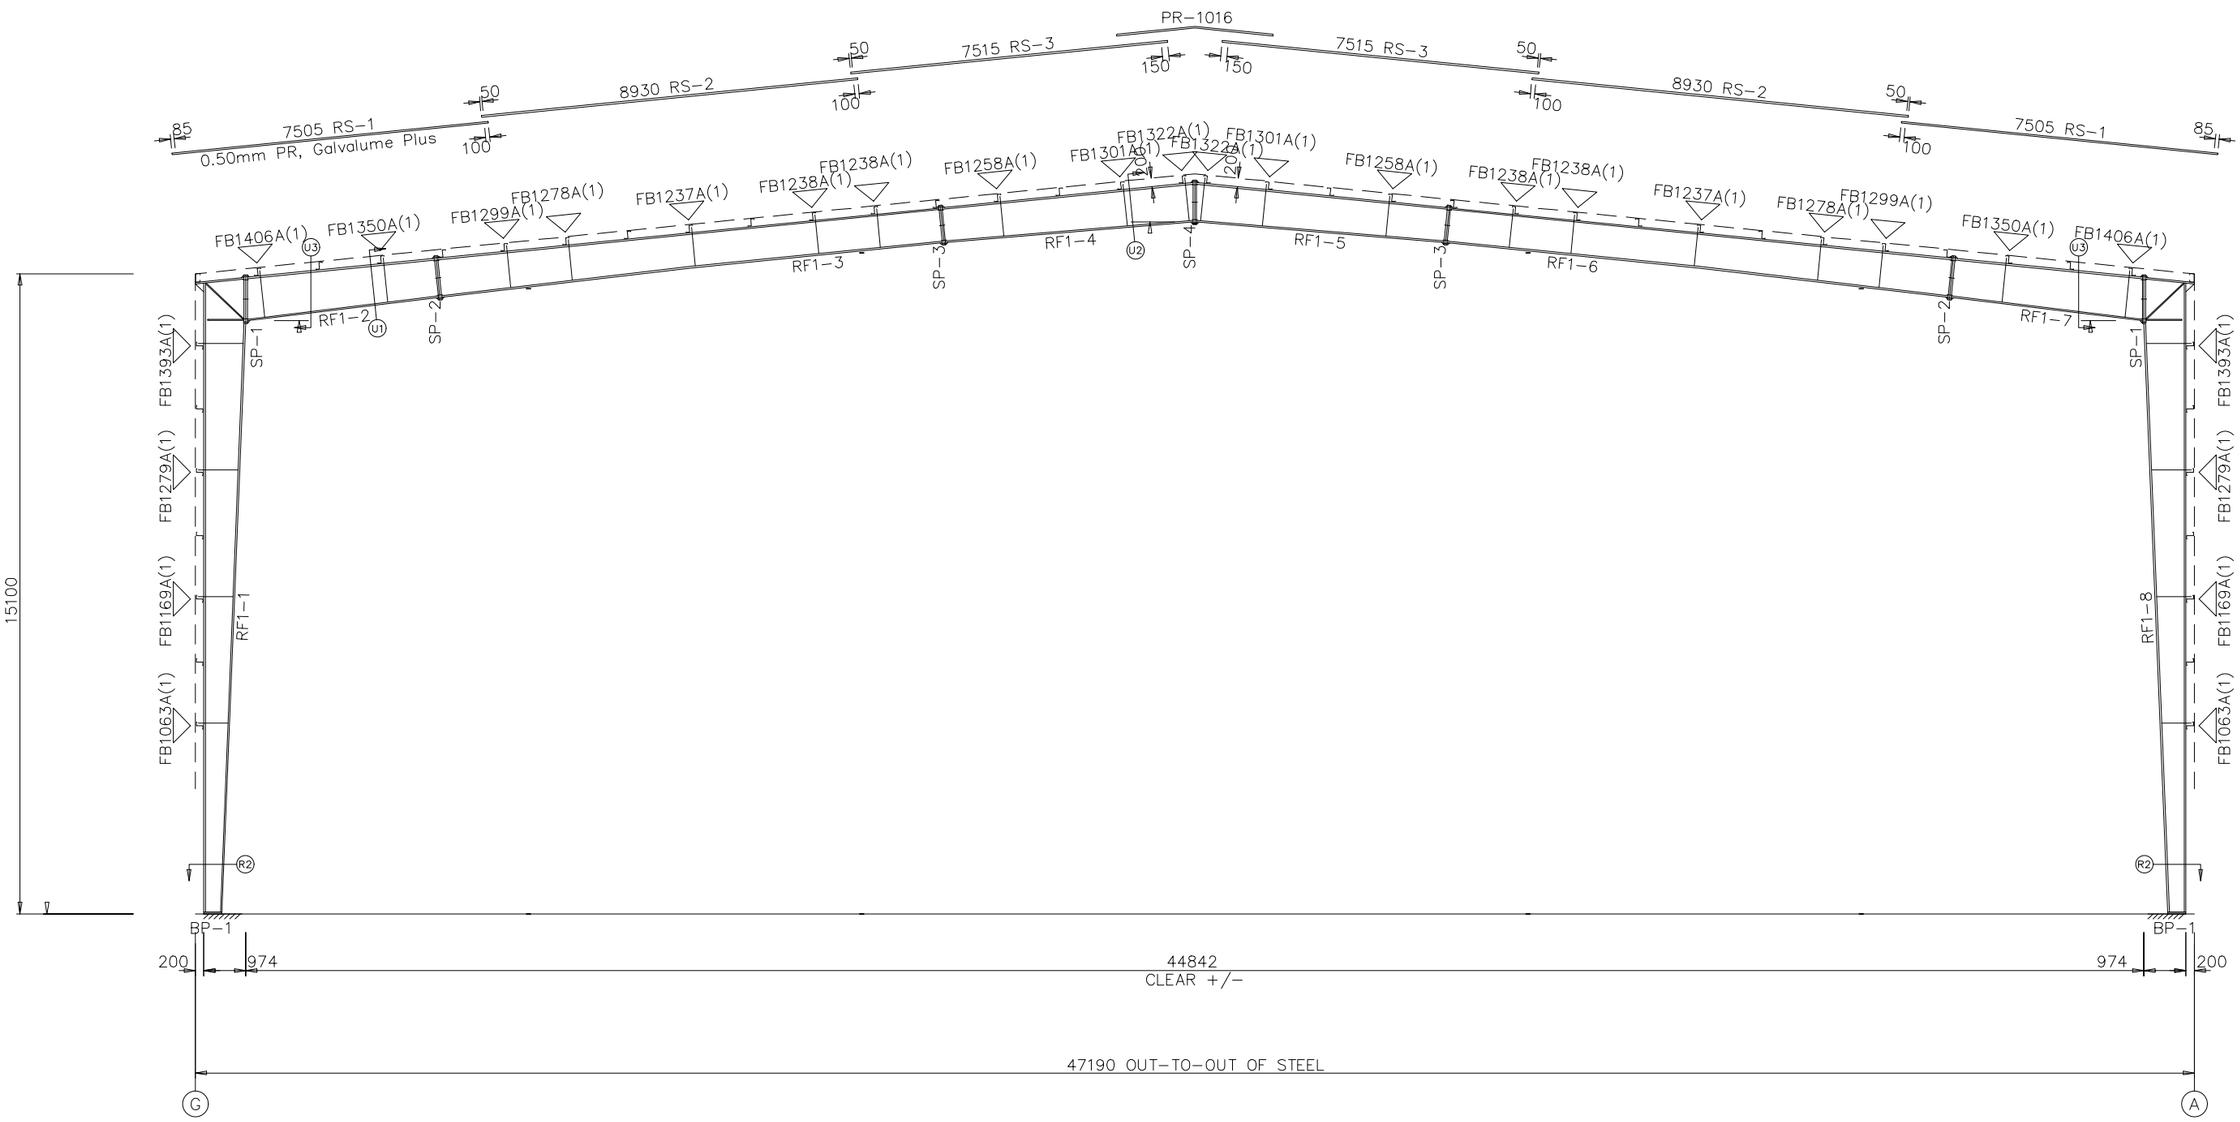


RIGID FRAME ELEVATION: FRAME LINE 1 2 3 4 5 6 7 8 9 10 11 12 13 14 15 16 17 18 19 20 21 22 23 24 25

ARCHITECT ZUBAIR AHMED ZAFAR ALI	PROJECT MANAGER TANVEER AHMED	CLIENT _____	PROJECT CONSTRUCTION OF PRE-ENGINEERED CEMENT PLANT - COAL SHED	DRAWN MUHMMAD SAEED
ADDRESS _____	No. / ISSUED / DATE 1. PROPOSED DRAWING	CONSULTANT : AHMED CONSTRUCTION COMPANY OFFICE NO.2,3RD FLOOR BIG CITY PLAZA, GULBERG-iii,Lahore 0322-8000190	DRAWING RIGID FRAME ELEVATION	PLOTTED DATE 18-November-2025 SCALE SCALED TO FIT

ACCO
ARCHITECTURE & CONSTRUCTION

DWG. NO. 02

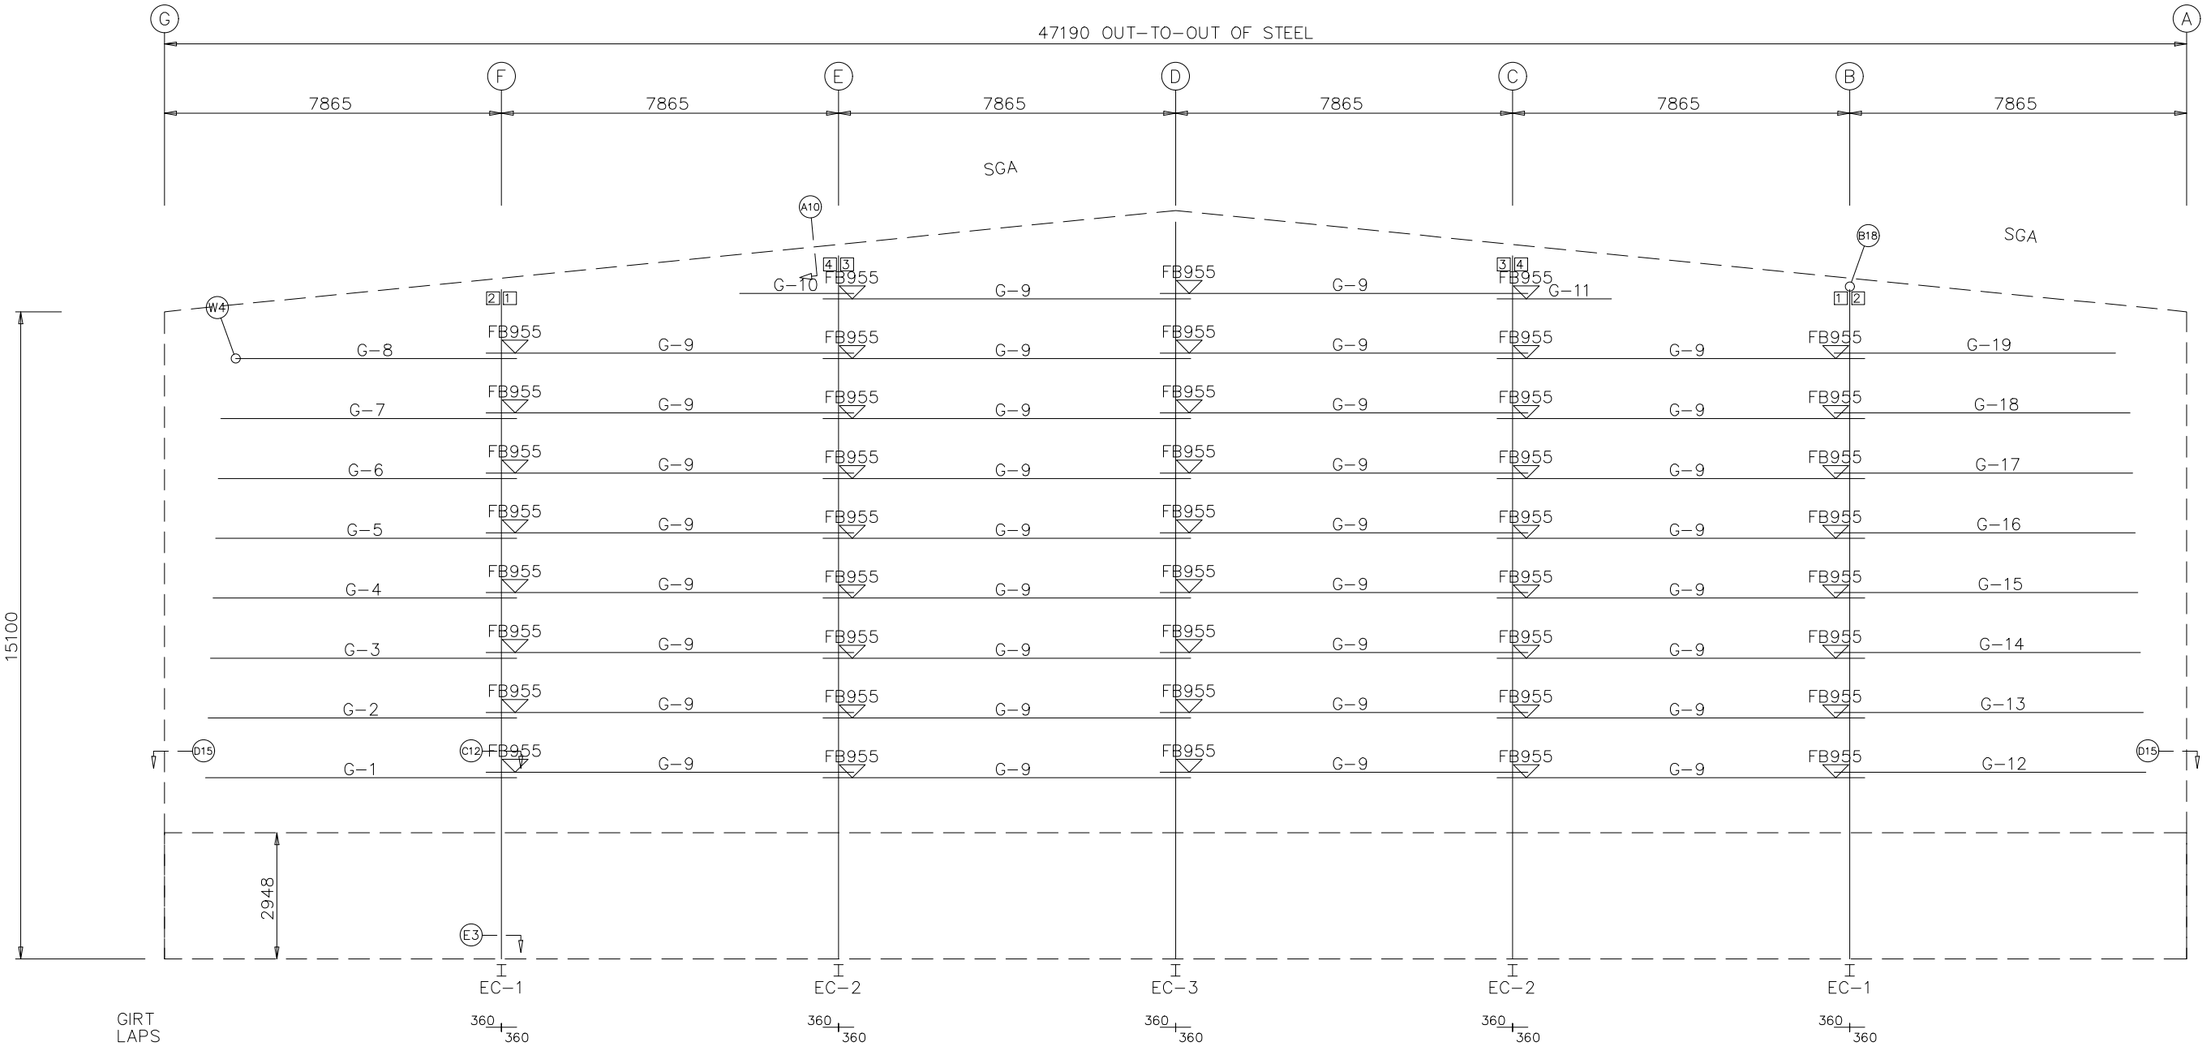


ENDWALL FRAMING: FRAME LINE 1 & 25

ARCHITECT ZUBAIR AHMED ZAFAR ALI	PROJECT MANAGER TANVEER AHMED	CLIENT _____	PROJECT CONSTRUCTION OF PRE-ENGINEERED CEMENT PLANT - COAL SHED
ADDRESS _____	No. / ISSUED / DATE 1. PROPOSED DRAWING	CONSULTANT : AHMED CONSTRUCTION COMPANY OFFICE NO.2,3RD FLOOR BIG CITY PLAZA, GULBERG-iii,Lahore 0322-8000190	DRAWING END WALL FRAMING

DRAWN	MUHMMAD SAEED
PLOTTED DATE	18-November-2025
SCALE	SCALED TO FIT
DWG. NO.	03

ACCO
ARCHITECTURE & CONSTRUCTION

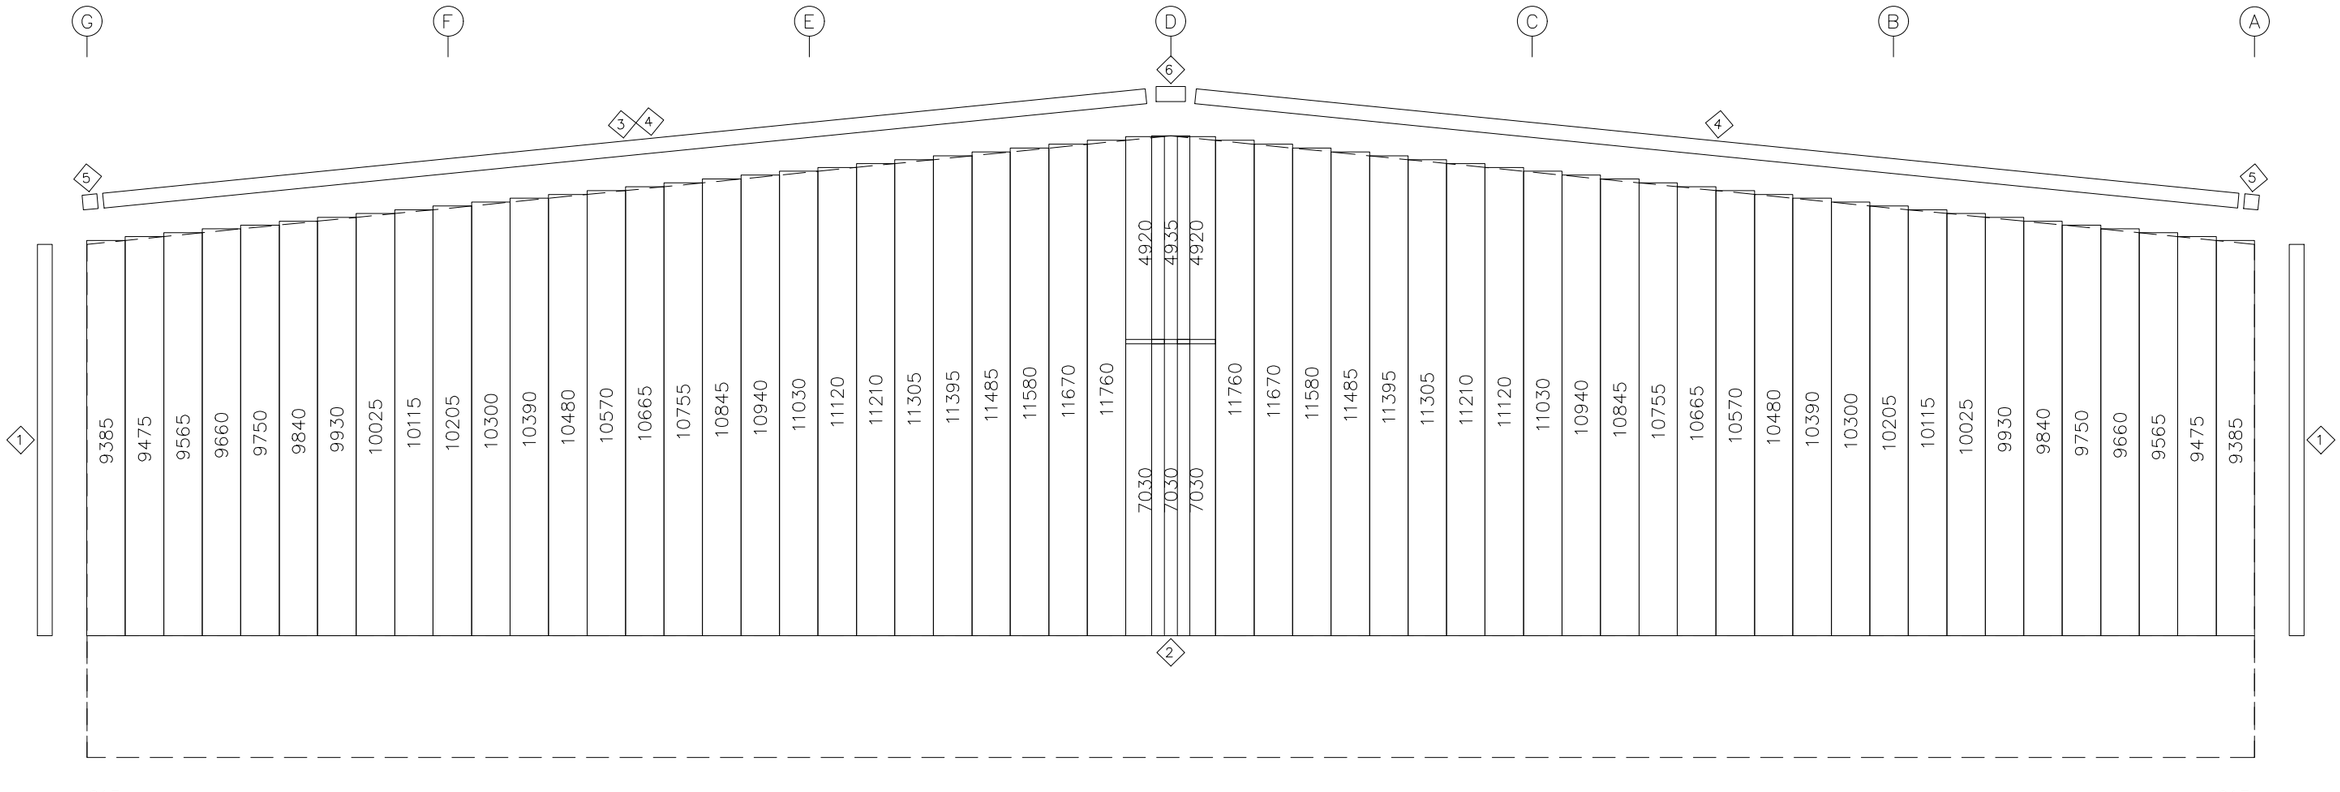


ENDWALL SHEETING & TRIM: FRAME LINE 1 & 25

PANELS: 0.50mm PR – Beige RAL1001

ARCHITECT ZUBAIR AHMED ZAFAR ALI	PROJECT MANAGER TANVEER AHMED	CLIENT _____
ADDRESS _____	No. / ISSUED / DATE 1. PROPOSED DRAWING	CONSULTANT : AHMED CONSTRUCTION COMPANY OFFICE NO.2,3RD FLOOR BIG CITY PLAZA, GULBERG-iii,Lahore 0322-8000190

PROJECT CONSTRUCTION OF PRE-ENGINEERED CEMENT PLANT - COAL SHED	DRAWN MUHMMAD SAEED	ACCO ARCHITECTURE & CONSTRUCTION	
DRAWING ENDWALL SHEETING & TRIM	PLOTTED DATE 18-November-2025		
	SCALE SCALED TO FIT	DWG. NO. 04	

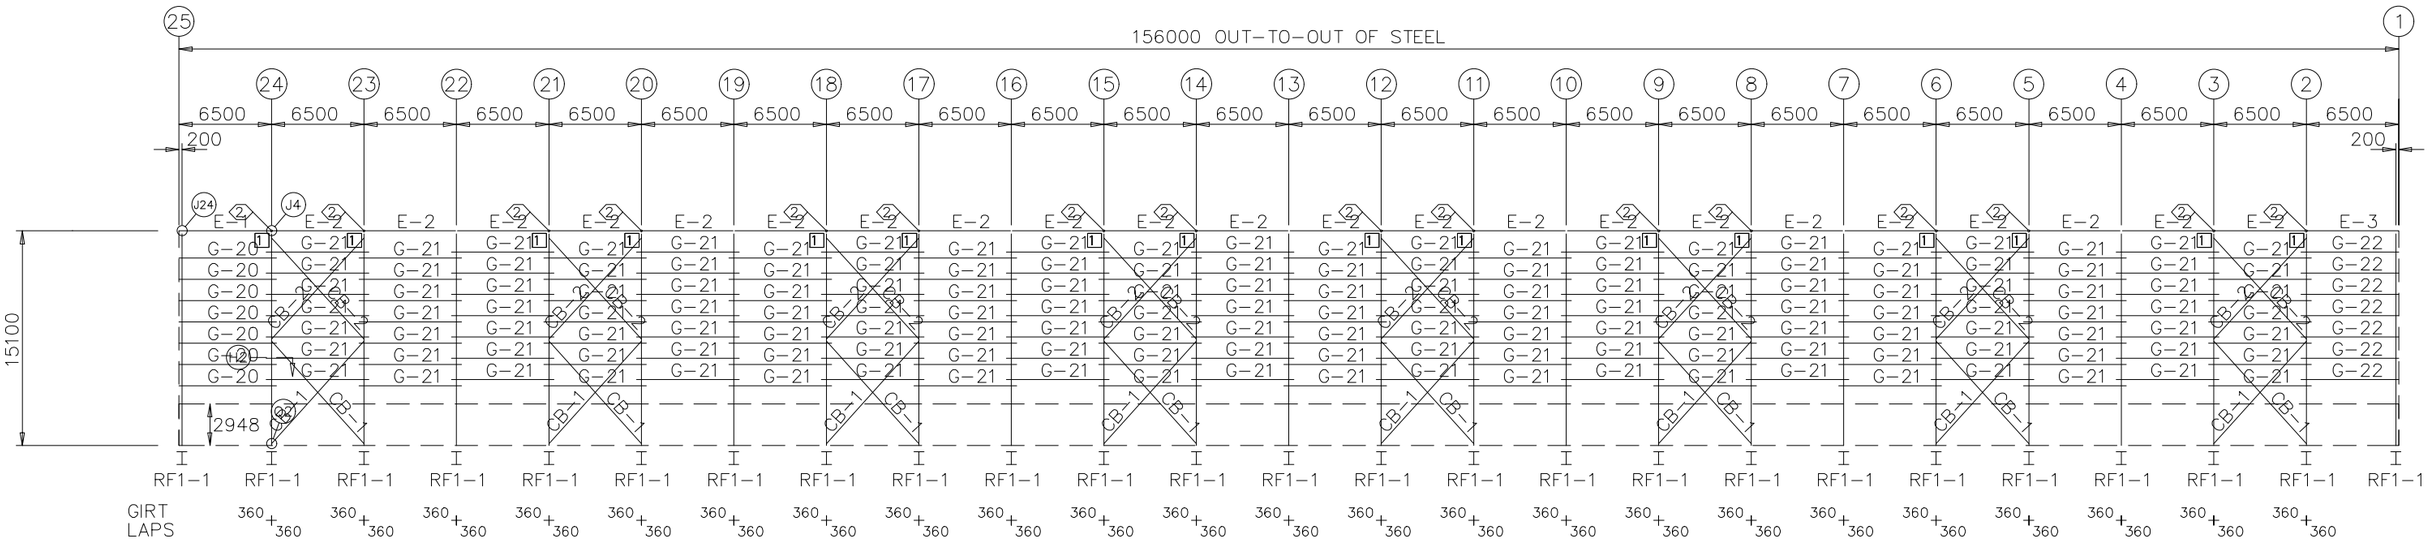


SIDEWALL FRAMING: FRAME LINE A & G

ARCHITECT ZUBAIR AHMED ZAFAR ALI	PROJECT MANAGER TANVEER AHMED	CLIENT _____	PROJECT CONSTRUCTION OF PRE-ENGINEERED CEMENT PLANT - COAL SHED
ADDRESS _____	No. / ISSUED / DATE 1. PROPOSED DRAWING	CONSULTANT : AHMED CONSTRUCTION COMPANY OFFICE NO.2,3RD FLOOR BIG CITY PLAZA, GULBERG-iii,Lahore 0322-8000190	DRAWING SIDEWALL FRAMING

DRAWN	MUHMMAD SAEED
PLOTTED DATE	18-November-2025
SCALE	SCALED TO FIT
DWG. NO.	05

ACCO
ARCHITECTURE & CONSTRUCTION

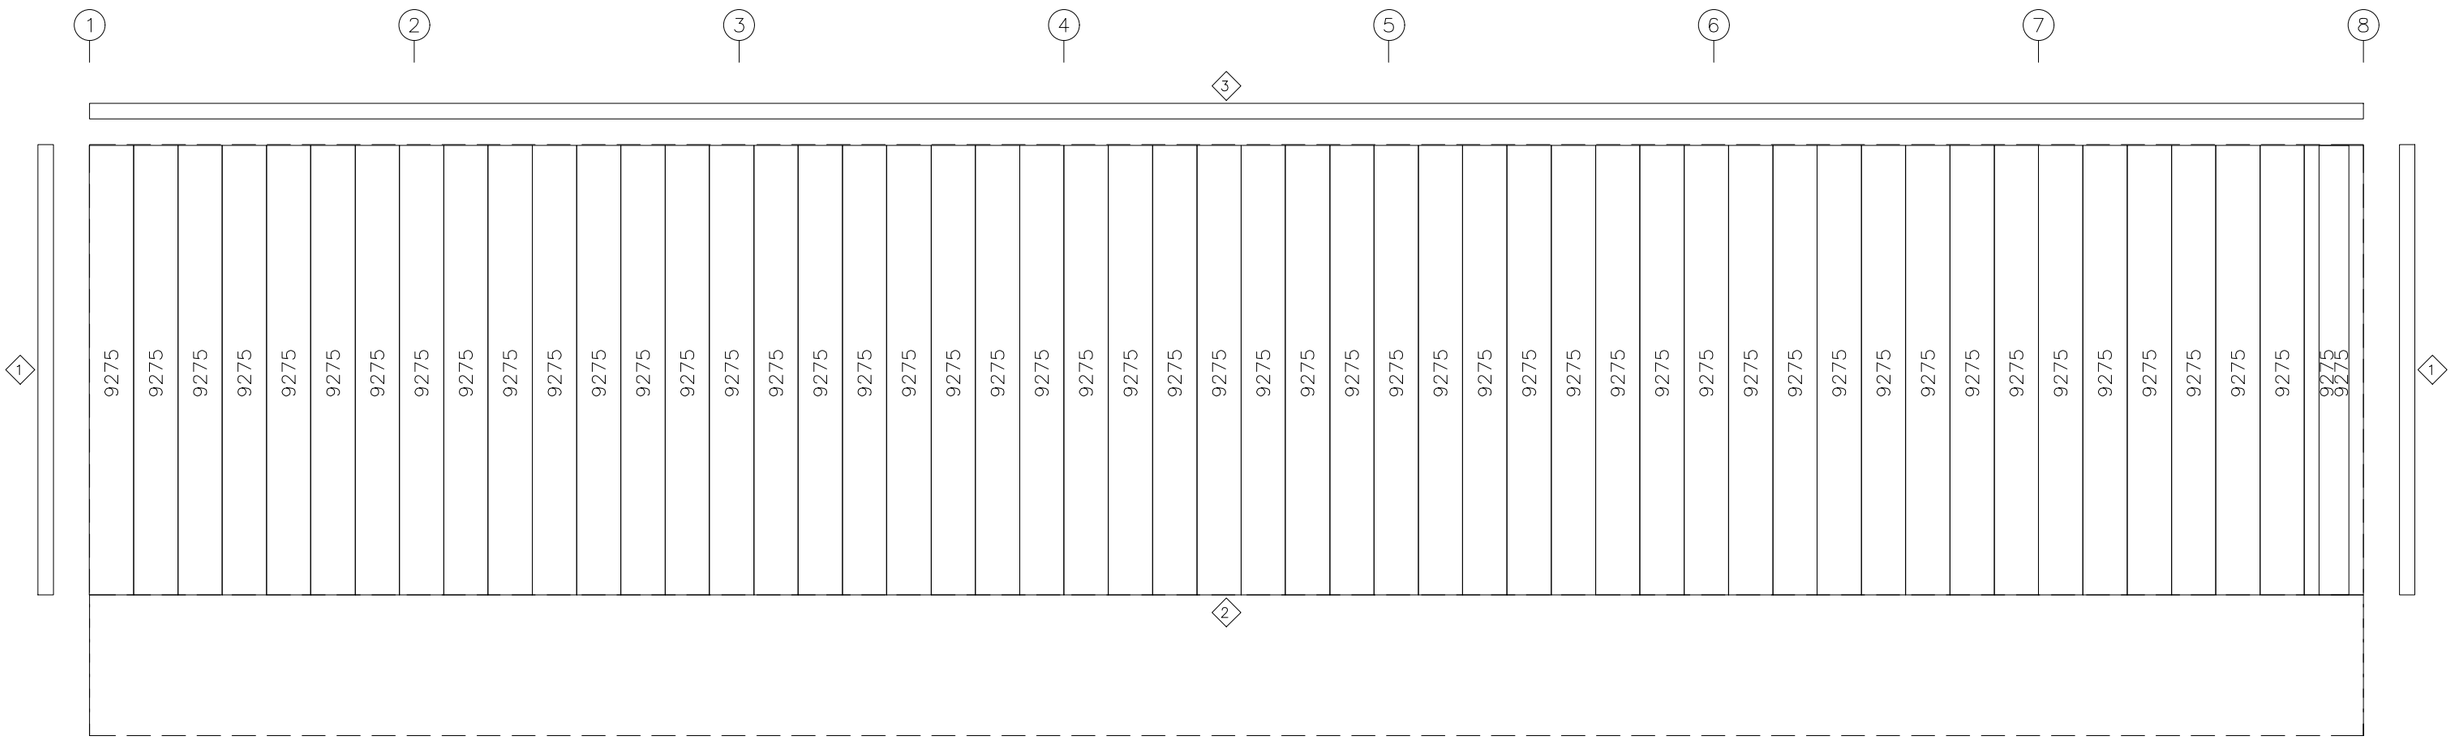


SIDEWALL SHEETING & TRIM: FRAME LINE A & G

PANELS: 0.50mm PR – Beige RAL1001

ARCHITECT ZUBAIR AHMED ZAFAR ALI	PROJECT MANAGER TANVEER AHMED	CLIENT _____
ADDRESS _____	No. / ISSUED / DATE 1. PROPOSED DRAWING	CONSULTANT : AHMED CONSTRUCTION COMPANY OFFICE NO.2,3RD FLOOR BIG CITY PLAZA, GULBERG-iii,Lahore 0322-8000190

PROJECT CONSTRUCTION OF PRE-ENGINEERED CEMENT PLANT - COAL SHED	DRAWN MUHMMAD SAEED	ACCO ARCHITECTURE & CONSTRUCTION	
DRAWING SIDEWALL SHEETING & TRIM	PLOTTED DATE 18-November-2025		
	SCALE SCALED TO FIT	DWG. NO. 06	

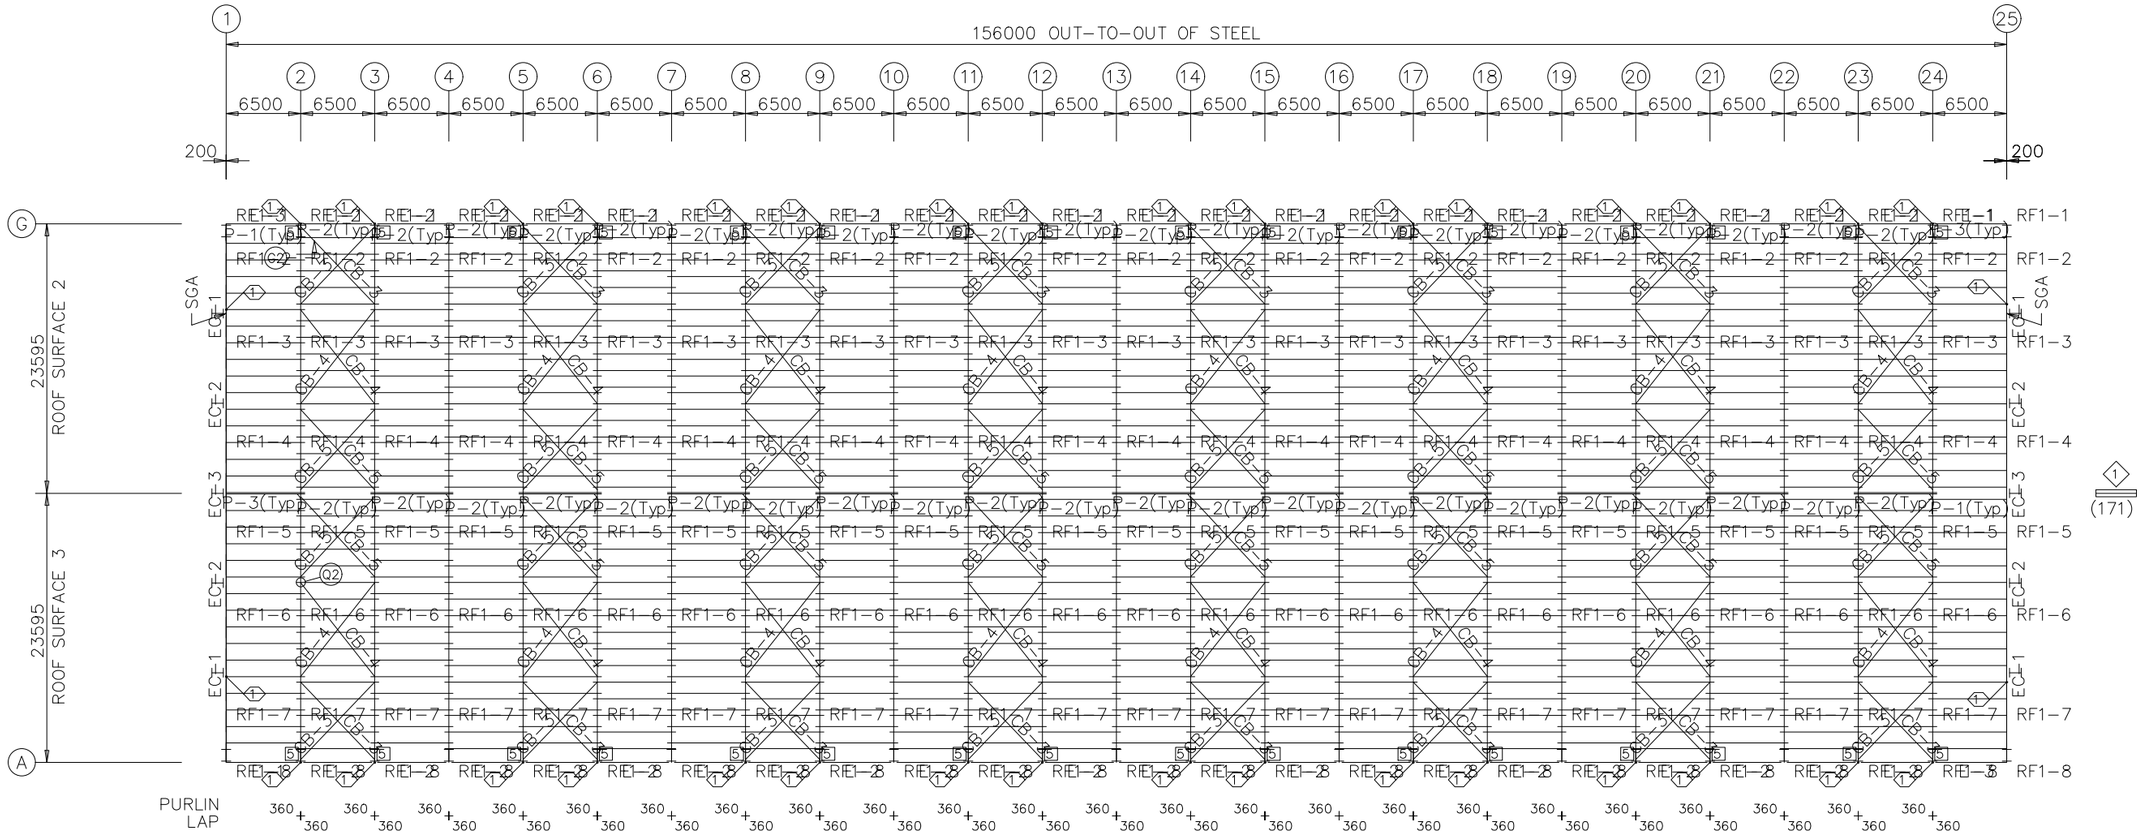

ROOF FRAMING PLAN


7505	(171)
8930	(171)
7515	(171)
7515	(171)
8930	(171)
7505	(171)

ROOF SHEETING

PANELS: 0.50mm PR Galvalume Plus

ARCHITECT: ZUBAIR AHMED, ZAFAR ALI	PROJECT MANAGER: TANVEER AHMED	CLIENT: _____
ADDRESS: ____	CONSULTANT : AHMED CONSTRUCTION COMPANY, OFFICE NO.2,3RD FLOOR BIG CITY PLAZA, GULBERG-iii,Lahore 0322-8000190	PROJECT: CONSTRUCTION OF PRE-ENGINEERED CEMENT PLANT - COAL SHED
DRAWN: MUHMMAD SAEED	PLOTTED DATE: 18-November-2025	SCALE: SCALED TO FIT
DRAWING: ROOF FRAMING PLAN	DWG. NO. 07	ACCO ARCHITECTURE & CONSTRUCTION

No.	ISSUED	DATE
1.	PROPOSED DRAWING	

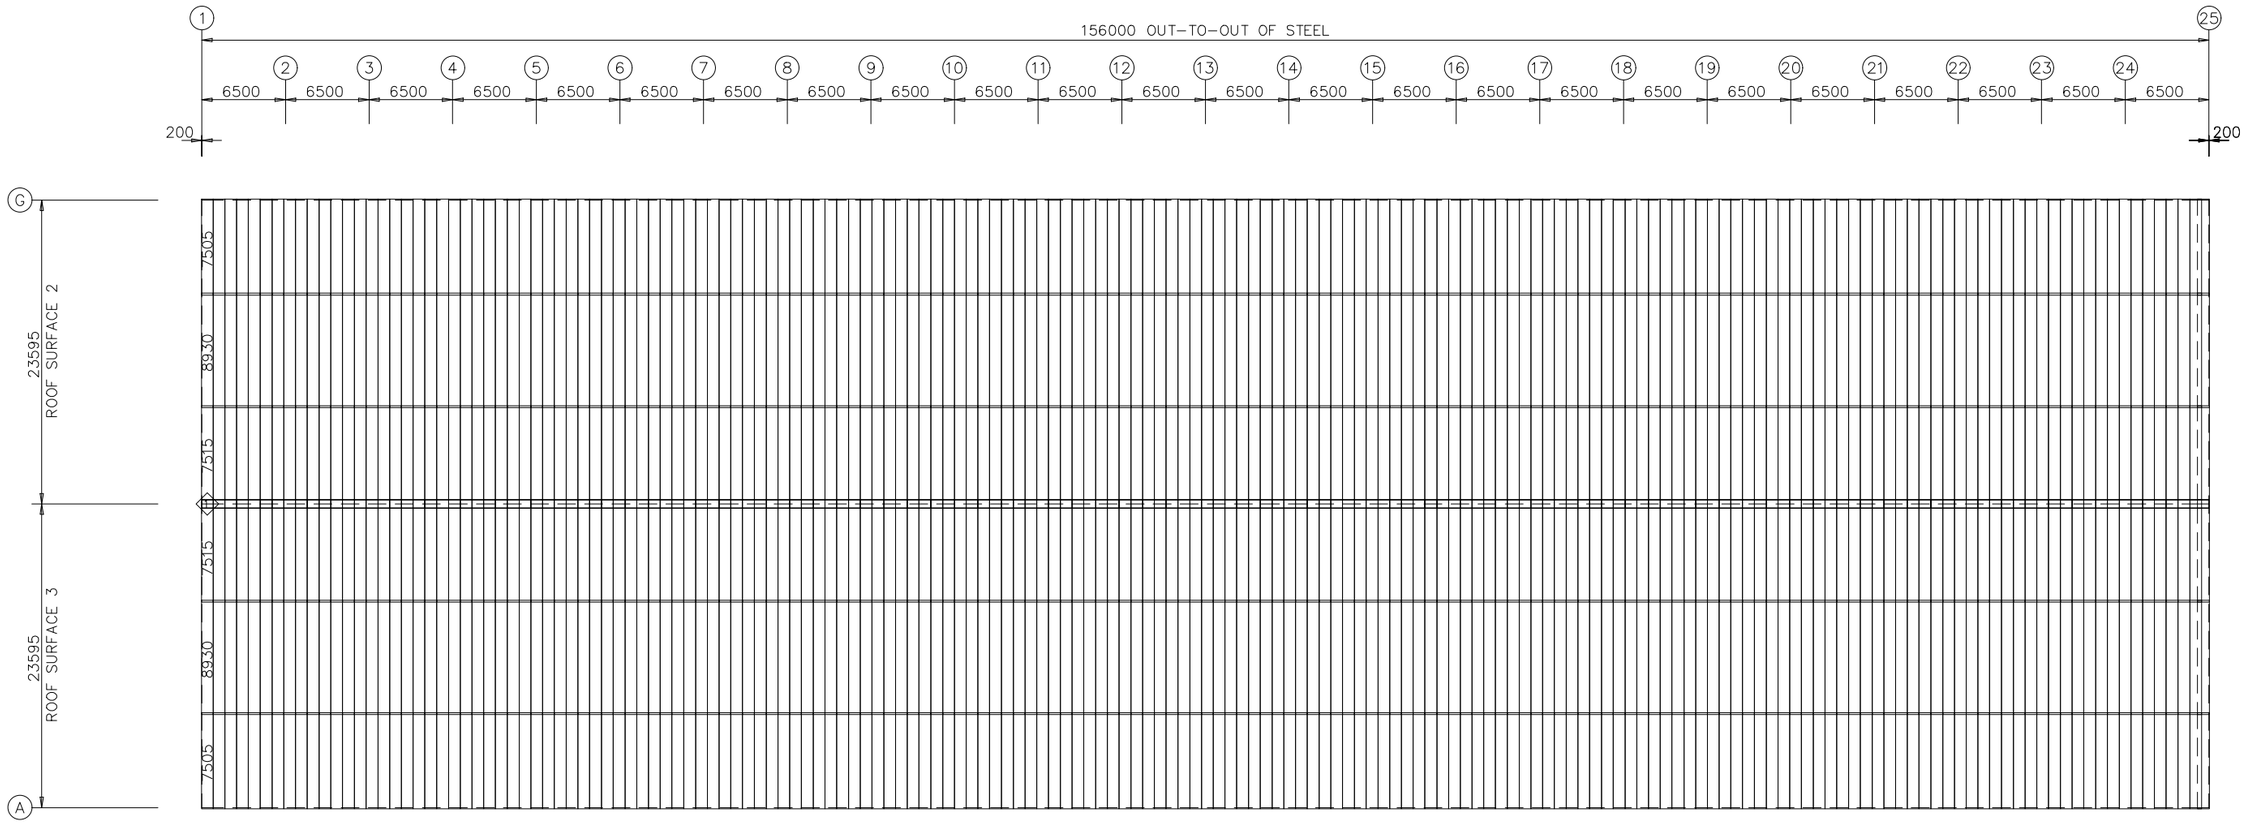

ROOF SHEETING PLAN

PANELS: 0.50mm PR – Galvalume Plus

ARCHITECT ZUBAIR AHMED ZAFAR ALI	PROJECT MANAGER TANVEER AHMED	CLIENT _____	PROJECT CONSTRUCTION OF PRE-ENGINEERED CEMENT PLANT - COAL SHED
ADDRESS _____	No. / ISSUED / DATE 1. PROPOSED DRAWING	CONSULTANT : AHMED CONSTRUCTION COMPANY OFFICE NO.2,3RD FLOOR BIG CITY PLAZA, GULBERG-iii,Lahore 0322-8000190	DRAWING ROOF SHEETING PLAN

DRAWN	MUHMMAD SAEED
PLOTTED DATE	18-November-2025
SCALE	SCALED TO FIT
DWG. NO.	08

ACCO
ARCHITECTURE & CONSTRUCTION

To,
Mr. Mohsin Baig Sahab
Manager Procurement, Gharibwal Cement Limited

Date: November 20, 2025
Ref#: ACCO/PEB/932

SUBJECT: - **QUOTATION FOR CONSTRUCTION OF LIMESTONE YARD PEB SHED BUILDING**

السلام علیکم
We are pleased to submit our best quote for subject work as follows: -

Sr.#	Item Description	Area (SFT)	Rate (Rs.)	Amount
1	Construction, supply and installation of a prefabricated steel shed for limestone yard peb shed extension work Complete in all respect. Height Approx. 46 feet 9 inches	56,511	1,831/-	103,528,152/-
	GST 18%			18,635,067.36/-
	Total Amount			**122,163,219.36/-**

Terms & Conditions:


1. This quotation excludes all taxes.
2. Complication Time 30 days
3. 50% Advance before starting the Project other balance Payment according to percentage of Work
4. Provision of storage facilities for our goods and equipment, where necessary, shall be client responsibility.
5. Electricity & water supply will be provided by the client.
6. This quotation is valid for 30 days from above mentioned date.
7. Civil Work is not included.

We will be obliged for your cooperation in this regard.
Thanks & Regards.
Truly yours,

Tanveer Ahmed
Director
+92-322-8000190

Product description

1. Building System

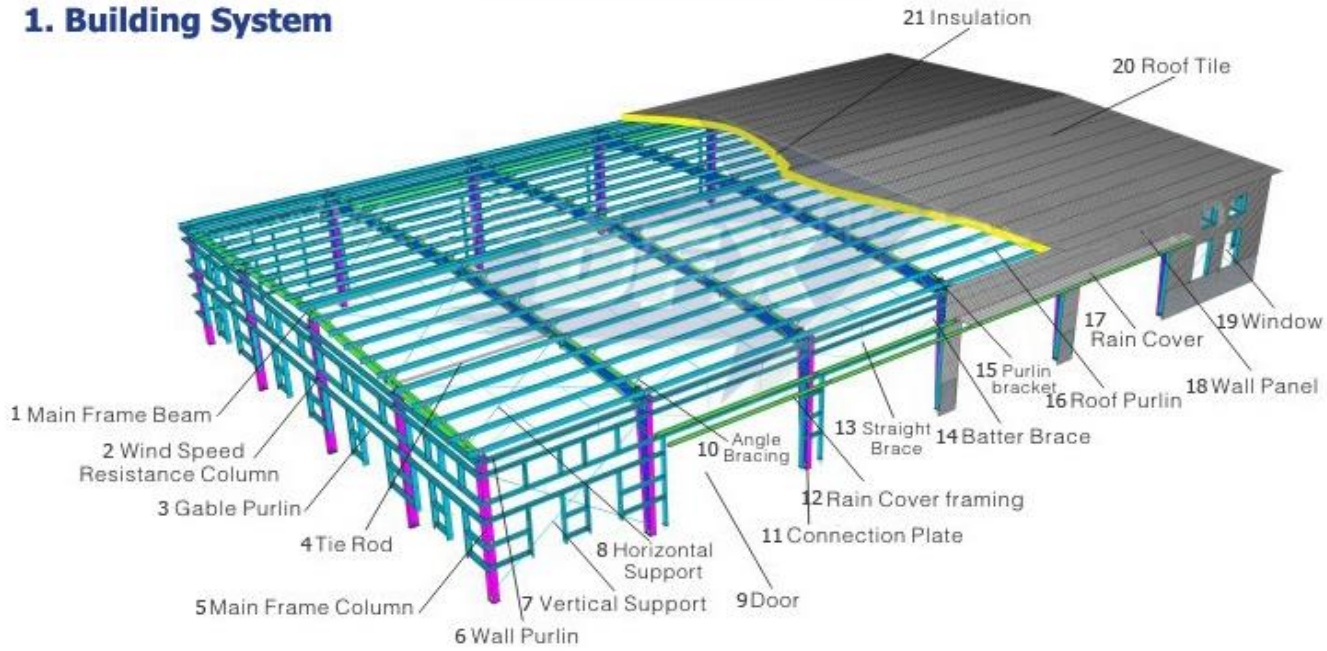

2. Specification

Items		Specification
Main Steel Frame	Column	5 mm and 6 mm
	Beam	5 mm and 6 mm
Secondary Frame	Purlin	1.5 mm
	Knee brace	12 mm
	Tie Rod	50 mm x 50 mm angle
	Brace	Sag Rod
	Vertical and Horizontal Support	Q235 Angle Steel, Round Bar or Steel Pipe
Maintenance system	Roof Panel	0.45 mm sheet PPGI (Pre-Painted Galvanized Iron)
	Wall Panel	0.45 mm sheet PPGI (Pre-Painted Galvanized Iron)
Accessories	Window	Nil
	Door	Nil
	Rainspout	MS Sheet
Live load on Roof		0.57 (kN/m2) (Color steel panel surrounded)
Live load on Frame		0.57 (kN/m2)

Wind Resistance (km/hr)	160 (Exposure C) / 140 km per hour
Seismic Zone	2-B
Structure Usage	Up to 50 years
Finishing Options	Vast array of colors and textures available
Paint Options	Alkyd painting, two primary painting, two finish painting (gray paint, red paint, white paint, epoxy zinc etc.) Or Galvanized.

3. Detailed Images




RELATED PRODUCTS



+92 322 8000 190 UAN: +923 111 749 849 info@acco.com.pk

Office 2nd, 3rd Floor, Bigcity Plaza, Gulberg-III, Lahore, Pakistan
www.acco.com.pk

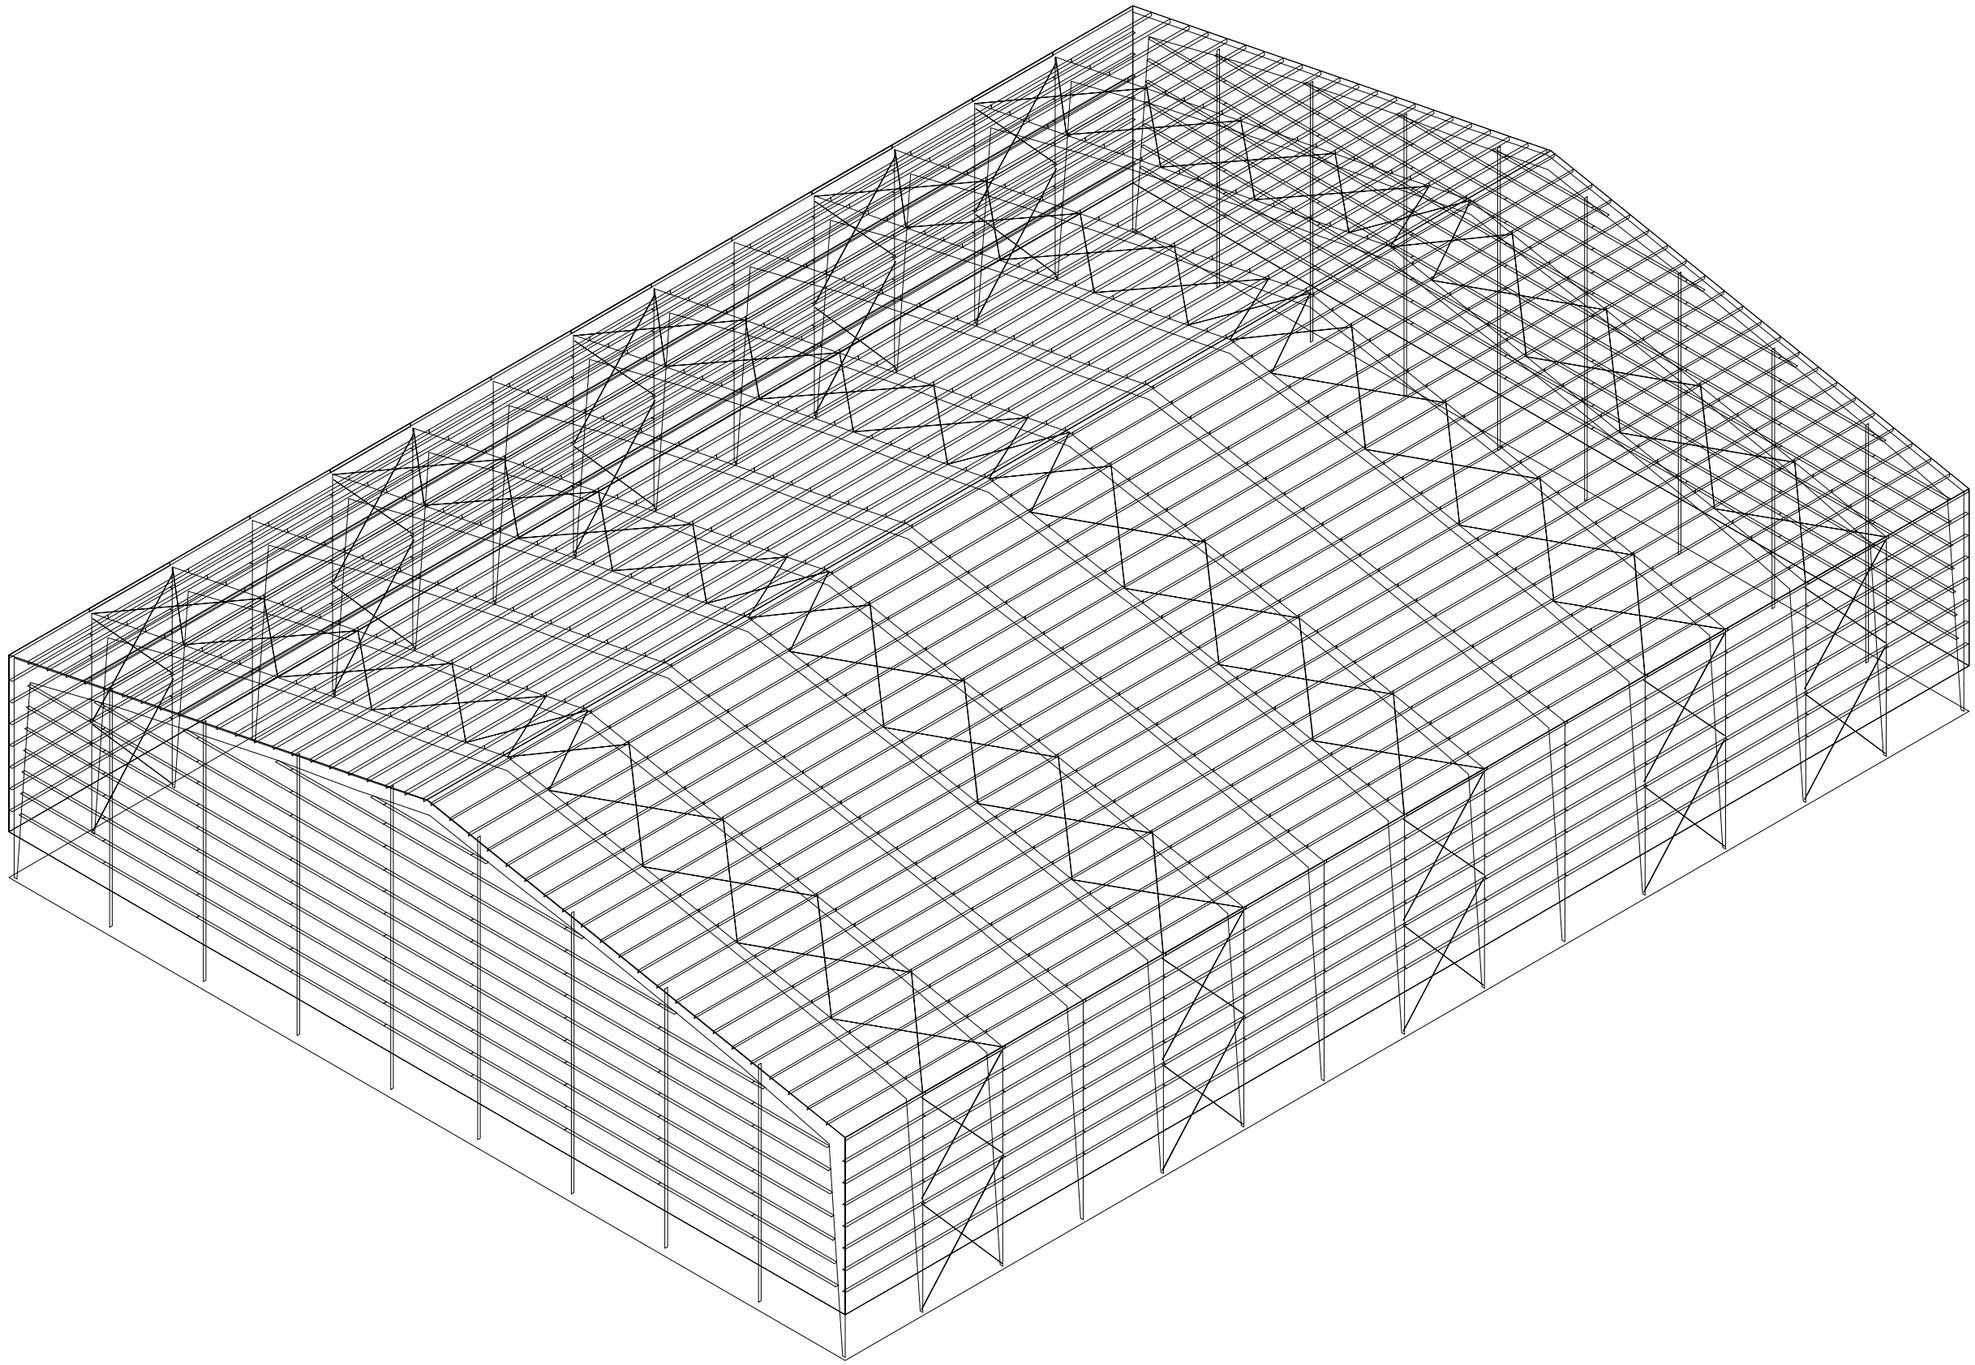

ARCHITECT

ZUBAIR AHMED
ZAFAR ALI

ADDRESS

———

PROJECT MANAGER

TANVEER AHMED

No.	ISSUED	DATE
1.	PROPOSED DRAWING	

CLIENT

_____

CONSULTANT :

AHMED CONSTRUCTION COMPANY

OFFICE NO.2,3RD FLOOR BIG CITY PLAZA,
GULBERG-iii,Lahore 0322-8000190

PROJECT

CONSTRUCTION OF PRE-ENGINEERED CEMENT PLANT
LIMESTONE YARD - 62.5 X 84

DRAWING

3D VIEW

DRAWN

MUHMMAD SAEED

PLOTTED DATE

18-November-2025

SCALE


SCALED TO FIT

ACCO

ARCHITECTURE & CONSTRUCTION

DWG. NO.

01

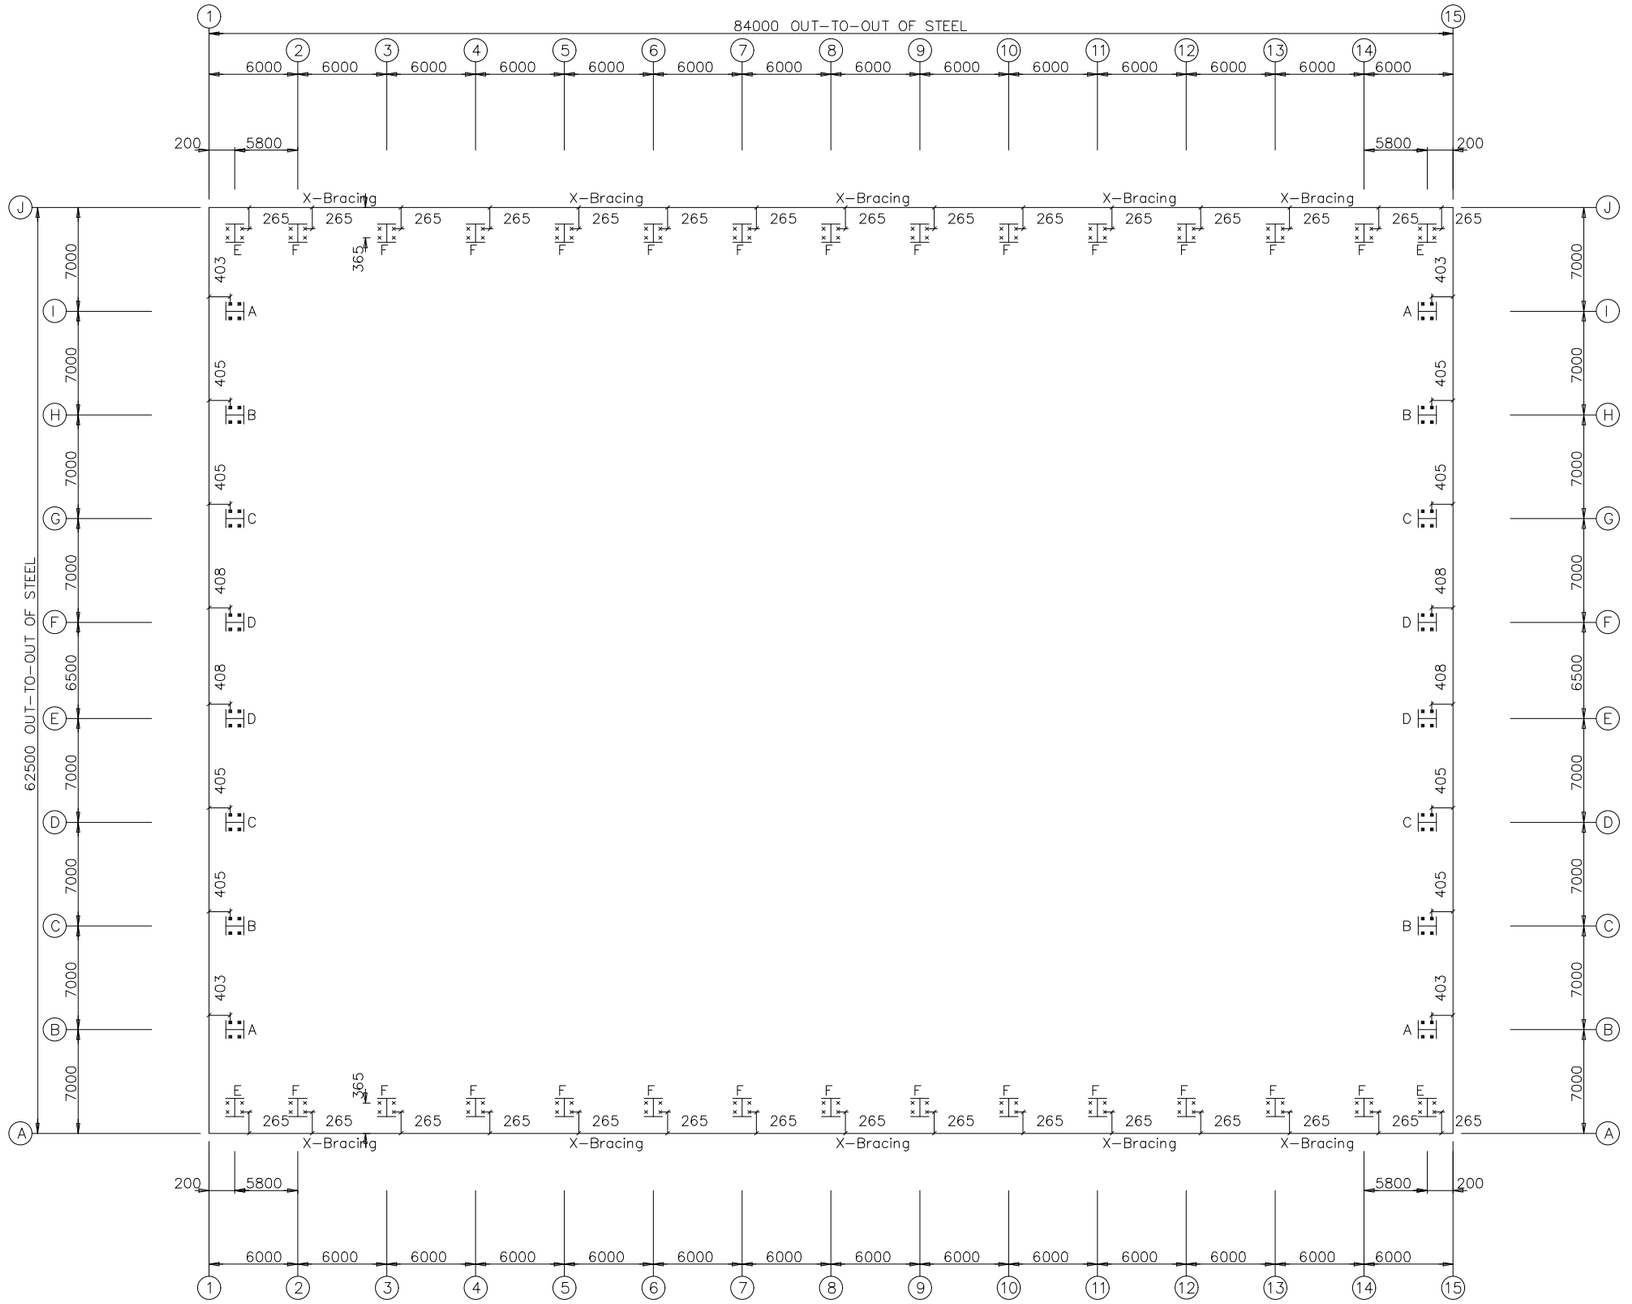


ANCHOR BOLT PLAN

NOTE: All Base Plates @ 0 (U.N.)

ARCHITECT ZUBAIR AHMED ZAFAR ALI	PROJECT MANAGER TANVEER AHMED	CLIENT _____	PROJECT CONSTRUCTION OF PRE-ENGINEERED CEMENT PLANT LIMESTONE YARD - 62.5 X 84	DRAWN MUHMMAD SAEED
ADDRESS _____	No. / ISSUED / DATE 1. PROPOSED DRAWING	CONSULTANT : AHMED CONSTRUCTION COMPANY OFFICE NO.2,3RD FLOOR BIG CITY PLAZA, GULBERG-iii,Lahore 0322-8000190	DRAWING ANCHOR BOLT PLAN	PLOTTED DATE 18-November-2025 SCALE SCALED TO FIT

ACCO
ARCHITECTURE & CONSTRUCTION

DWG. NO. 02

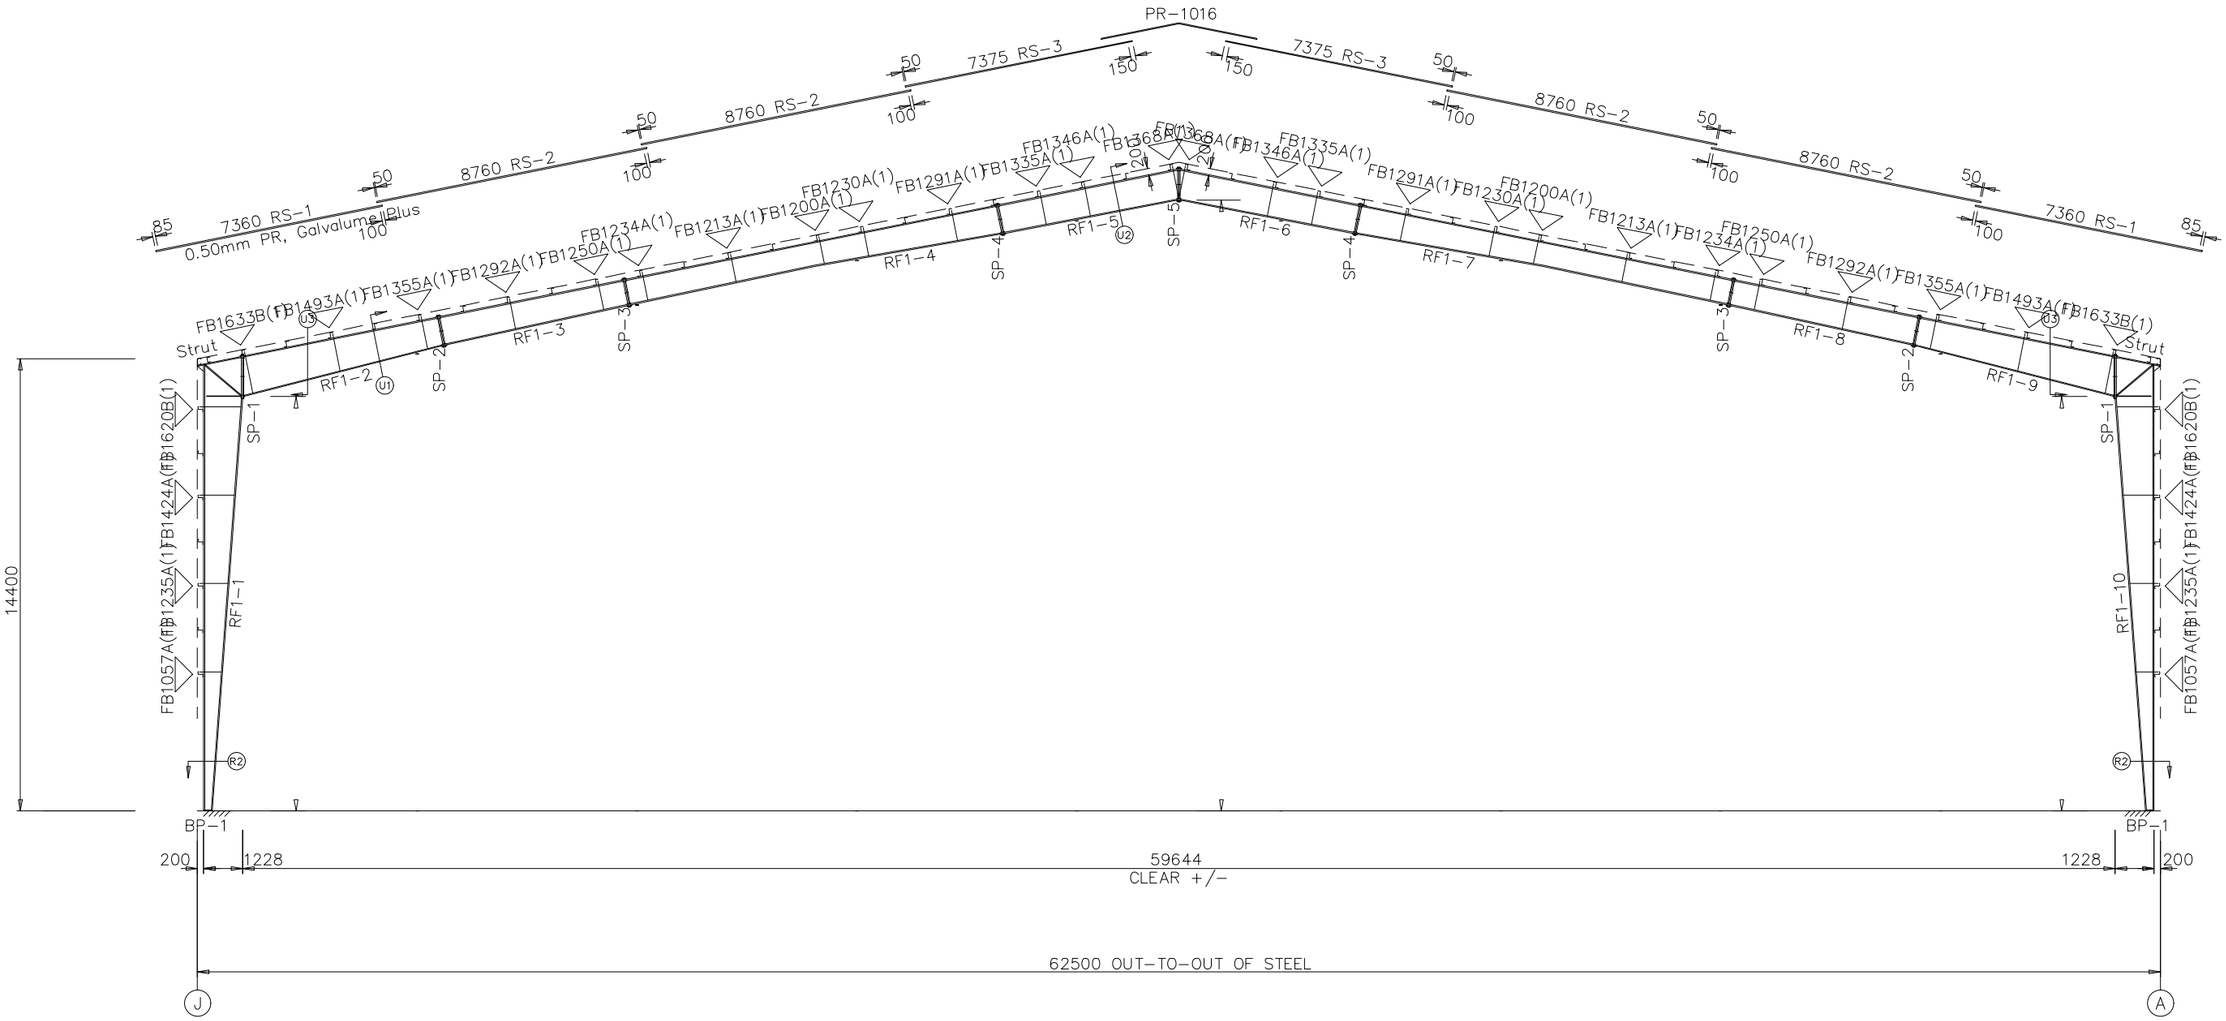


RIGID FRAME ELEVATION: FRAME LINE 1 2 3 4 5 6 7 8 9 10 11 12 13 14 15

ARCHITECT ZUBAIR AHMED ZAFAR ALI	PROJECT MANAGER TANVEER AHMED	CLIENT _____	PROJECT CONSTRUCTION OF PRE-ENGINEERED CEMENT PLANT LIMESTONE YARD - 62.5 X 84
ADDRESS _____	No. / ISSUED / DATE 1. PROPOSED DRAWING	CONSULTANT : AHMED CONSTRUCTION COMPANY OFFICE NO.2,3RD FLOOR BIG CITY PLAZA, GULBERG-iii,Lahore 0322-8000190	DRAWING RIGID FRAME ELEVATION

DRAWN	MUHMMAD SAEED
PLOTTED DATE	18-November-2025
SCALE	SCALED TO FIT
DWG. NO.	03


ACCO
ARCHITECTURE & CONSTRUCTION

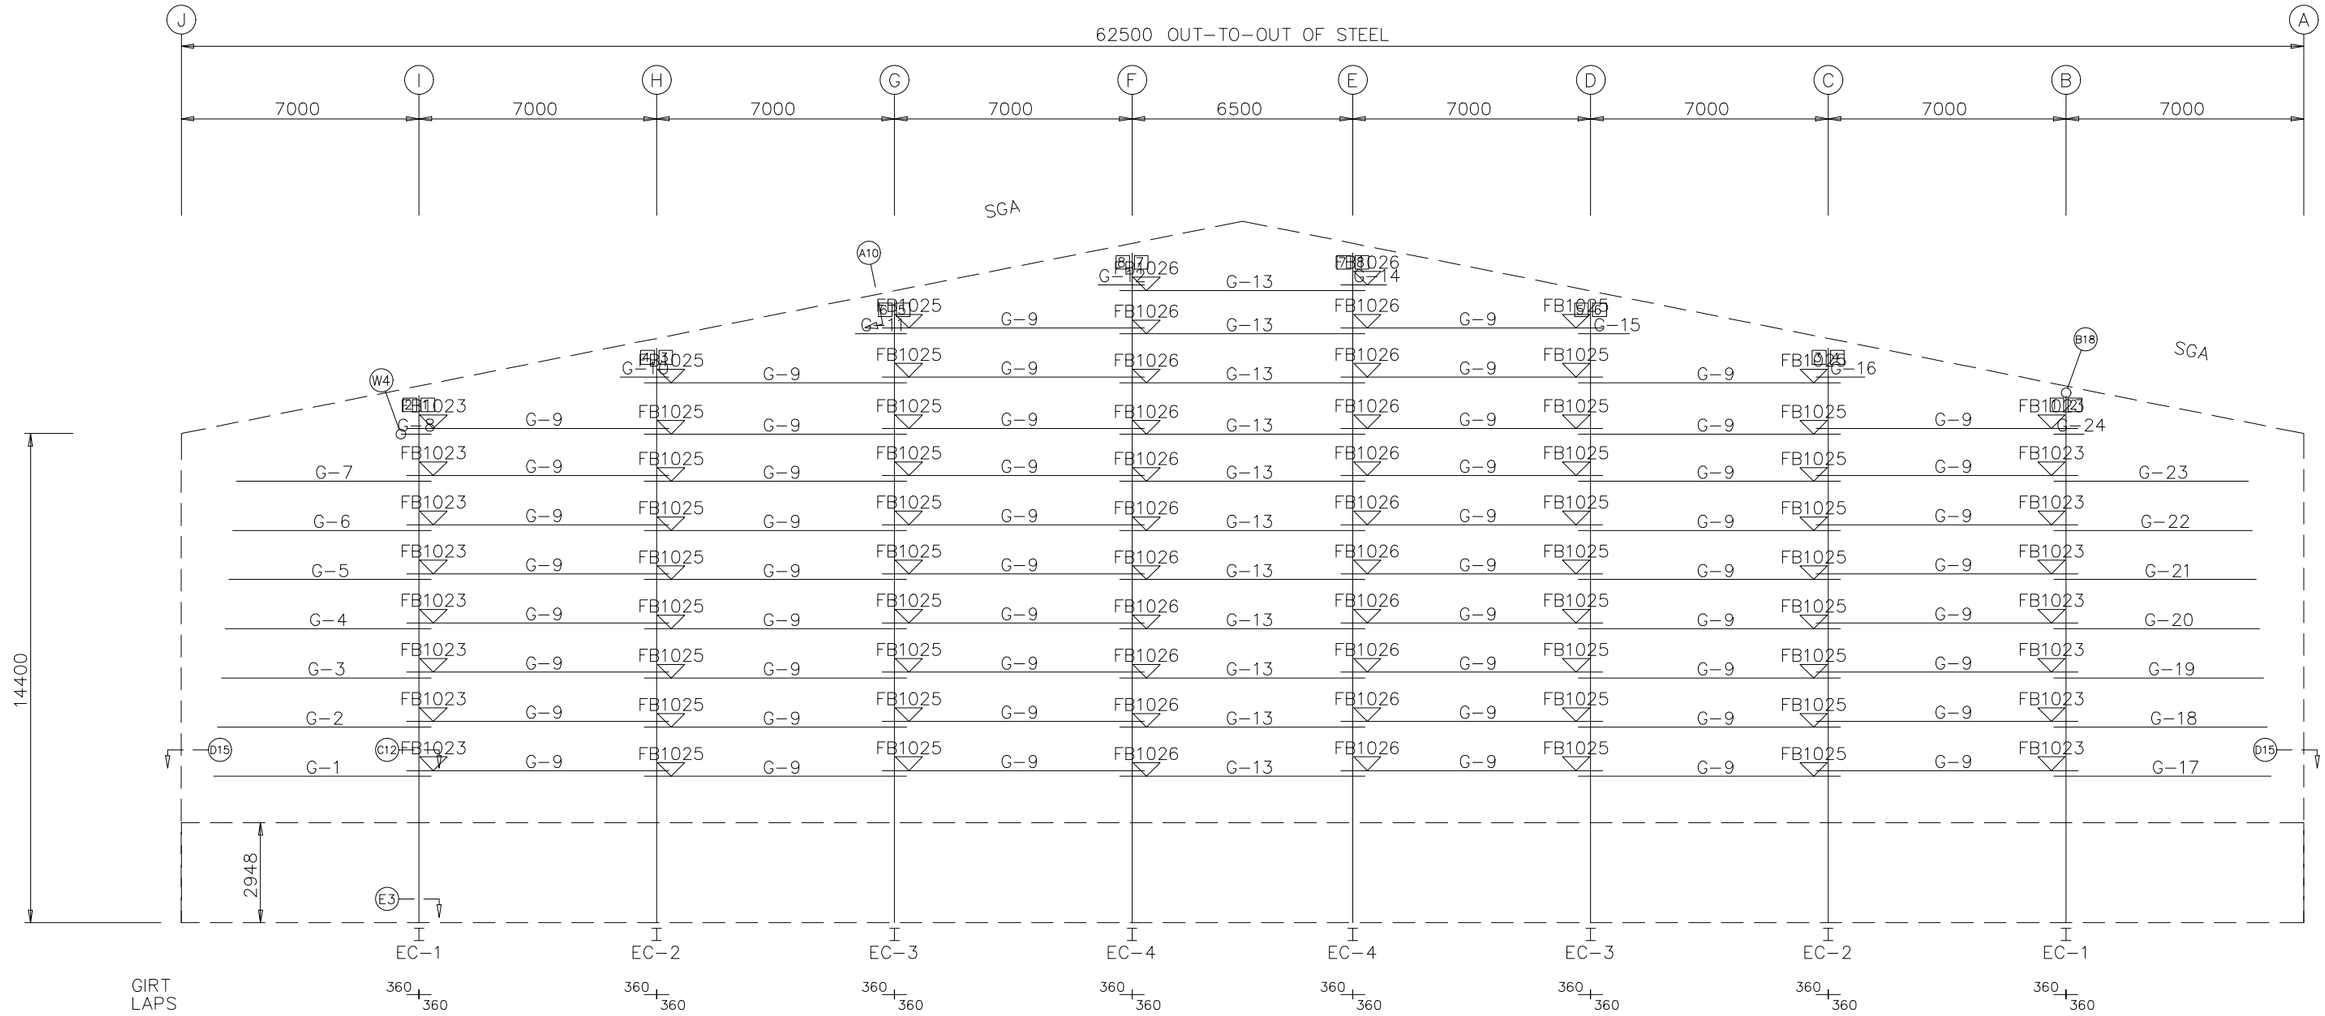

ENDWALL FRAMING: FRAME LINE 1 & 15

ARCHITECT ZUBAIR AHMED ZAFAR ALI	PROJECT MANAGER TANVEER AHMED	CLIENT _____	PROJECT CONSTRUCTION OF PRE-ENGINEERED CEMENT PLANT LIMESTONE YARD - 62.5 X 84
ADDRESS _____	No. / ISSUED / DATE 1. PROPOSED DRAWING	CONSULTANT : AHMED CONSTRUCTION COMPANY OFFICE NO.2,3RD FLOOR BIG CITY PLAZA, GULBERG-iii,Lahore 0322-8000190	DRAWING END WALL FRAMING

DRAWN MUHMMAD SAEED	ACCO ARCHITECTURE & CONSTRUCTION
PLOTTED DATE 18-November-2025	
SCALE SCALED TO FIT	DWG. NO. 04

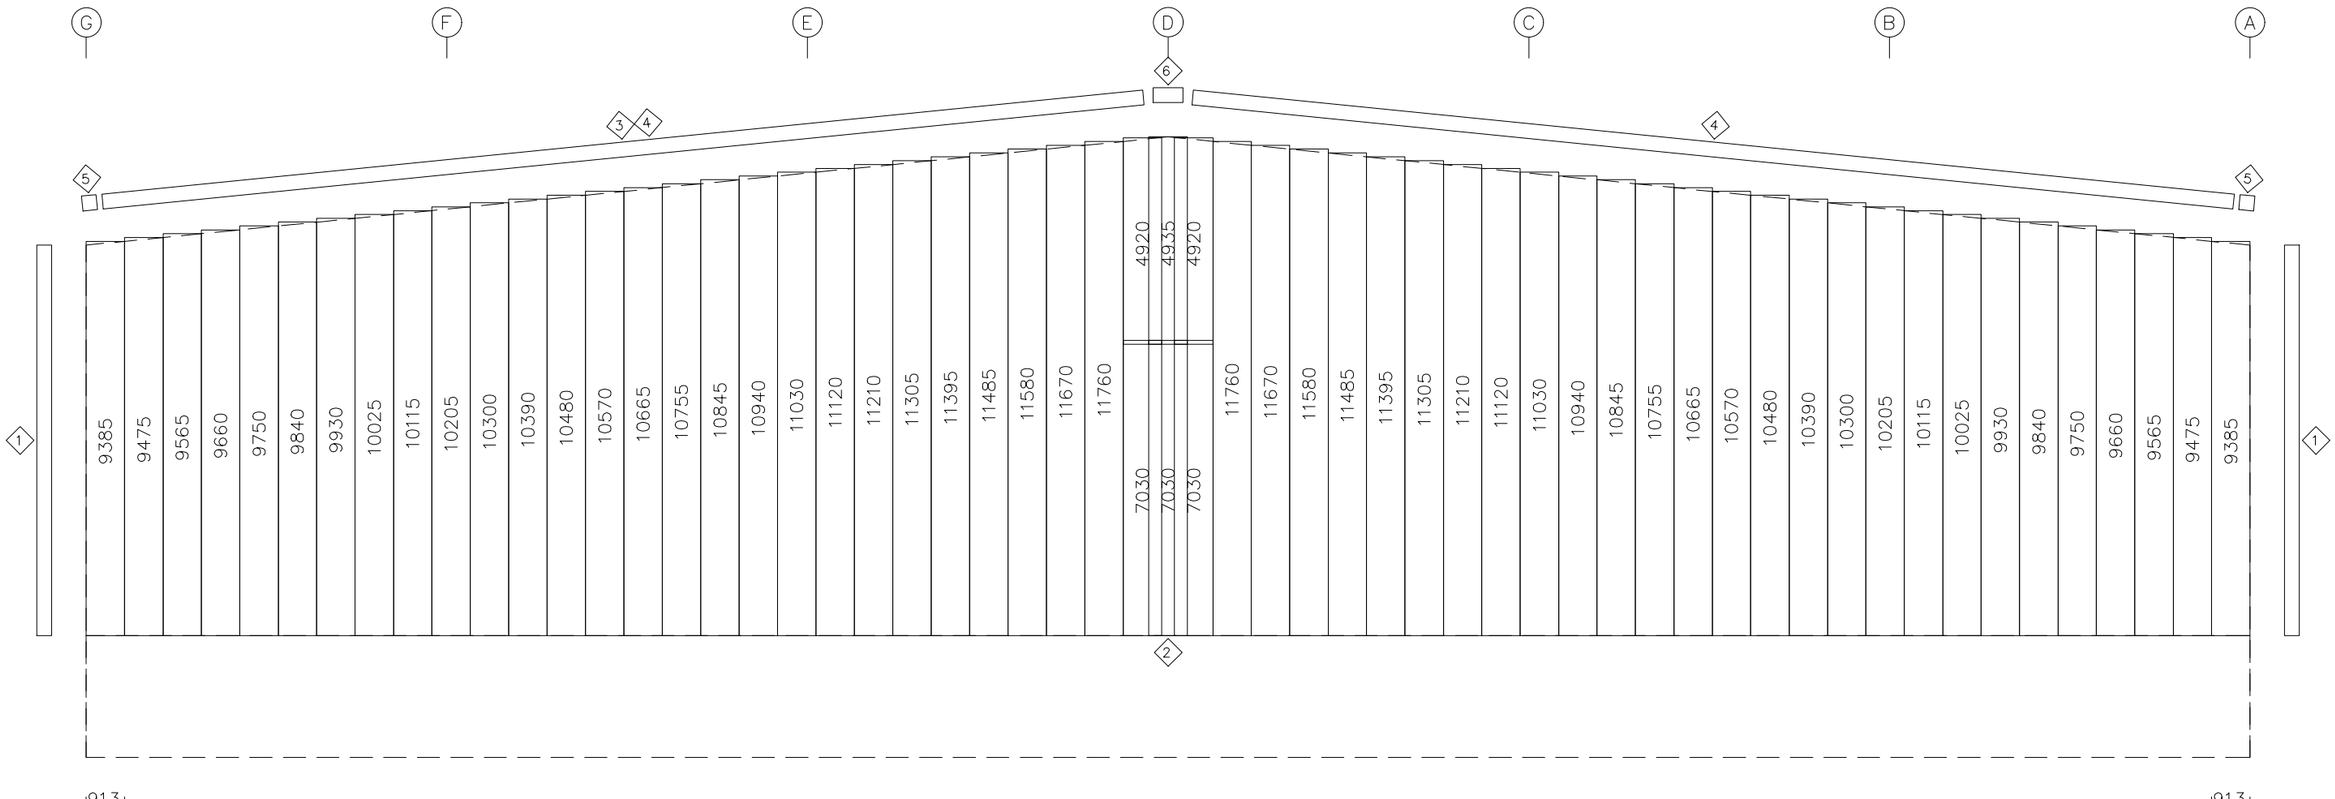

ENDWALL SHEETING & TRIM: FRAME LINE 1

PANELS: 0.50mm PR – Beige RAL1001

ARCHITECT: ZUBAIR AHMED, ZAFAR ALI	PROJECT MANAGER: TANVEER AHMED	CLIENT: _____	PROJECT: CONSTRUCTION OF PRE-ENGINEERED CEMENT PLANT, LIMESTONE YARD - 62.5 X 84
ADDRESS: ____	CONSULTANT : AHMED CONSTRUCTION COMPANY, OFFICE NO.2,3RD FLOOR BIG CITY PLAZA, GULBERG-iii,Lahore 0322-8000190		DRAWING: ENDWALL SHEETING & TRIM

No.	ISSUED	DATE
1.	PROPOSED DRAWING	


DRAWN: MUHMMAD SAEED

PLOTTED DATE: 18-November-2025

SCALE: SCALED TO FIT


ACCO
ARCHITECTURE & CONSTRUCTION

DWG. NO. 05

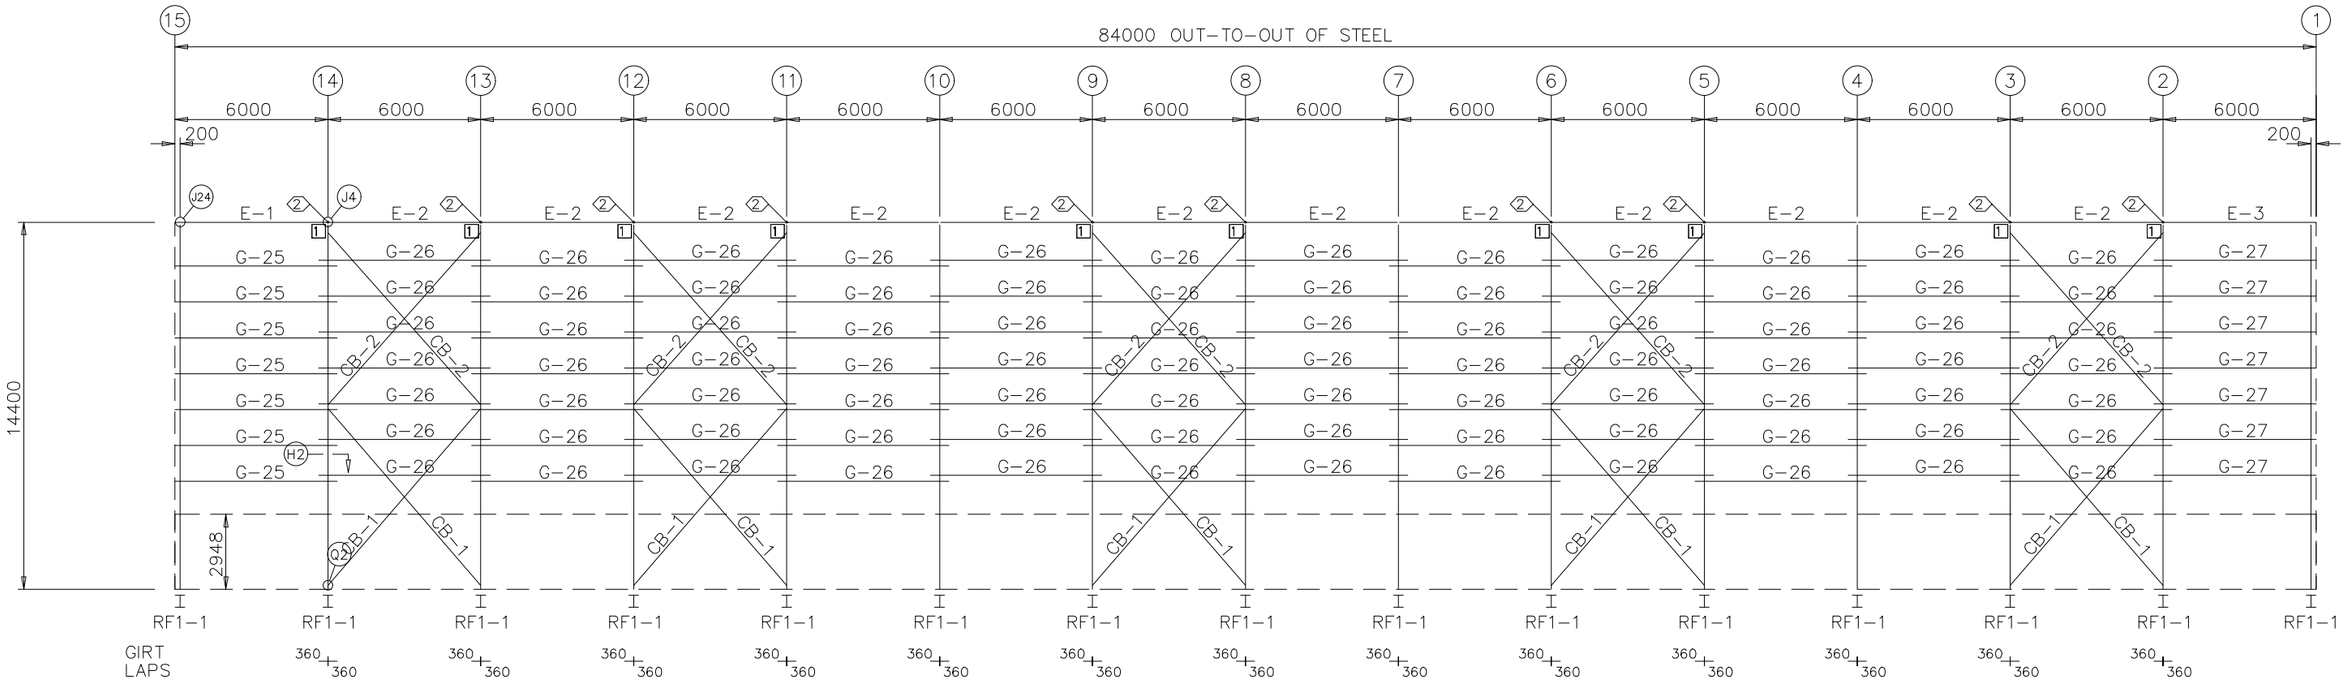

SIDEWALL FRAMING: FRAME LINE A & J

ARCHITECT ZUBAIR AHMED ZAFAR ALI	PROJECT MANAGER TANVEER AHMED	CLIENT _____	PROJECT CONSTRUCTION OF PRE-ENGINEERED CEMENT PLANT LIMESTONE YARD - 62.5 X 84	DRAWN MUHMMAD SAEED	ACCO ARCHITECTURE & CONSTRUCTION
ADDRESS _____	No. / ISSUED / DATE 1. PROPOSED DRAWING	CONSULTANT : AHMED CONSTRUCTION COMPANY OFFICE NO.2,3RD FLOOR BIG CITY PLAZA, GULBERG-iii,Lahore 0322-8000190	DRAWING SIDEWALL FRAMING	PLOTTED DATE 18-November-2025 SCALE SCALED TO FIT	DWG. NO. 06

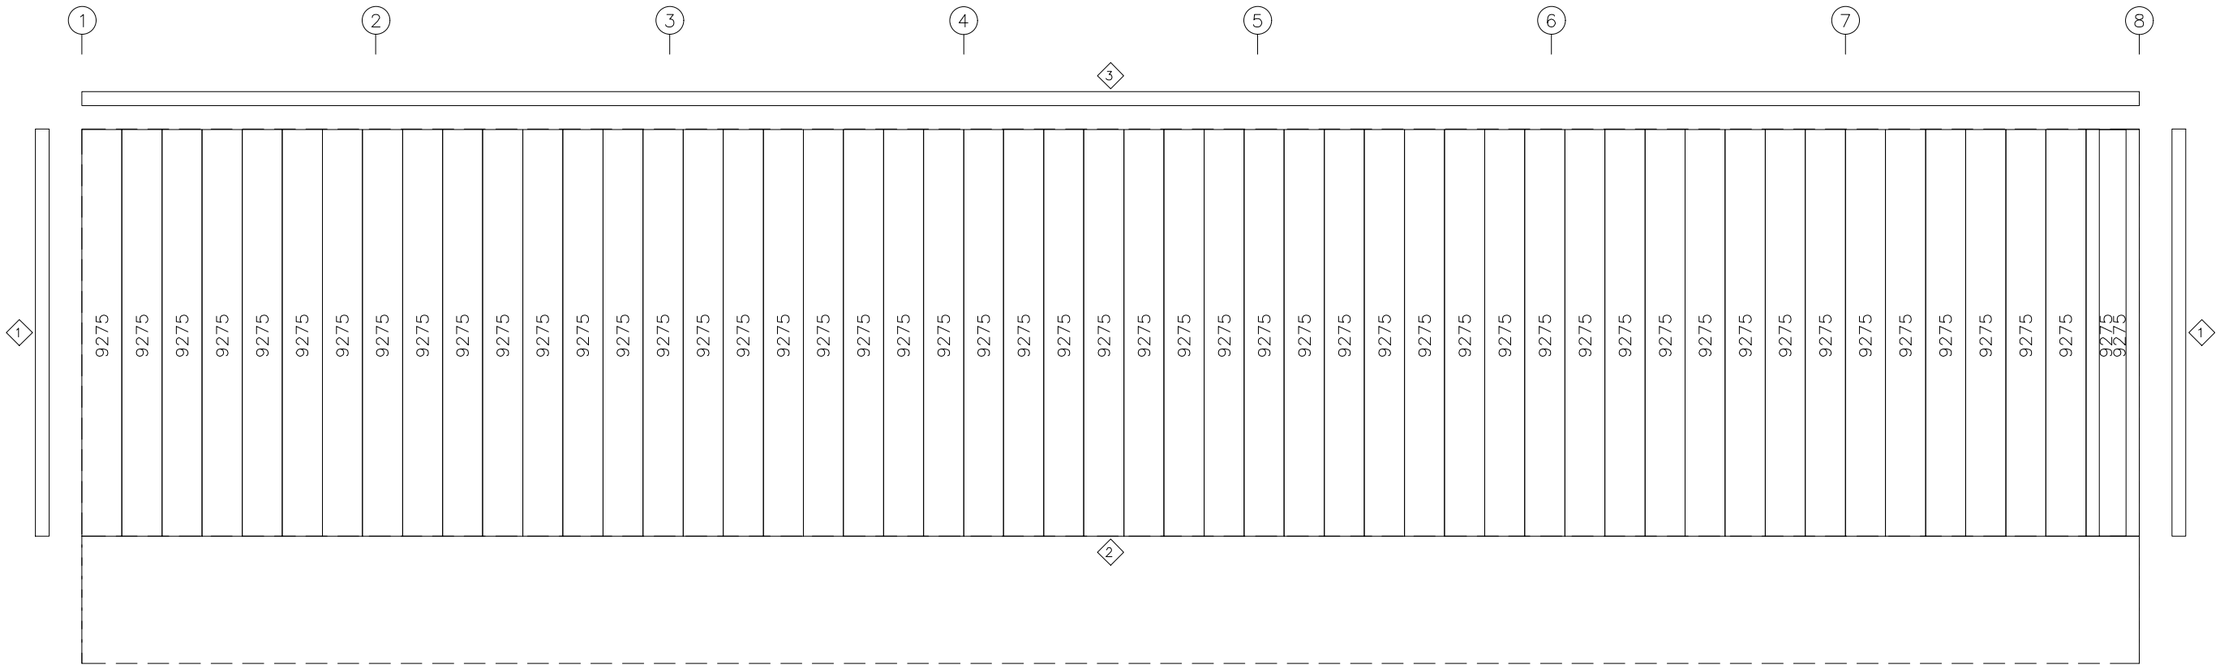


SIDEWALL SHEETING & TRIM: FRAME LINE A

PANELS: 0.50mm PR – Beige RAL1001

ARCHITECT ZUBAIR AHMED ZAFAR ALI	PROJECT MANAGER TANVEER AHMED	CLIENT _____	PROJECT CONSTRUCTION OF PRE-ENGINEERED CEMENT PLANT LIMESTONE YARD - 62.5 X 84	DRAWN MUHMMAD SAEED
ADDRESS _____	No. / ISSUED / DATE 1. PROPOSED DRAWING	CONSULTANT : AHMED CONSTRUCTION COMPANY OFFICE NO.2,3RD FLOOR BIG CITY PLAZA, GULBERG-iii,Lahore 0322-8000190	DRAWING SIDEWALL SHEETING & TRIM	PLOTTED DATE 18-November-2025 SCALE SCALED TO FIT

ACCO
ARCHITECTURE & CONSTRUCTION

DWG. NO. 07

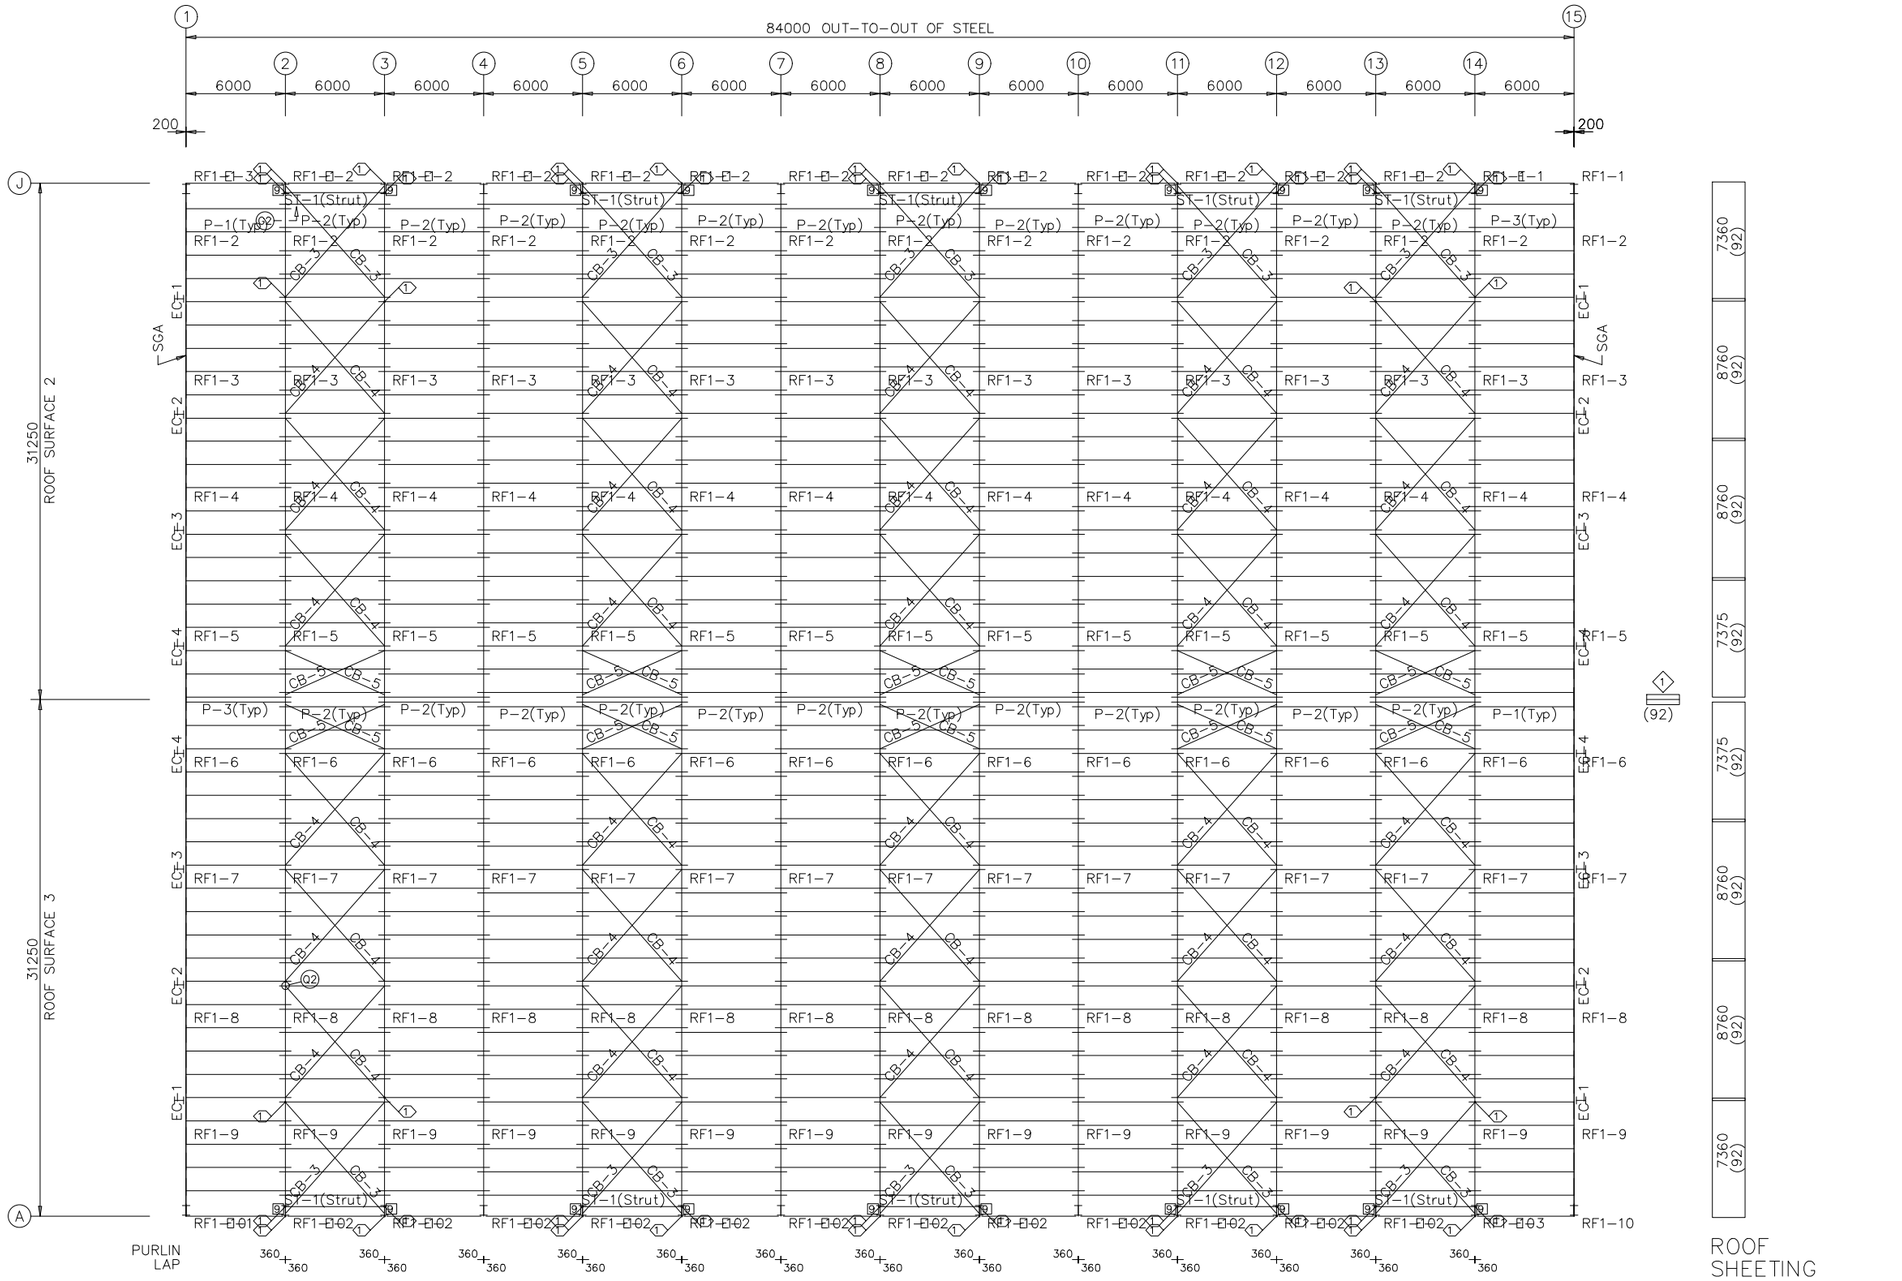

ROOF FRAMING PLAN


ROOF SHEETING

PANELS: 0.50mm PR Galvalume Plus

ARCHITECT: ZUBAIR AHMED, ZAFAR ALI	PROJECT MANAGER: TANVEER AHMED	CLIENT: _____	PROJECT: CONSTRUCTION OF PRE-ENGINEERED CEMENT PLANT, LIMESTONE YARD - 62.5 X 84
ADDRESS: ____	No. / ISSUED / DATE: 1. PROPOSED DRAWING	CONSULTANT : AHMED CONSTRUCTION COMPANY, OFFICE NO.2,3RD FLOOR BIG CITY PLAZA, GULBERG-iii,Lahore 0322-8000190	DRAWING: ROOF FRAMING PLAN

DRAWN	MUHMMAD SAEED
PLOTTED DATE	18-November-2025
SCALE	SCALED TO FIT
DWG. NO.	08

ACCO
ARCHITECTURE & CONSTRUCTION

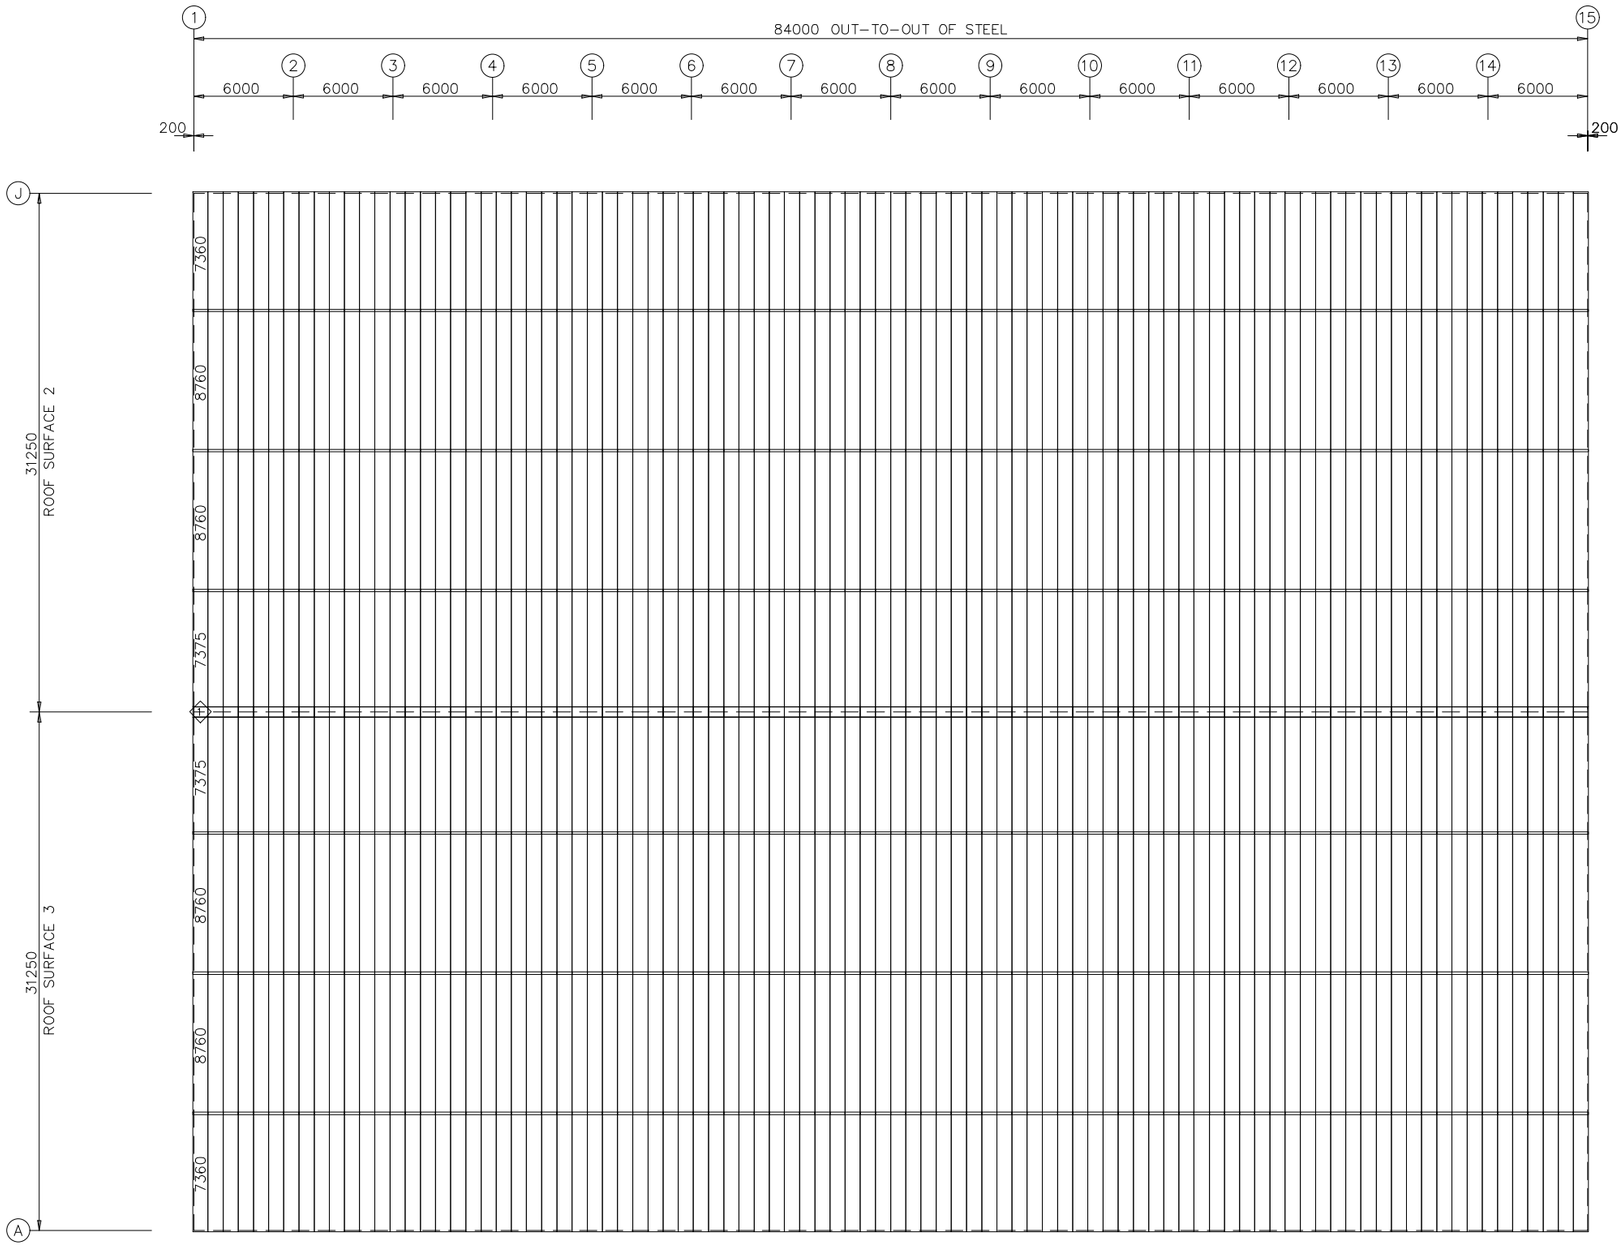

ROOF SHEETING PLAN

PANELS: 0.50mm PR – Galvalume Plus

ARCHITECT ZUBAIR AHMED ZAFAR ALI	PROJECT MANAGER TANVEER AHMED	CLIENT _____	PROJECT CONSTRUCTION OF PRE-ENGINEERED CEMENT PLANT LIMESTONE YARD - 62.5 X 84
ADDRESS ____	No. / ISSUED / DATE 1. PROPOSED DRAWING	CONSULTANT : AHMED CONSTRUCTION COMPANY OFFICE NO.2,3RD FLOOR BIG CITY PLAZA, GULBERG-iii,Lahore 0322-8000190	DRAWING ROOF SHEETING PLAN

DRAWN	MUHMMAD SAEED
PLOTTED DATE	18-November-2025
SCALE	SCALED TO FIT
DWG. NO.	09

ACCO
ARCHITECTURE & CONSTRUCTION
