To,
Mr. Abbas Mujahid Sahab
Quaid e Azam Industrial Area, Lahore Punjab

Date: November 27, 2025
Ref#: ACCO/PEB/1009

SUBJECT: - **QUOTATION FOR CONSTRUCTION OF PRE-ENGINEERED BUILDING FOR ADSELLS**

السلام علیکم
We are pleased to submit our best quote for subject work as follows: -

Sr.#	Item Description	Area (SFT)	Rate (Rs.)	Amount
1	Construction, supply and installation of a prefabricated steel shed floor for production unit Complete in all respect. Area: 80x49 feet Height Approx. 14 feet	3,920	1,596 /-	6,256,320/-
	Total Amount without Taxes			**6,256,320/-**
	GST 18%			**1,126,137.6/-**
	Total Amount with Taxes			**7,382,457.6/-**

Terms & Conditions:


1. This quotation excludes all taxes.
2. Complication Time 30 days
3. 50% Advance before starting the Project other balance Payment according to percentage of Work
4. Provision of storage facilities for our goods and equipment, where necessary, shall be client responsibility.
5. Electricity & water supply will be provided by the client.
6. This quotation is valid for 30 days from above mentioned date.
7. Civil Work is not included.

We will be obliged for your cooperation in this regard.
Thanks & Regards.
Truly yours,

Tanveer Ahmed
Director
+92-322-8000190

Product description

1. Building System

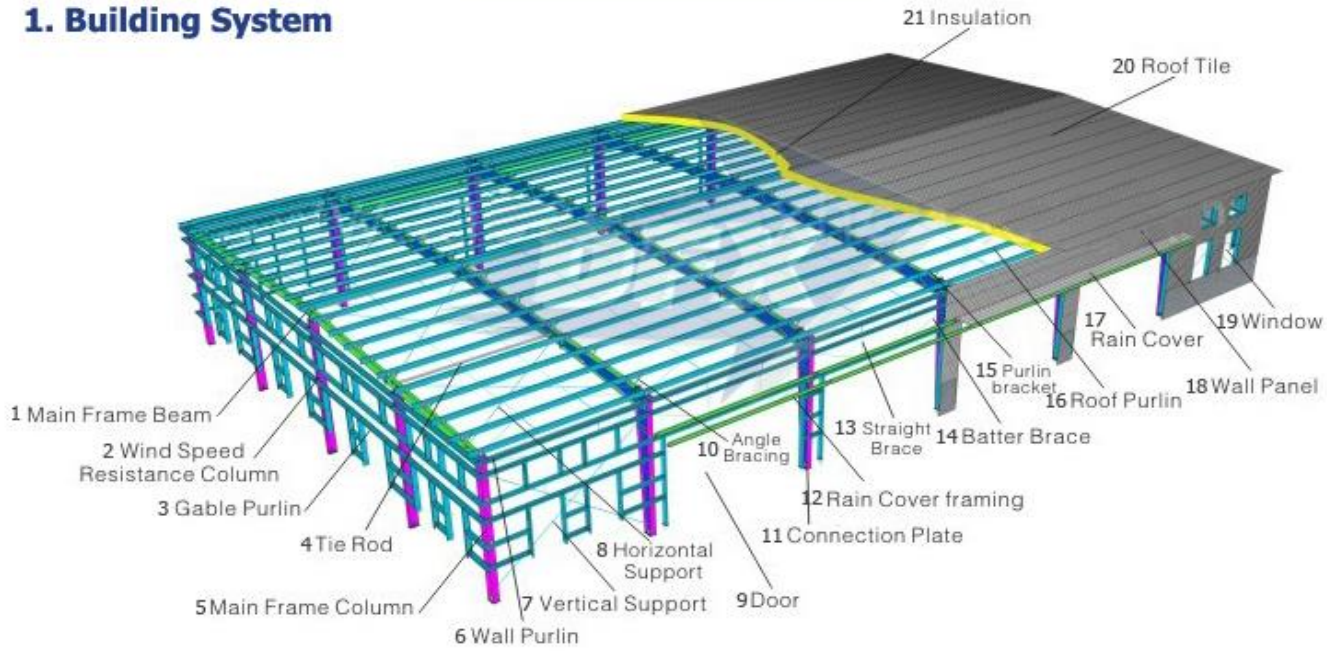

2. Specification

Items		Specification
Main Steel Frame	Column	5 mm and 6 mm
	Beam	5 mm and 6 mm
Secondary Frame	Purlin	1.5 mm
	Knee brace	12 mm
	Tie Rod	50 mm x 50 mm angle
	Brace	Sag Rod
	Vertical and Horizontal Support	Q235 Angle Steel, Round Bar or Steel Pipe
Maintenance system	Roof Panel	0.45 mm sheet PPGI (Pre-Painted Galvanized Iron) – 50 mm Glass Wool
	Wall Panel	0.45 mm sheet PPGI (Pre-Painted Galvanized Iron) – 50 mm Glass Wool
Accessories	Window	Nil
	Door	Nil
	Rainspout	MS Sheet
Live load on Roof		0.57 (kN/m2) (Color steel panel surrounded)

Live load on Frame	0.57 (kN/m2)
Wind Resistance (km/hr)	160 (Exposure C) / 140 km per hour
Seismic Zone	2-B
Structure Usage	Up to 50 years
Finishing Options	Vast array of colors and textures available
Paint Options	Alkyd painting, two primary painting, two finish painting (gray paint, red paint, white paint, epoxy zinc etc.) Or Galvanized.

3. Detailed Images




RELATED PRODUCTS




+92 322 8000 190 UAN: +923 111 749 849 info@acco.com.pk

Office 2nd, 3rd Floor, Bigcity Plaza, Gulberg-III, Lahore, Pakistan
www.acco.com.pk

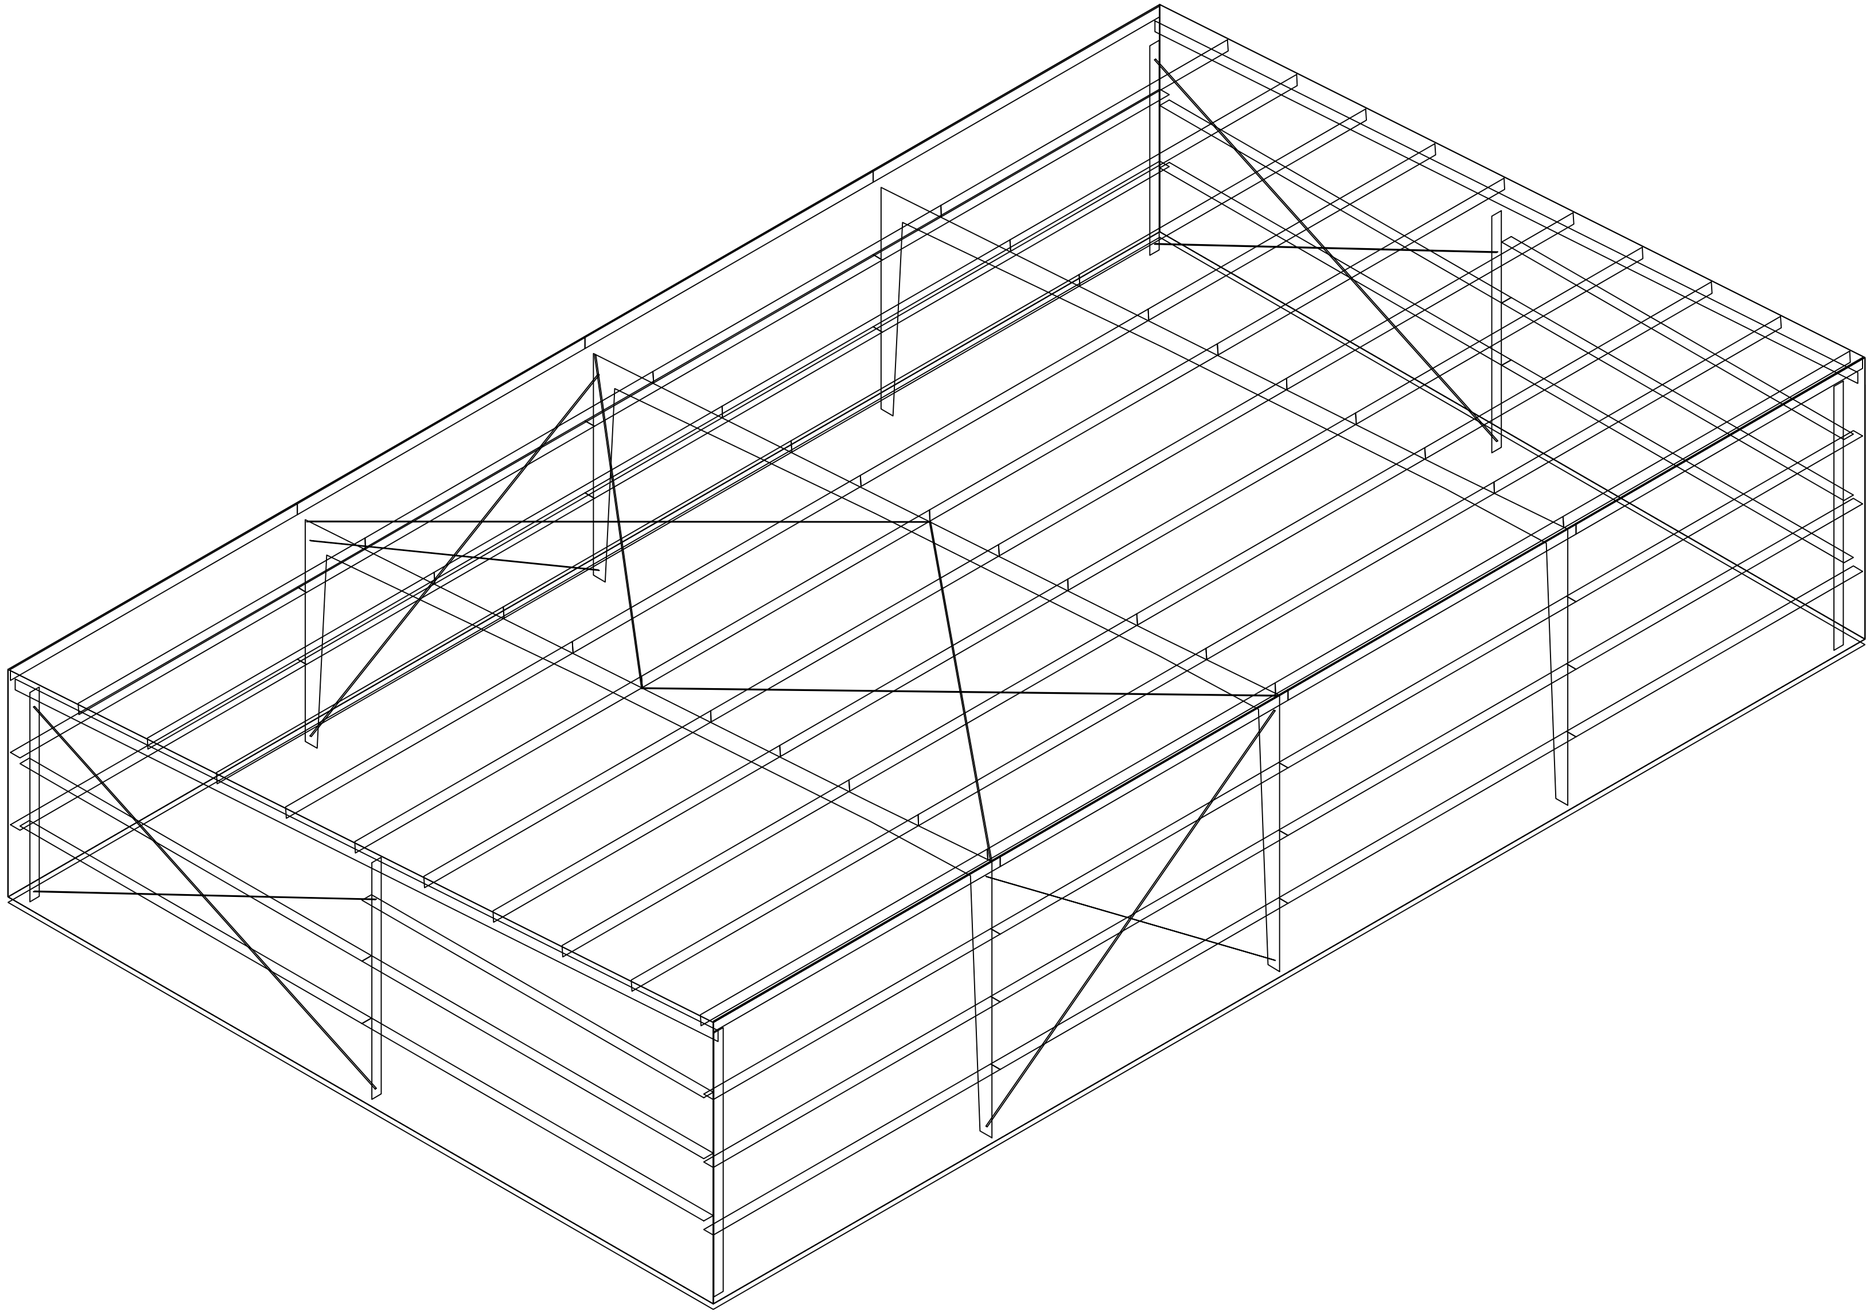

ARCHITECT ZUBAIR AHMED ZAFAR ALI	PROJECT MANAGER TANVEER AHMED	CLIENT _____	PROJECT CONSTRUCTION OF PRE-ENGINEERED SHED 49x80	DRAWN REHAN SALEEM	ACCO ARCHITECTURE & CONSTRUCTION
ADDRESS _____	No. / ISSUED / DATE 1. PROPOSED DRAWING	CONSULTANT : AHMED CONSTRUCTION COMPANY OFFICE NO.2,3RD FLOOR BIG CITY PLAZA, GULBERG-iii,Lahore 0322-8000190	DRAWING 3D VIEW	PLOTTED DATE 27-November-2025 SCALE SCALED TO FIT	DWG. NO. 01

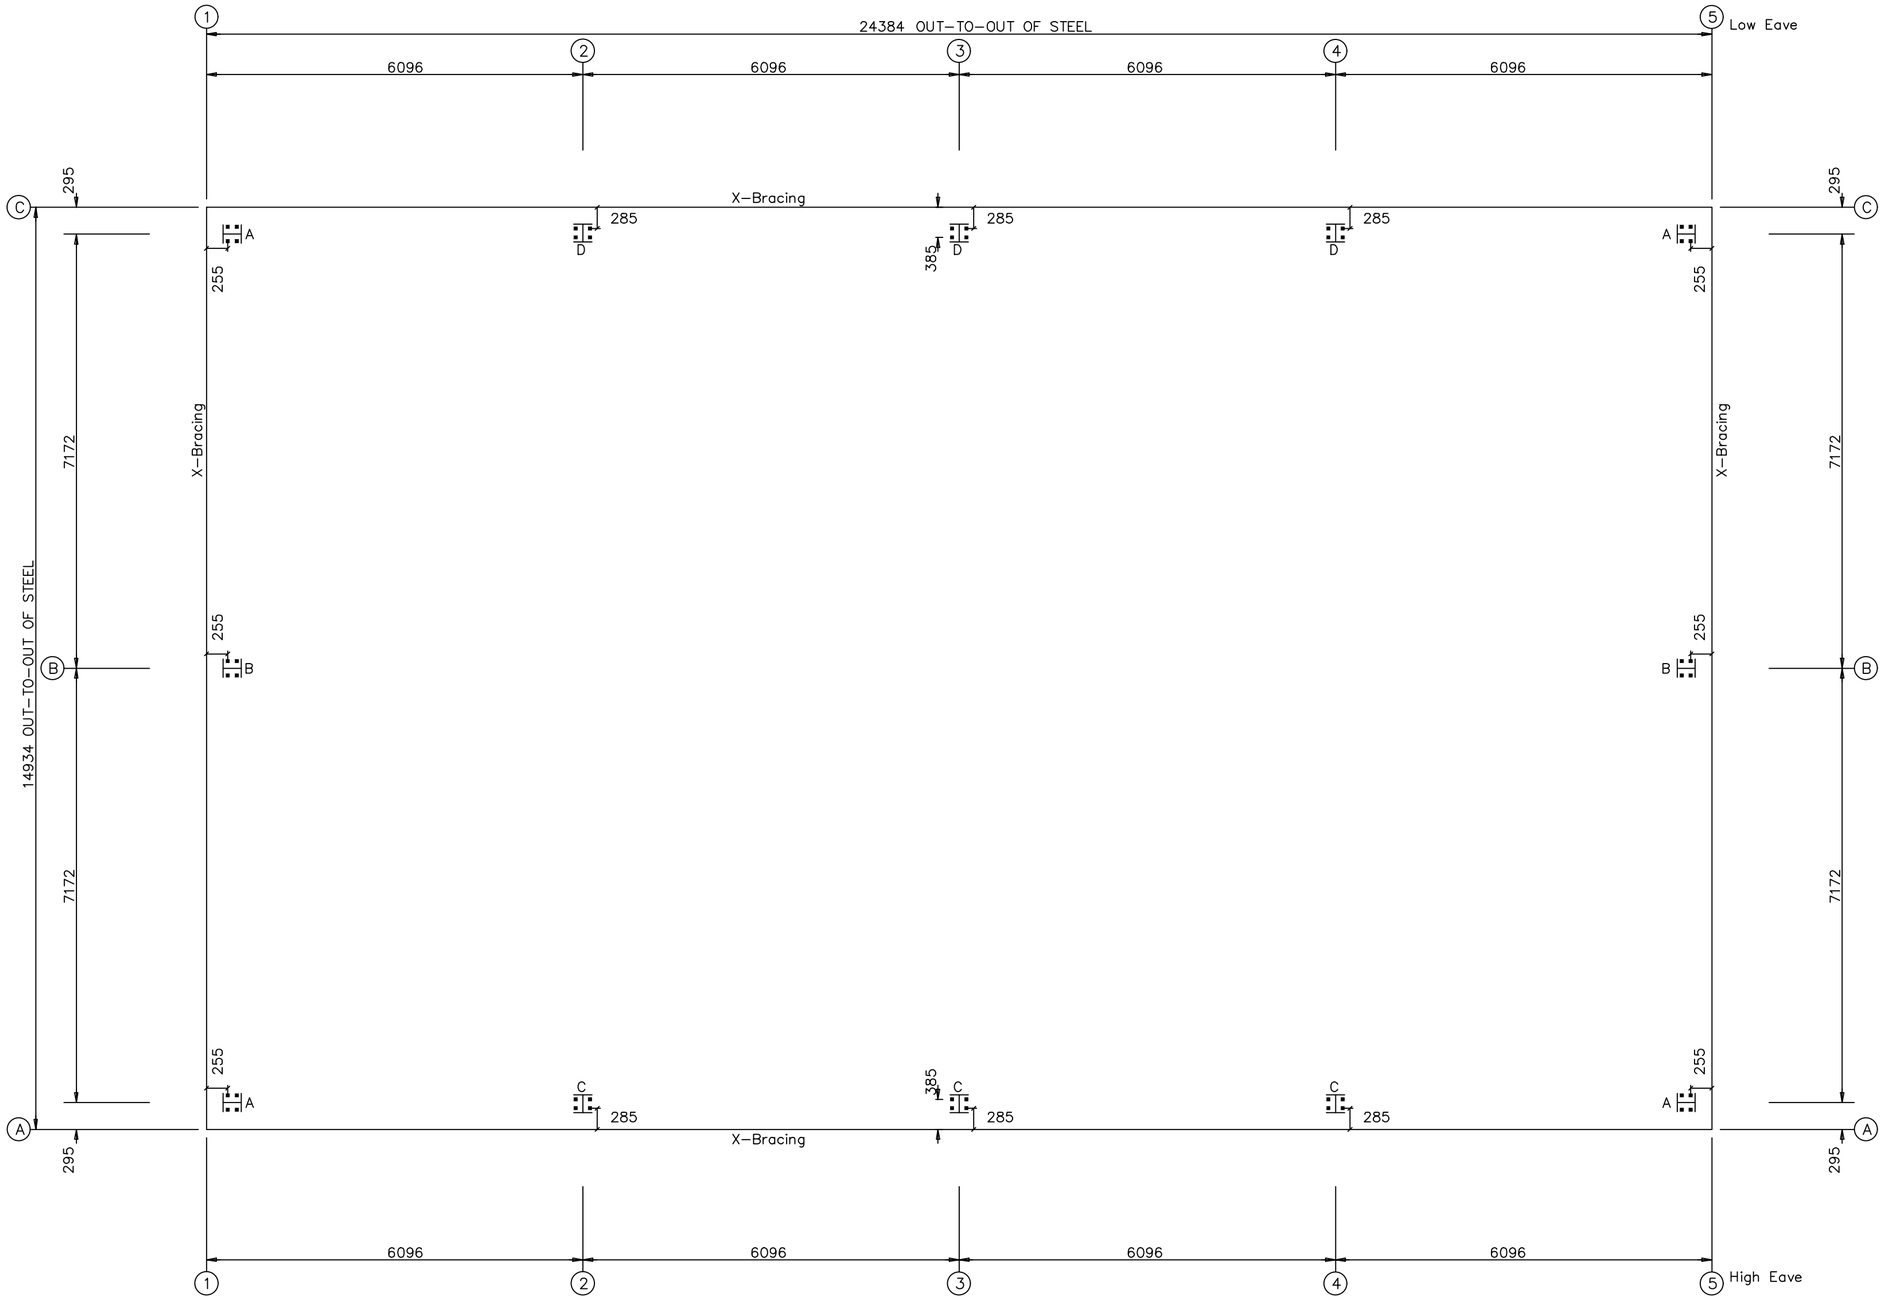


ANCHOR BOLT PLAN

NOTE: All Base Plates @ 0 (U.N.)

ARCHITECT ZUBAIR AHMED ZAFAR ALI	PROJECT MANAGER TANVEER AHMED	CLIENT _____	PROJECT CONSTRUCTION OF PRE-ENGINEERED SHED 49x80
ADDRESS _____	No. / ISSUED / DATE 1. PROPOSED DRAWING	CONSULTANT : AHMED CONSTRUCTION COMPANY OFFICE NO.2,3RD FLOOR BIG CITY PLAZA, GULBERG-iii,Lahore 0322-8000190	DRAWING ANCHOR BOLT PLAN


DRAWN	REHAN SALEEM
PLOTTED DATE	27-November-2025
SCALE	SCALED TO FIT
DWG. NO.	02

ACCO
ARCHITECTURE & CONSTRUCTION

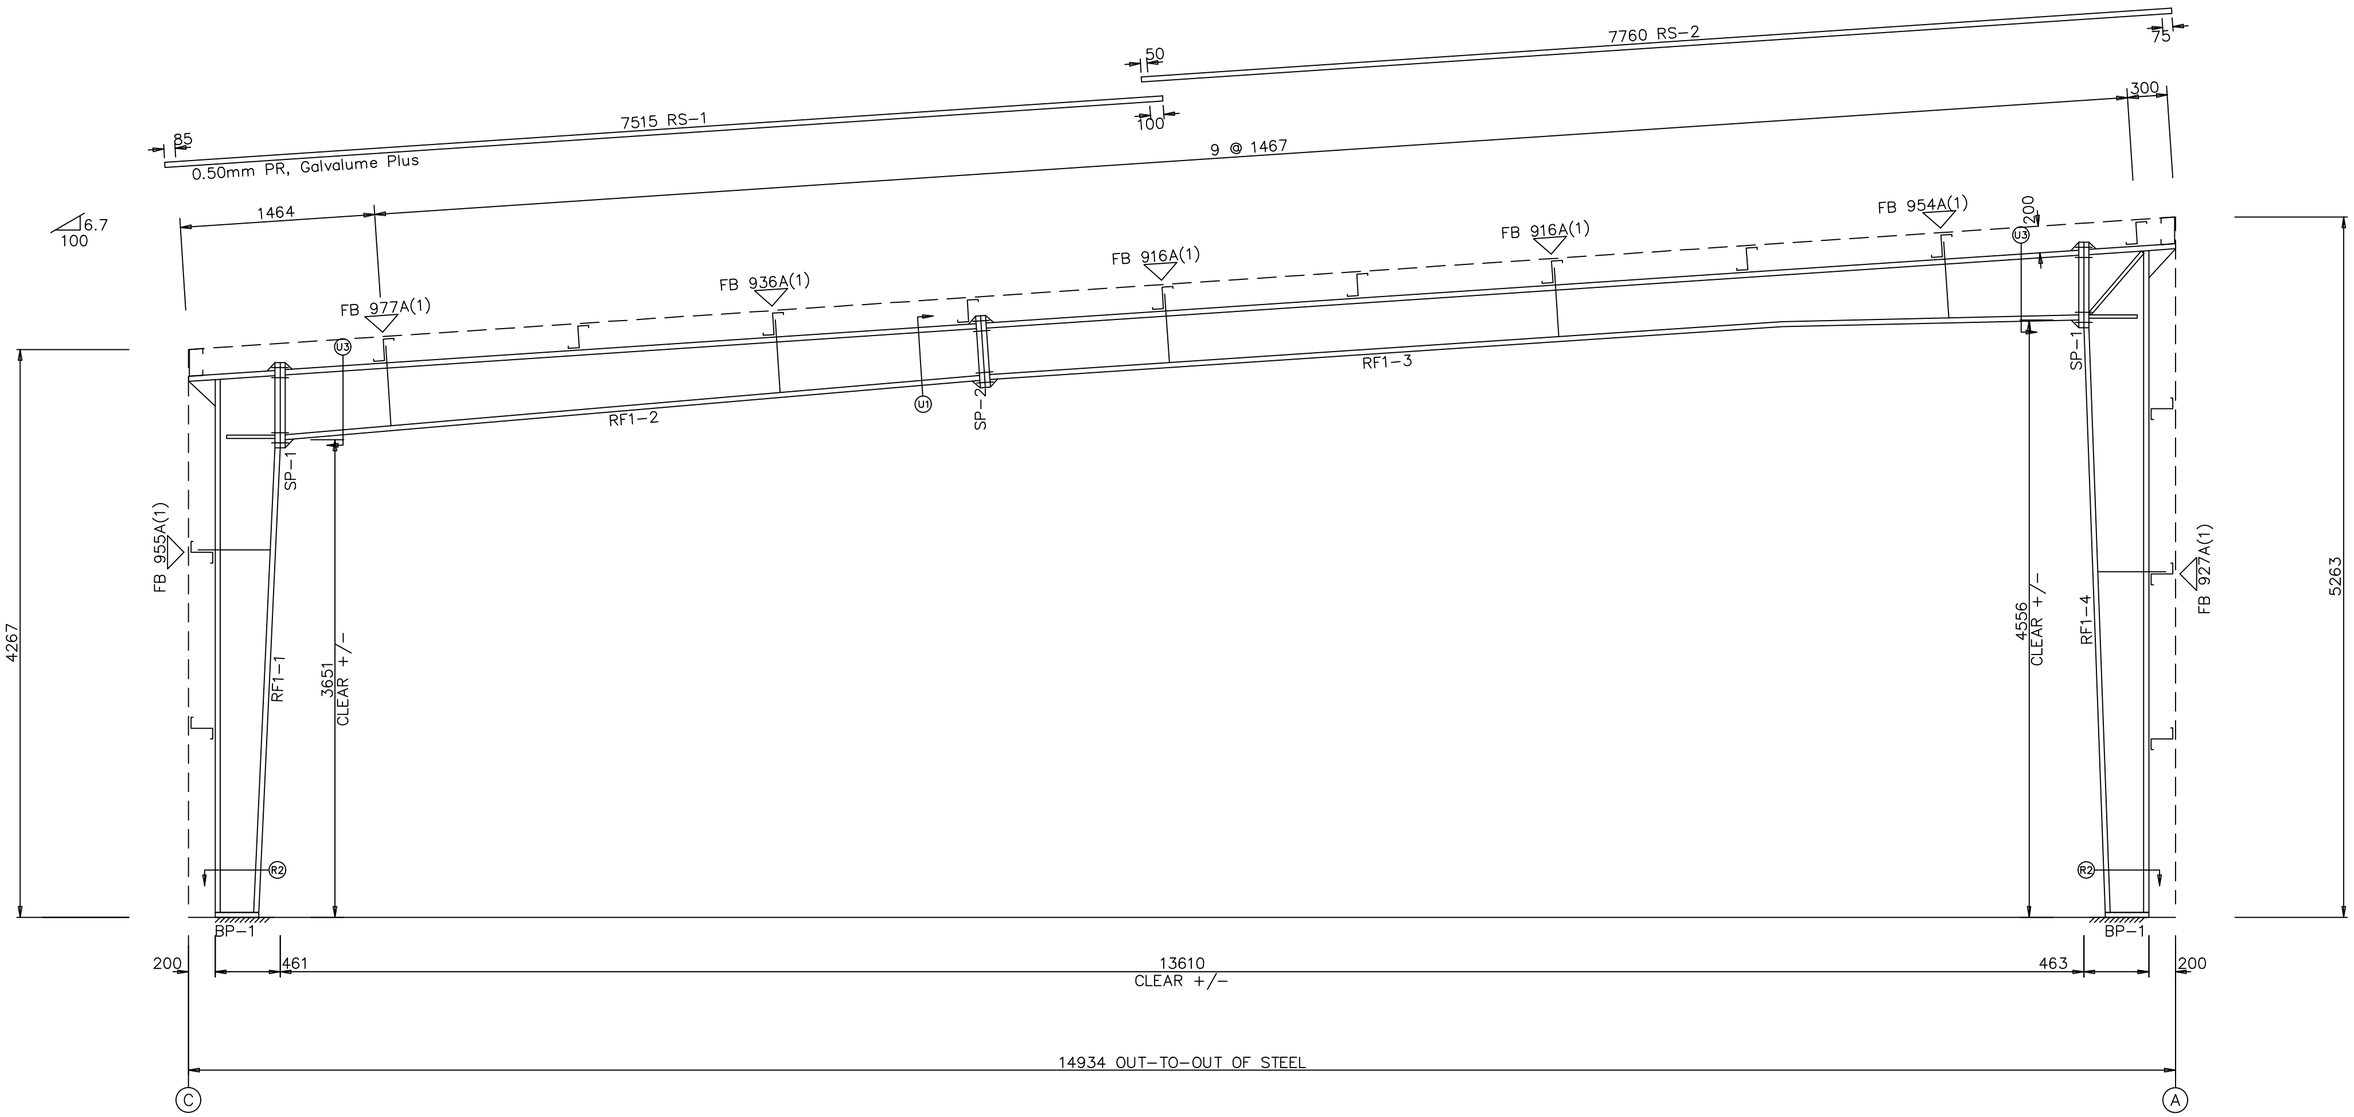

RIGID FRAME ELEVATION: FRAME LINE 2 3 4

ARCHITECT ZUBAIR AHMED ZAFAR ALI	PROJECT MANAGER TANVEER AHMED	CLIENT _____	PROJECT CONSTRUCTION OF PRE-ENGINEERED SHED 49x80	DRAWN REHAN SALEEM	ACCO ARCHITECTURE & CONSTRUCTION
ADDRESS _____	No. / ISSUED / DATE 1. PROPOSED DRAWING	CONSULTANT : AHMED CONSTRUCTION COMPANY OFFICE NO.2,3RD FLOOR BIG CITY PLAZA, GULBERG-iii,Lahore 0322-8000190	DRAWING RIGID FRAME ELEVATION	PLOTTED DATE 27-November-2025 SCALE SCALED TO FIT	DWG. NO. 03

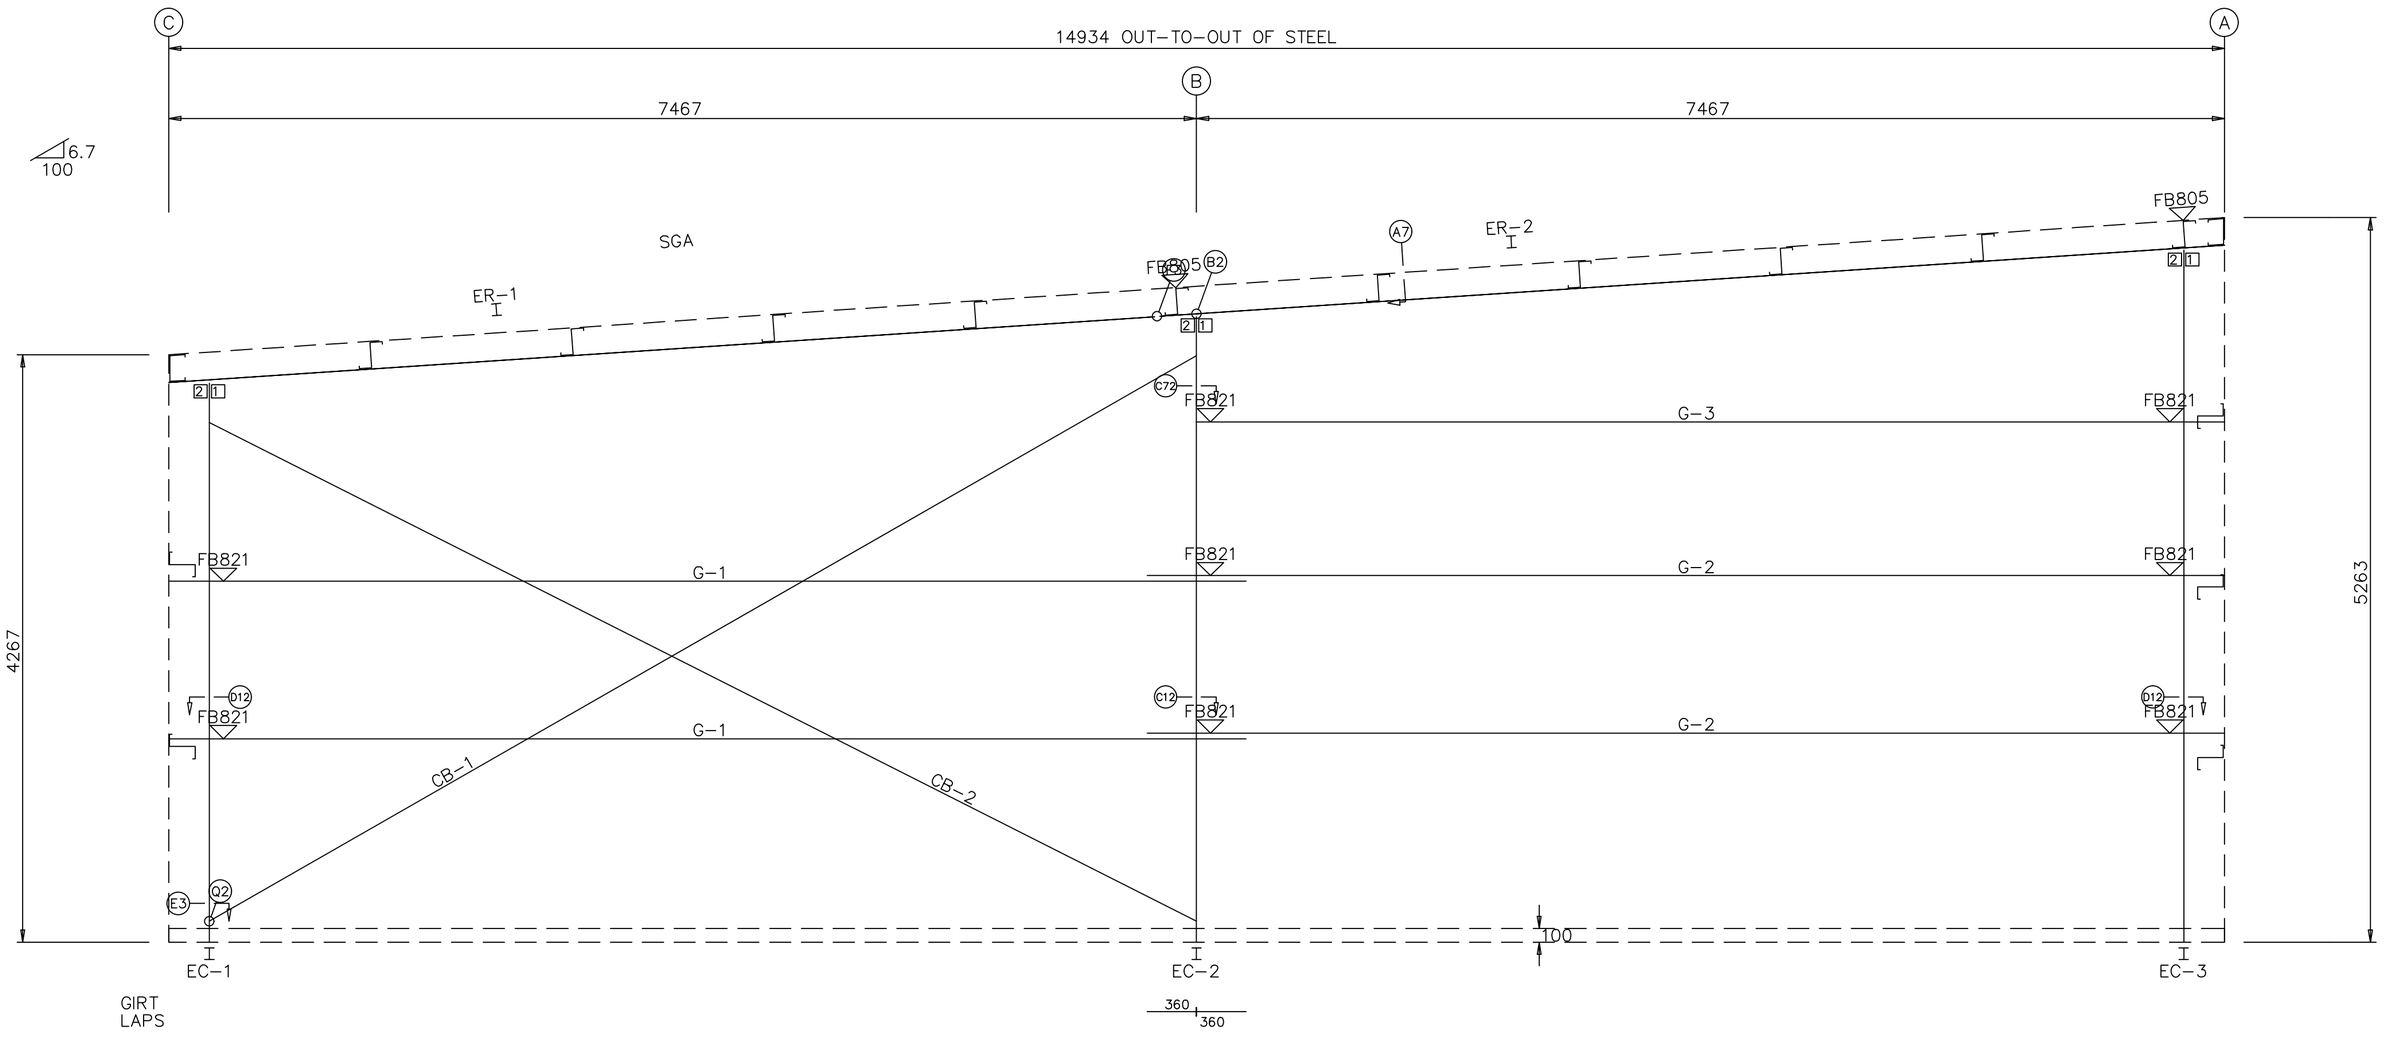


ENDWALL FRAMING: FRAME LINE 1

ARCHITECT ZUBAIR AHMED ZAFAR ALI	PROJECT MANAGER TANVEER AHMED	CLIENT _____	PROJECT CONSTRUCTION OF PRE-ENGINEERED SHED 49x80	DRAWN REHAN SALEEM
ADDRESS _____	No. / ISSUED / DATE 1. PROPOSED DRAWING	CONSULTANT : AHMED CONSTRUCTION COMPANY OFFICE NO.2,3RD FLOOR BIG CITY PLAZA, GULBERG-iii,Lahore 0322-8000190	DRAWING END WALL FRAMING	PLOTTED DATE 27-November-2025 SCALE SCALED TO FIT

ACCO
ARCHITECTURE & CONSTRUCTION

DWG. NO. 04

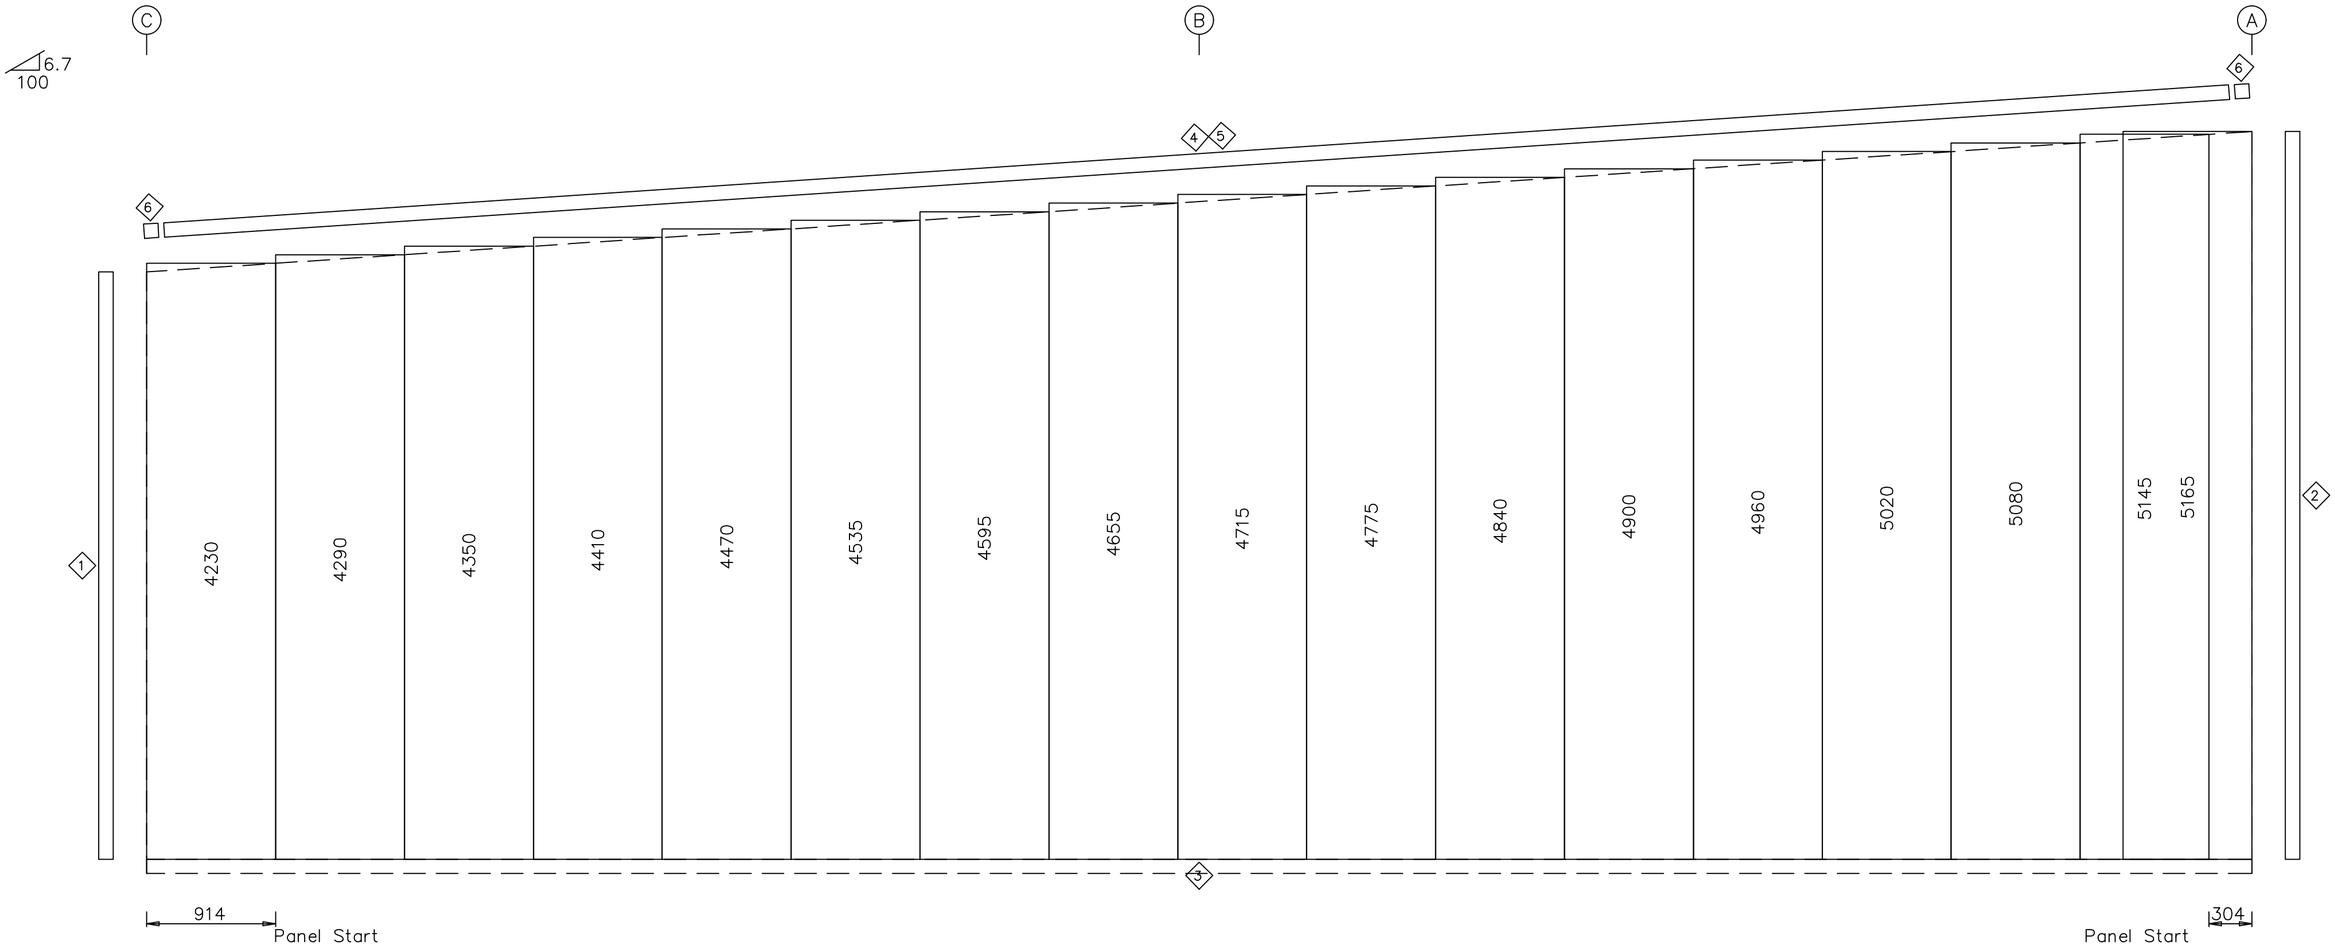


ENDWALL SHEETING & TRIM: FRAME LINE 1

PANELS: 0.50mm PR – Beige RAL1001


ARCHITECT: ZUBAIR AHMED, ZAFAR ALI	PROJECT MANAGER: TANVEER AHMED	CLIENT: _____
ADDRESS: _____	CONSULTANT : AHMED CONSTRUCTION COMPANY, OFFICE NO.2,3RD FLOOR BIG CITY PLAZA, GULBERG-iii,Lahore 0322-8000190	PROJECT: CONSTRUCTION OF PRE-ENGINEERED SHED 49x80
	DRAWING: ENDWALL SHEETING & TRIM	DRAWN: REHAN SALEEM
		PLOTTED DATE: 27-November-2025
		SCALE: SCALED TO FIT
		ACCO ARCHITECTURE & CONSTRUCTION
		DWG. NO. 05

No.	ISSUED	DATE
1.	PROPOSED DRAWING	

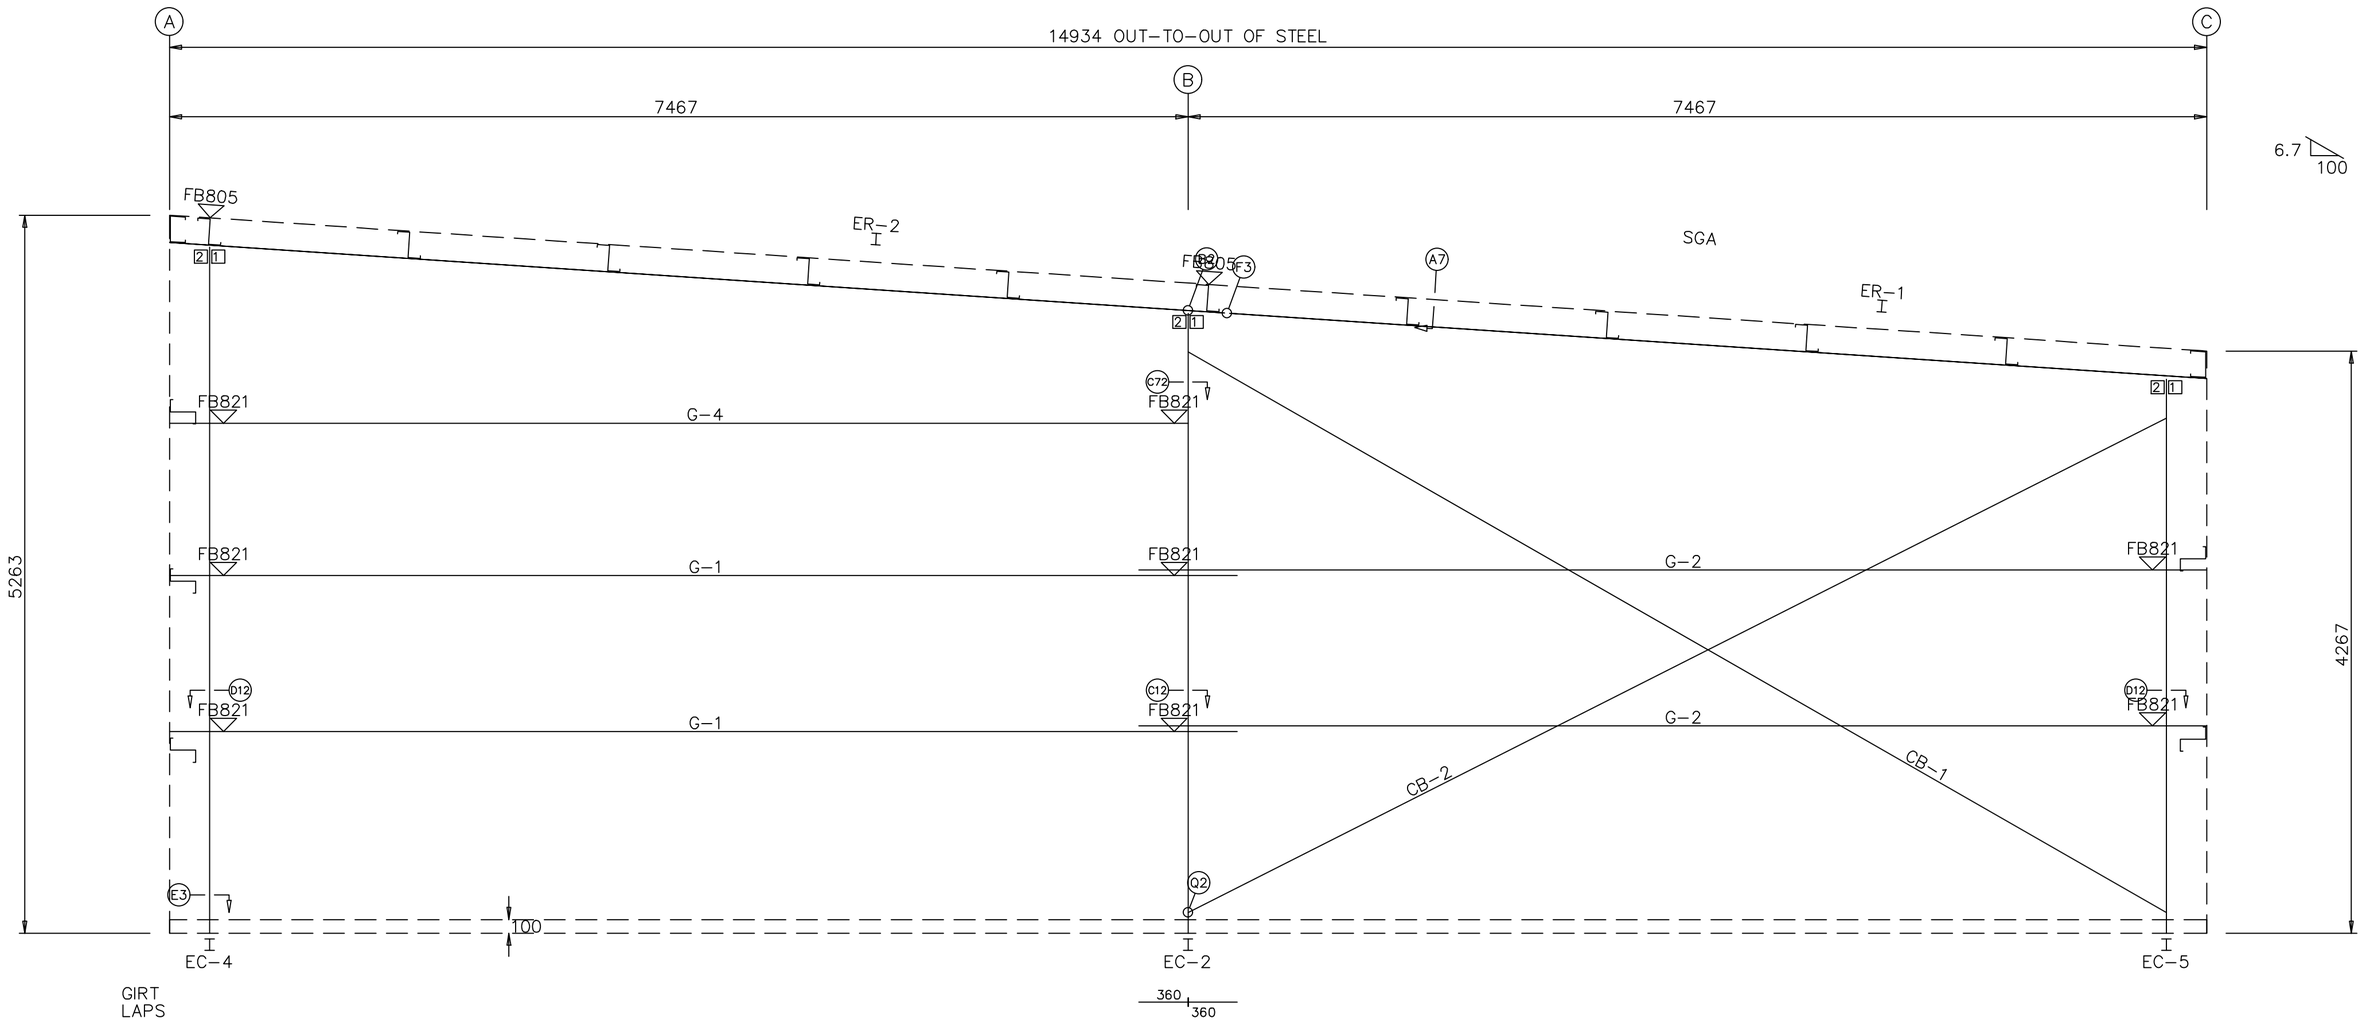

ENDWALL FRAMING: FRAME LINE 5

ARCHITECT ZUBAIR AHMED ZAFAR ALI	PROJECT MANAGER TANVEER AHMED	CLIENT _____	PROJECT CONSTRUCTION OF PRE-ENGINEERED SHED 49x80	DRAWN REHAN SALEEM	ACCO ARCHITECTURE & CONSTRUCTION
ADDRESS _____	No. / ISSUED / DATE 1. PROPOSED DRAWING	CONSULTANT : AHMED CONSTRUCTION COMPANY OFFICE NO.2,3RD FLOOR BIG CITY PLAZA, GULBERG-iii,Lahore 0322-8000190	DRAWING ENDWALL FRAMING	PLOTTED DATE 27-November-2025 SCALE SCALED TO FIT	DWG. NO. 06

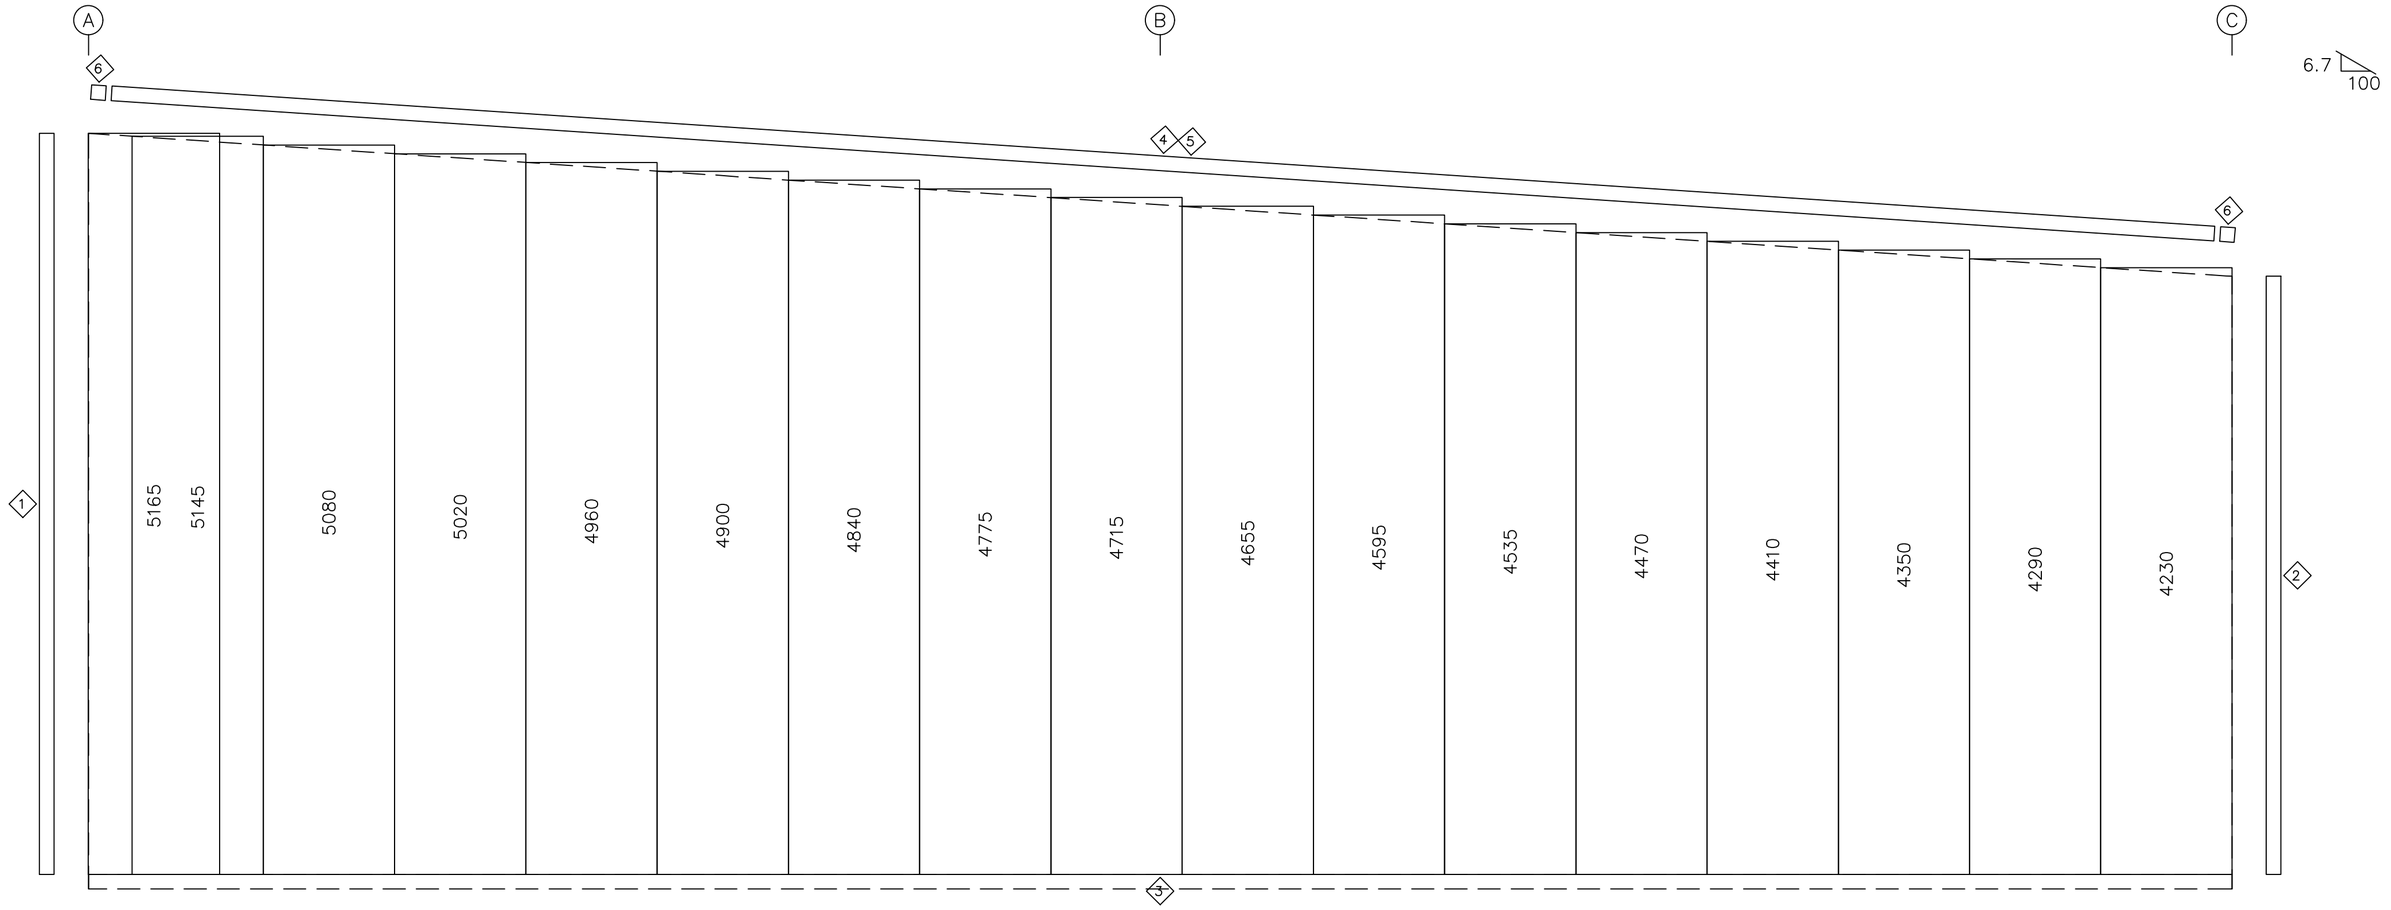


ENDWALL SHEETING & TRIM: FRAME LINE 5

PANELS: 0.50mm PR – Beige RAL1001

ARCHITECT: ZUBAIR AHMED, ZAFAR ALI	PROJECT MANAGER: TANVEER AHMED	CLIENT: _____
ADDRESS: _____	CONSULTANT : AHMED CONSTRUCTION COMPANY, OFFICE NO.2,3RD FLOOR BIG CITY PLAZA, GULBERG-iii,Lahore 0322-8000190	PROJECT: CONSTRUCTION OF PRE-ENGINEERED SHED 49x80
	DRAWING: ENDWALL SHEETING & TRIM	DRAWN: REHAN SALEEM
		PLOTTED DATE: 27-November-2025
		SCALE: SCALED TO FIT
		ACCO ARCHITECTURE & CONSTRUCTION
		DWG. NO. 07

No.	ISSUED	DATE
1.	PROPOSED DRAWING	

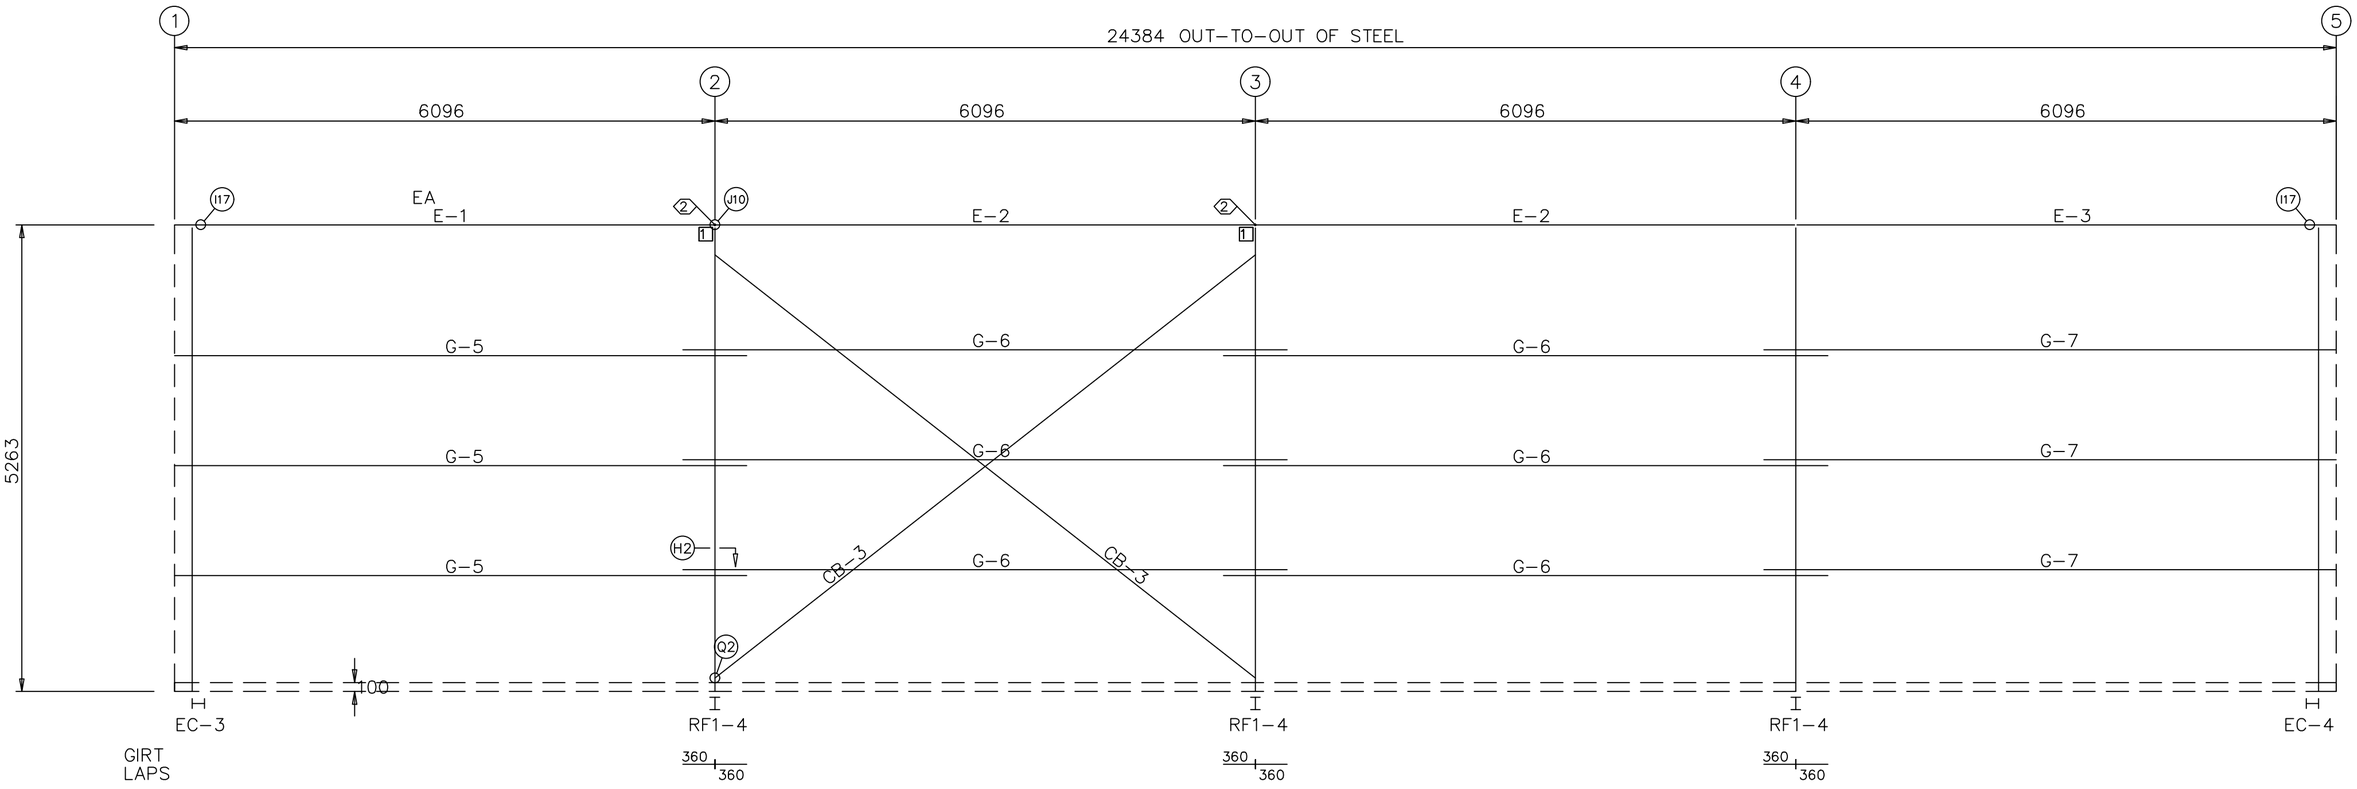


SIDEWALL FRAMING: FRAME LINE A

ARCHITECT ZUBAIR AHMED ZAFAR ALI	PROJECT MANAGER TANVEER AHMED	CLIENT _____	PROJECT CONSTRUCTION OF PRE-ENGINEERED SHED 49x80
ADDRESS _____	No. / ISSUED / DATE 1. PROPOSED DRAWING	CONSULTANT : AHMED CONSTRUCTION COMPANY OFFICE NO.2,3RD FLOOR BIG CITY PLAZA, GULBERG-iii,Lahore 0322-8000190	DRAWING SIDEWALL FRAMING

DRAWN	REHAN SALEEM
PLOTTED DATE	27-November-2025
SCALE	SCALED TO FIT
DWG. NO.	08


ACCO
ARCHITECTURE & CONSTRUCTION

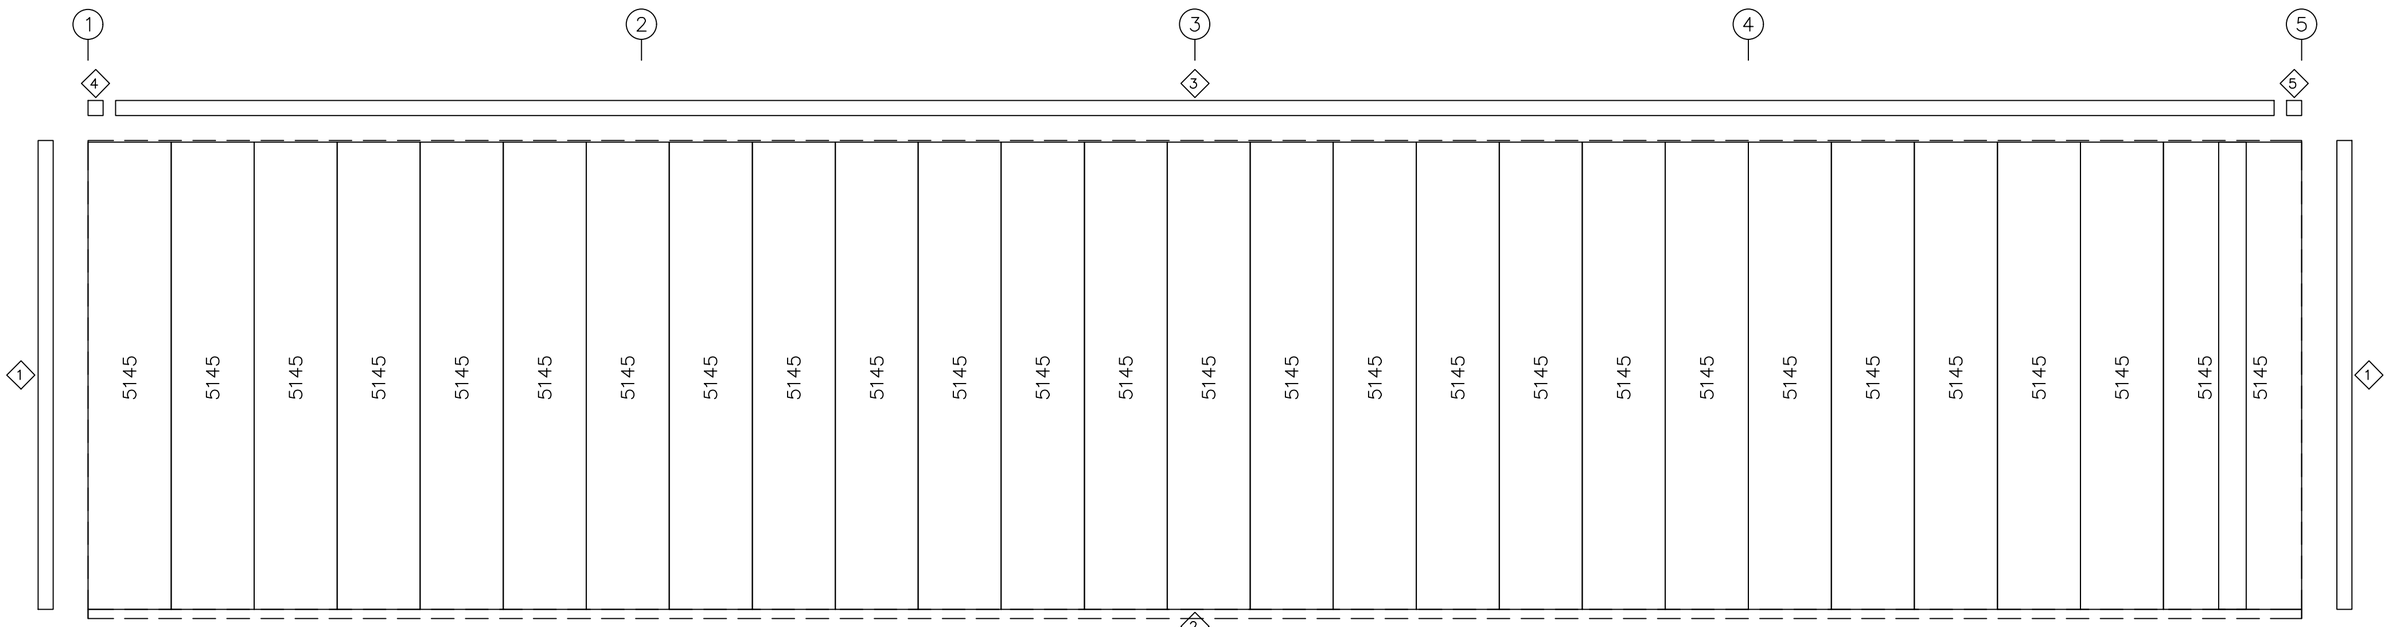

SIDEWALL SHEETING & TRIM: FRAME LINE A

PANELS: 0.50mm PR – Beige RAL1001

ARCHITECT ZUBAIR AHMED ZAFAR ALI	PROJECT MANAGER TANVEER AHMED	CLIENT _____	PROJECT CONSTRUCTION OF PRE-ENGINEERED SHED 49x80	DRAWN REHAN SALEEM	ACCO ARCHITECTURE & CONSTRUCTION
ADDRESS _____	No. / ISSUED / DATE 1. PROPOSED DRAWING	CONSULTANT : AHMED CONSTRUCTION COMPANY OFFICE NO.2,3RD FLOOR BIG CITY PLAZA, GULBERG-iii,Lahore 0322-8000190	DRAWING SIDEWALL SHEETING & TRIM	PLOTTED DATE 27-November-2025 SCALE SCALED TO FIT	DWG. NO. 09

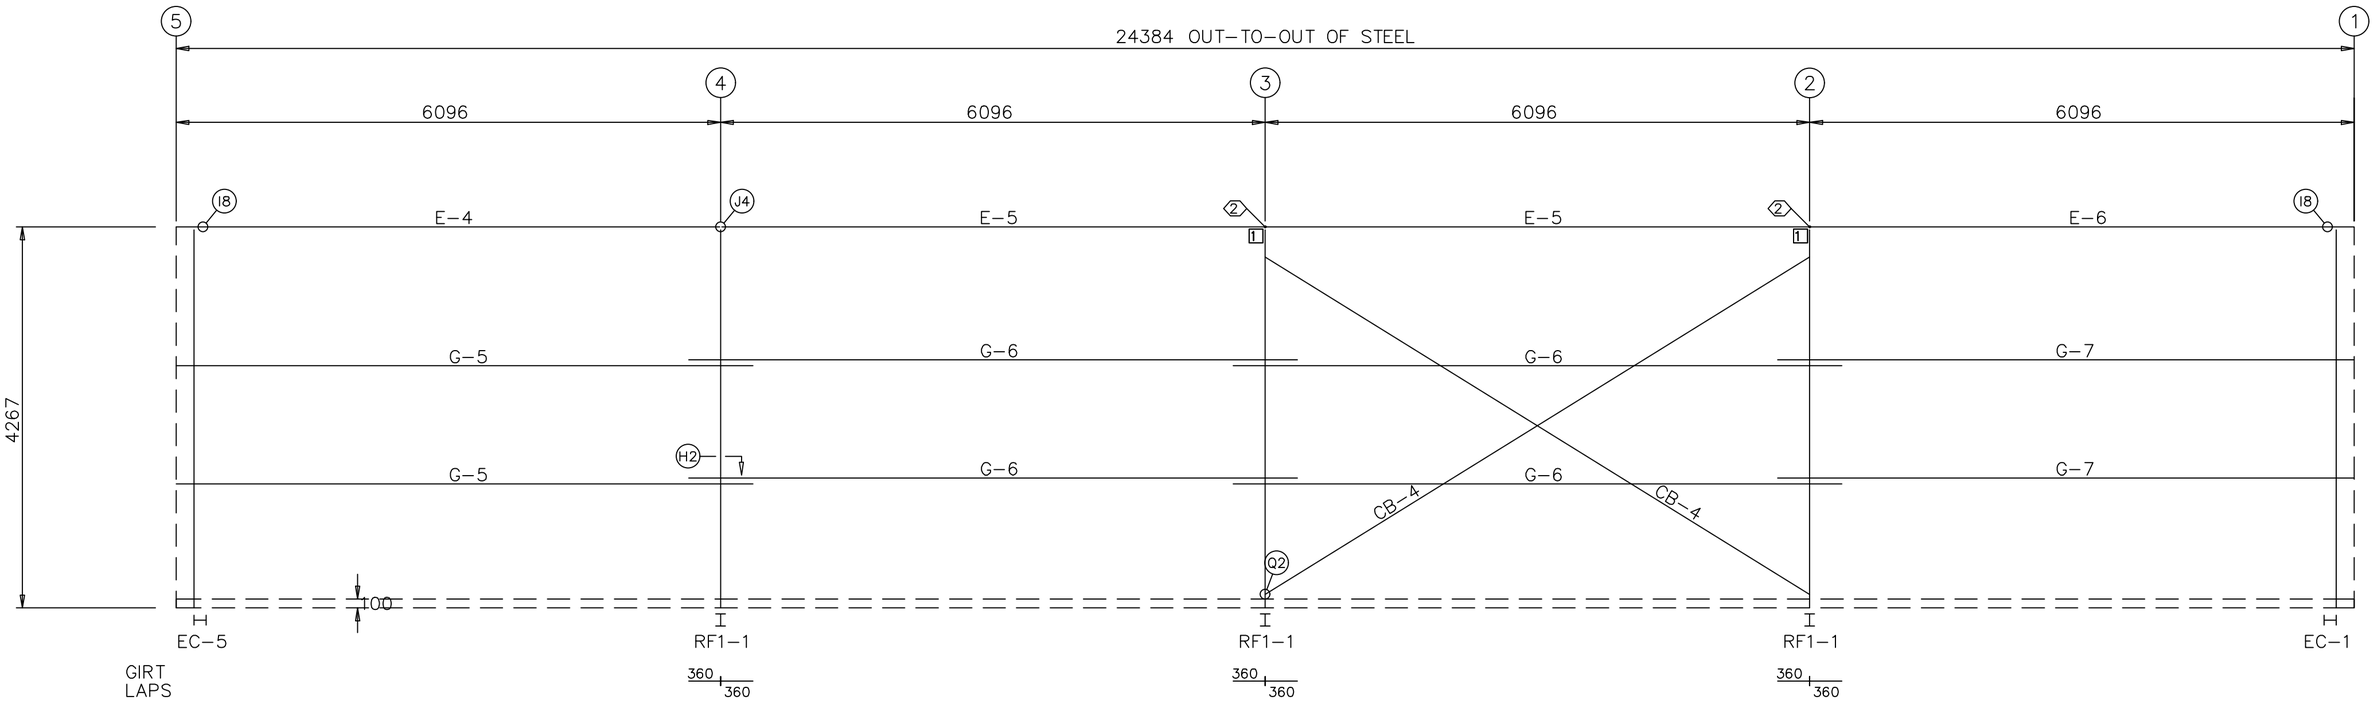


SIDEWALL FRAMING: FRAME LINE C

ARCHITECT ZUBAIR AHMED ZAFAR ALI	PROJECT MANAGER TANVEER AHMED	CLIENT _____	PROJECT CONSTRUCTION OF PRE-ENGINEERED SHED 49x80
ADDRESS _____	No. / ISSUED / DATE 1. PROPOSED DRAWING	CONSULTANT : AHMED CONSTRUCTION COMPANY OFFICE NO.2,3RD FLOOR BIG CITY PLAZA, GULBERG-iii,Lahore 0322-8000190	DRAWING SIDEWALL FRAMING

DRAWN	REHAN SALEEM
PLOTTED DATE	27-November-2025
SCALE	SCALED TO FIT
DWG. NO.	10


ACCO
ARCHITECTURE & CONSTRUCTION

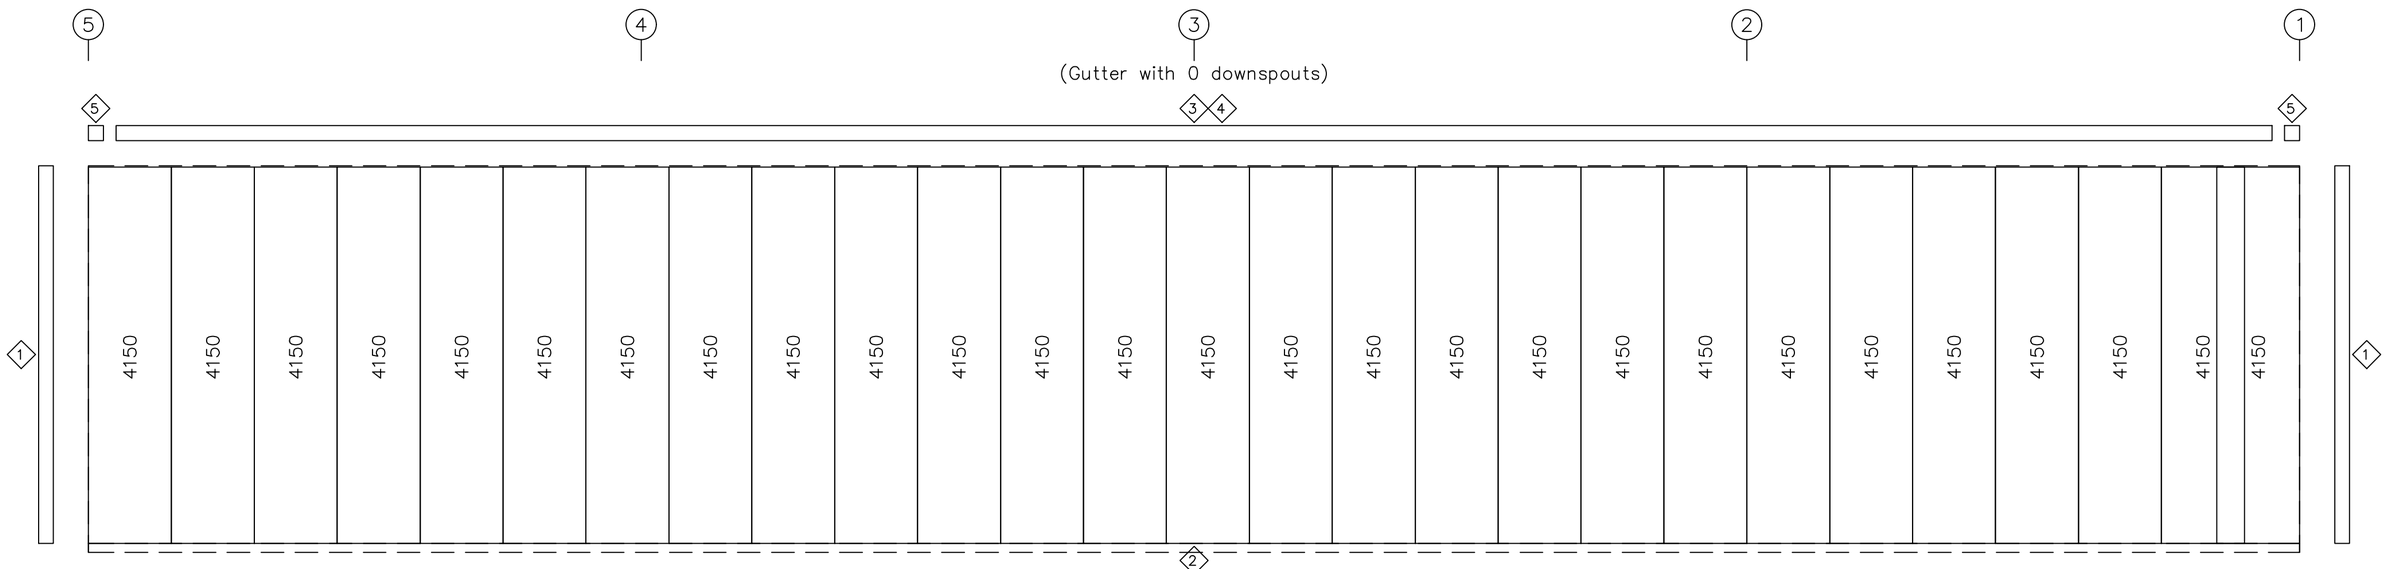

SIDEWALL SHEETING & TRIM: FRAME LINE C

PANELS: 0.50mm PR – Beige RAL1001

ARCHITECT ZUBAIR AHMED ZAFAR ALI	PROJECT MANAGER TANVEER AHMED	CLIENT _____	PROJECT CONSTRUCTION OF PRE-ENGINEERED SHED 49x80	DRAWN REHAN SALEEM	ACCO ARCHITECTURE & CONSTRUCTION
ADDRESS _____	No. / ISSUED / DATE 1. PROPOSED DRAWING	CONSULTANT : AHMED CONSTRUCTION COMPANY OFFICE NO.2,3RD FLOOR BIG CITY PLAZA, GULBERG-iii,Lahore 0322-8000190	DRAWING SIDEWALL SHEETING & TRIM	PLOTTED DATE 27-November-2025 SCALE SCALED TO FIT	DWG. NO. 11

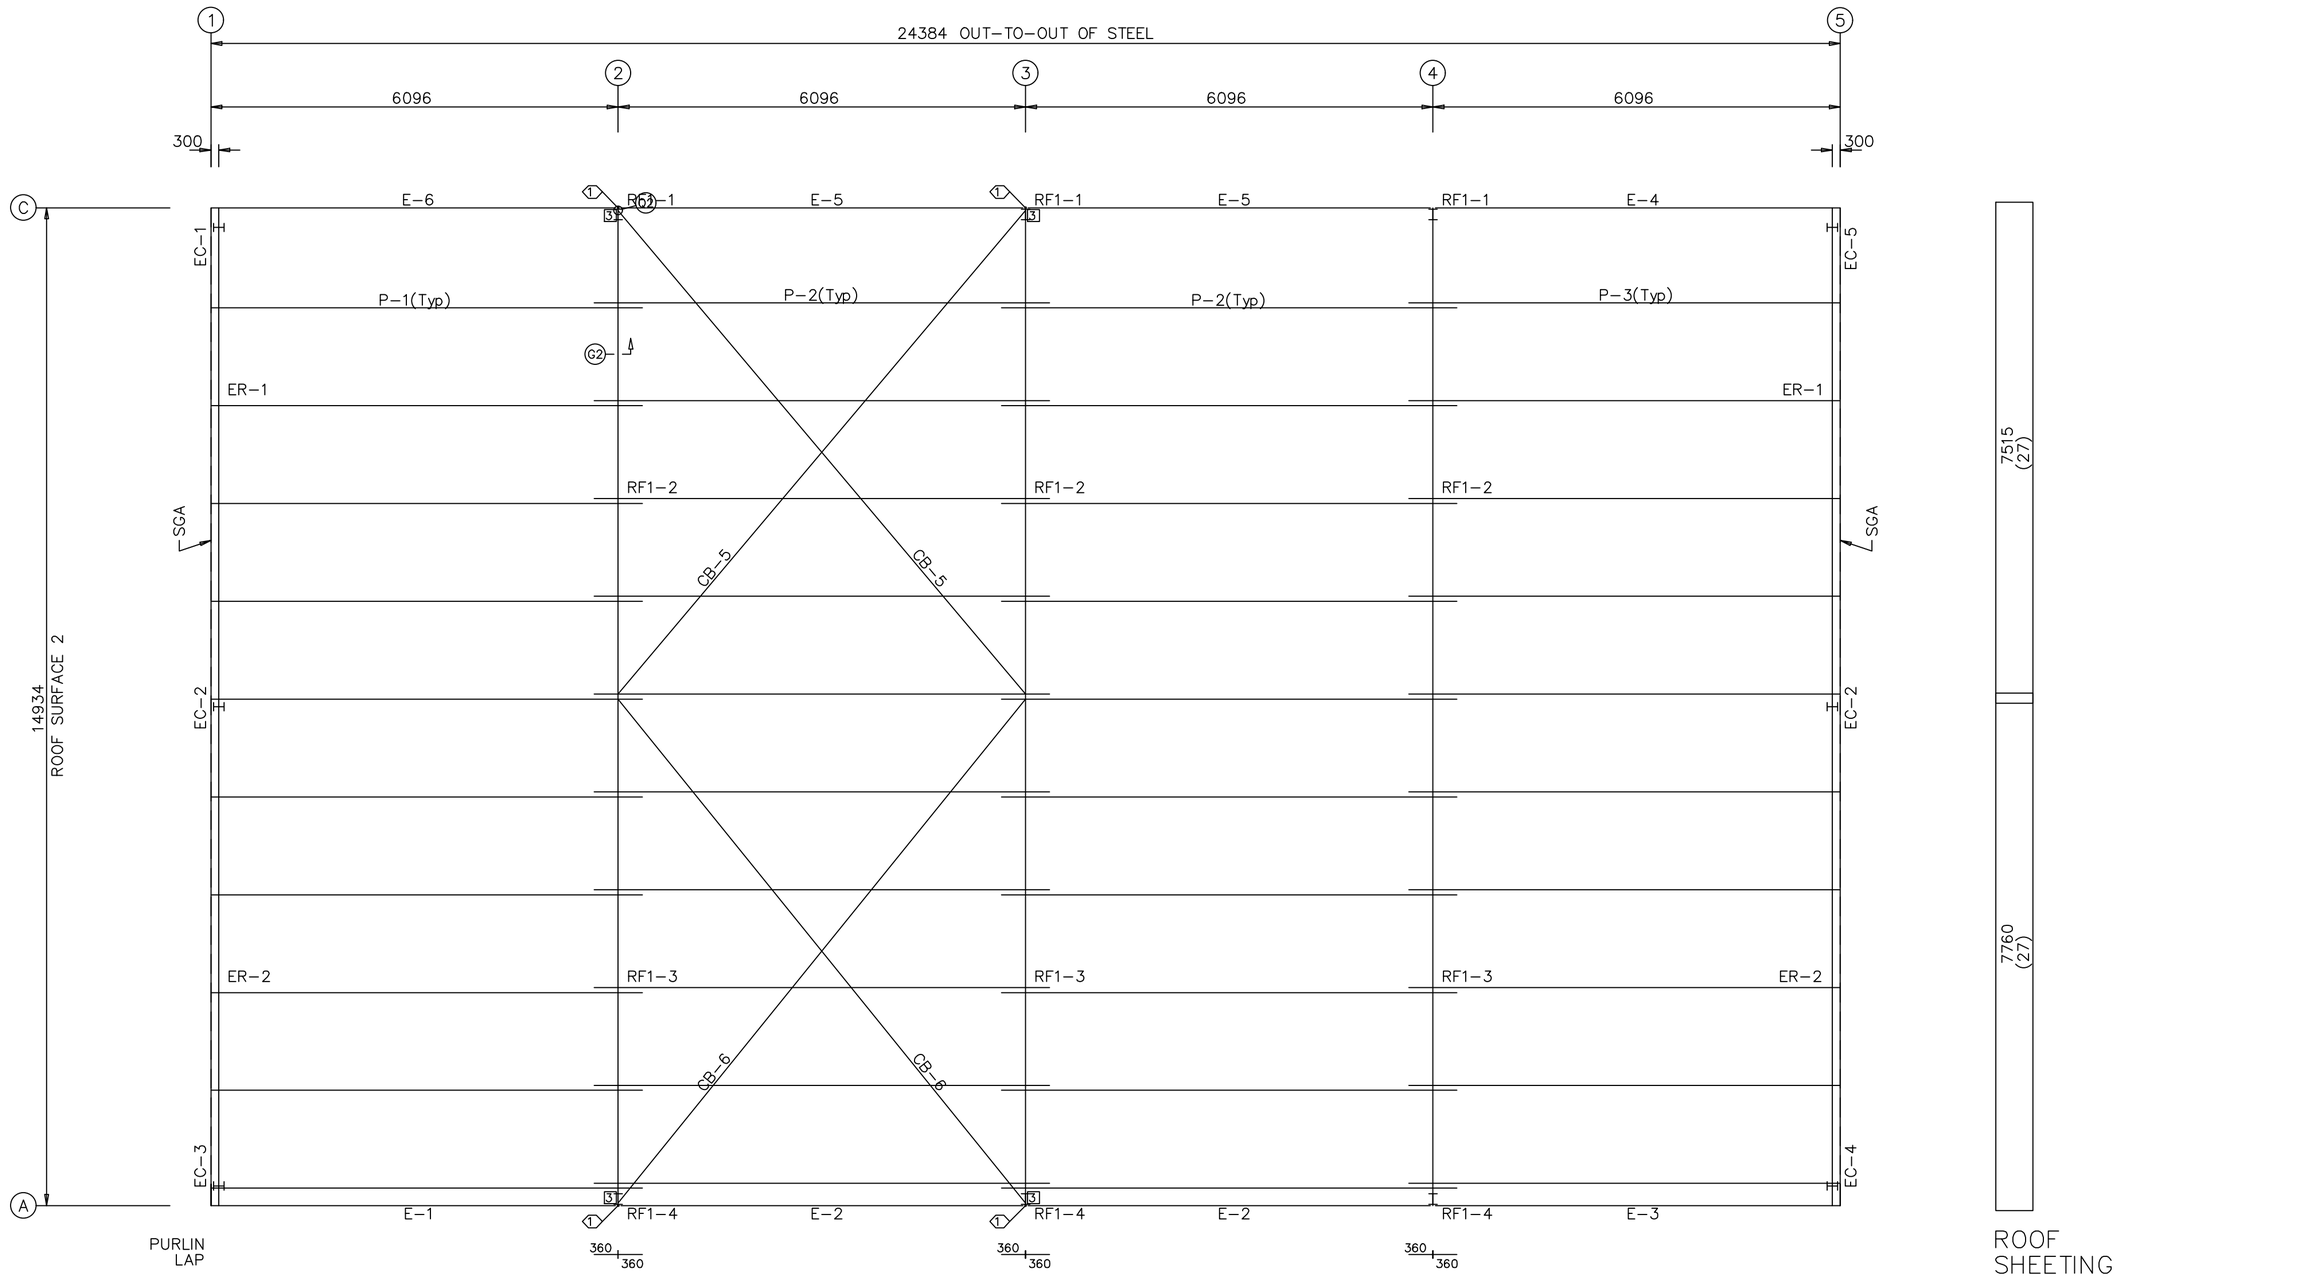


ROOF FRAMING PLAN

ARCHITECT ZUBAIR AHMED ZAFAR ALI	PROJECT MANAGER TANVEER AHMED	CLIENT _____	PROJECT CONSTRUCTION OF PRE-ENGINEERED SHED 49x80
ADDRESS _____	No. / ISSUED / DATE 1. PROPOSED DRAWING	CONSULTANT : AHMED CONSTRUCTION COMPANY OFFICE NO.2,3RD FLOOR BIG CITY PLAZA, GULBERG-iii,Lahore 0322-8000190	DRAWING ROOF FRAMING PLAN

DRAWN	REHAN SALEEM
PLOTTED DATE	27-November-2025
SCALE	SCALED TO FIT
DWG. NO.	12

ACCO
ARCHITECTURE & CONSTRUCTION

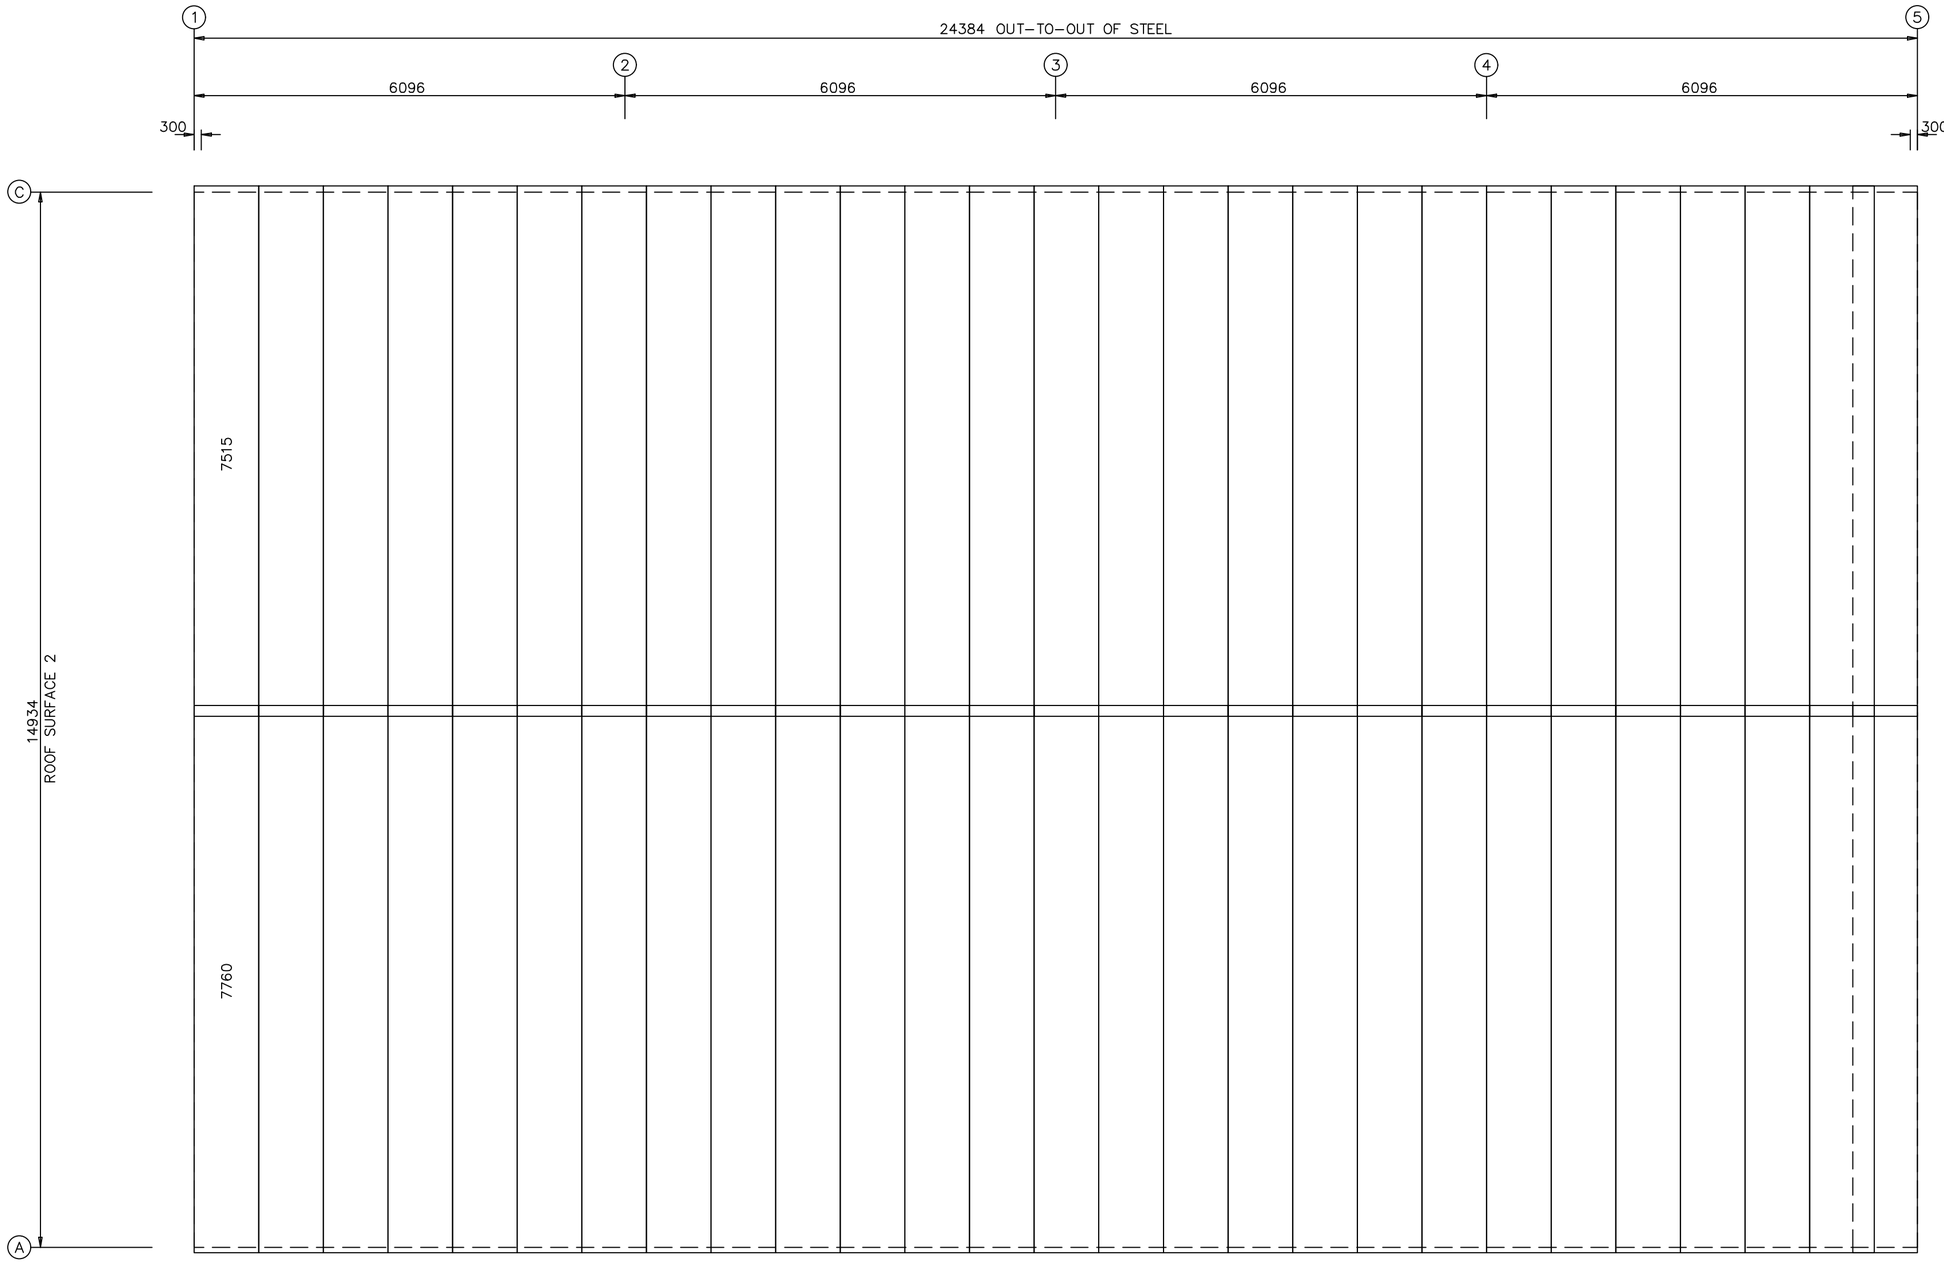

ROOF SHEETING PLAN

PANELS: 0.50mm PR – Galvalume Plus

ARCHITECT ZUBAIR AHMED ZAFAR ALI	PROJECT MANAGER TANVEER AHMED	CLIENT _____	PROJECT CONSTRUCTION OF PRE-ENGINEERED SHED 49x80
ADDRESS _____	No. / ISSUED / DATE 1. PROPOSED DRAWING	CONSULTANT : AHMED CONSTRUCTION COMPANY OFFICE NO.2,3RD FLOOR BIG CITY PLAZA, GULBERG-iii,Lahore 0322-8000190	DRAWING ROOF SHEETING PLAN

DRAWN	REHAN SALEEM
PLOTTED DATE	27-November-2025
SCALE	SCALED TO FIT
DWG. NO.	13

ACCO
ARCHITECTURE & CONSTRUCTION

To,
Mr. Abbas Mujahid Sahab
Quaid e Azam Industrial Area, Lahore Punjab

Date: November 27, 2025
Ref#: ACCO/PEB/1009

SUBJECT: - **QUOTATION FOR CONSTRUCTION OF PRE-ENGINEERED BUILDING FOR ADSELLS**

السلام علیکم
We are pleased to submit our best quote for subject work as follows: -

Sr.#	Item Description	Area (SFT)	Rate (Rs.)	Amount
1	Construction, supply and installation of a prefabricated steel shed floor for production unit Complete in all respect. Area: 141x59.6 feet Height Approx. 14 feet	8,389.5	1,361/-	11,420,207/-
	Total Amount without Taxes			**11,420,207/-**
	GST 18%			**2,055,637/-**
	Total Amount with Taxes			**13,473,744/-**

Terms & Conditions:


1. This quotation excludes all taxes.
2. Complication Time 30 days
3. 50% Advance before starting the Project other balance Payment according to percentage of Work
4. Provision of storage facilities for our goods and equipment, where necessary, shall be client responsibility.
5. Electricity & water supply will be provided by the client.
6. This quotation is valid for 30 days from above mentioned date.
7. Civil Work is not included.

We will be obliged for your cooperation in this regard.
Thanks & Regards.
Truly yours,

Tanveer Ahmed
Director
+92-322-8000190

Product description

1. Building System

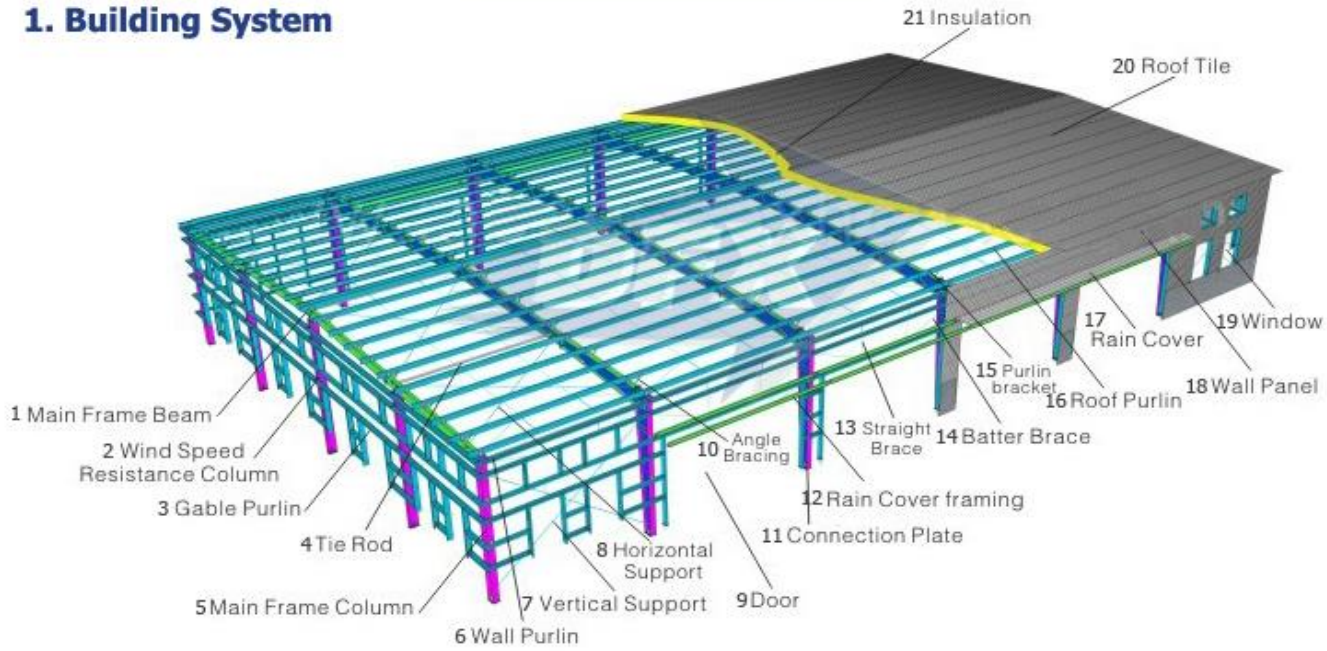

2. Specification

Items		Specification
Main Steel Frame	Column	5 mm and 6 mm
	Beam	5 mm and 6 mm
Secondary Frame	Purlin	1.5 mm
	Knee brace	12 mm
	Tie Rod	50 mm x 50 mm angle
	Brace	Sag Rod
	Vertical and Horizontal Support	Q235 Angle Steel, Round Bar or Steel Pipe
Maintenance system	Roof Panel	0.45 mm sheet PPGI (Pre-Painted Galvanized Iron) – 50 mm Glass Wool
	Wall Panel	0.45 mm sheet PPGI (Pre-Painted Galvanized Iron) – 50 mm Glass Wool
Accessories	Window	Nil
	Door	Nil
	Rainspout	MS Sheet
Live load on Roof		0.57 (kN/m2) (Color steel panel surrounded)

Live load on Frame	0.57 (kN/m2)
Wind Resistance (km/hr)	160 (Exposure C) / 140 km per hour
Seismic Zone	2-B
Structure Usage	Up to 50 years
Finishing Options	Vast array of colors and textures available
Paint Options	Alkyd painting, two primary painting, two finish painting (gray paint, red paint, white paint, epoxy zinc etc.) Or Galvanized.

3. Detailed Images




RELATED PRODUCTS




+92 322 8000 190 UAN: +923 111 749 849 info@acco.com.pk

Office 2nd, 3rd Floor, Bigcity Plaza, Gulberg-III, Lahore, Pakistan
www.acco.com.pk

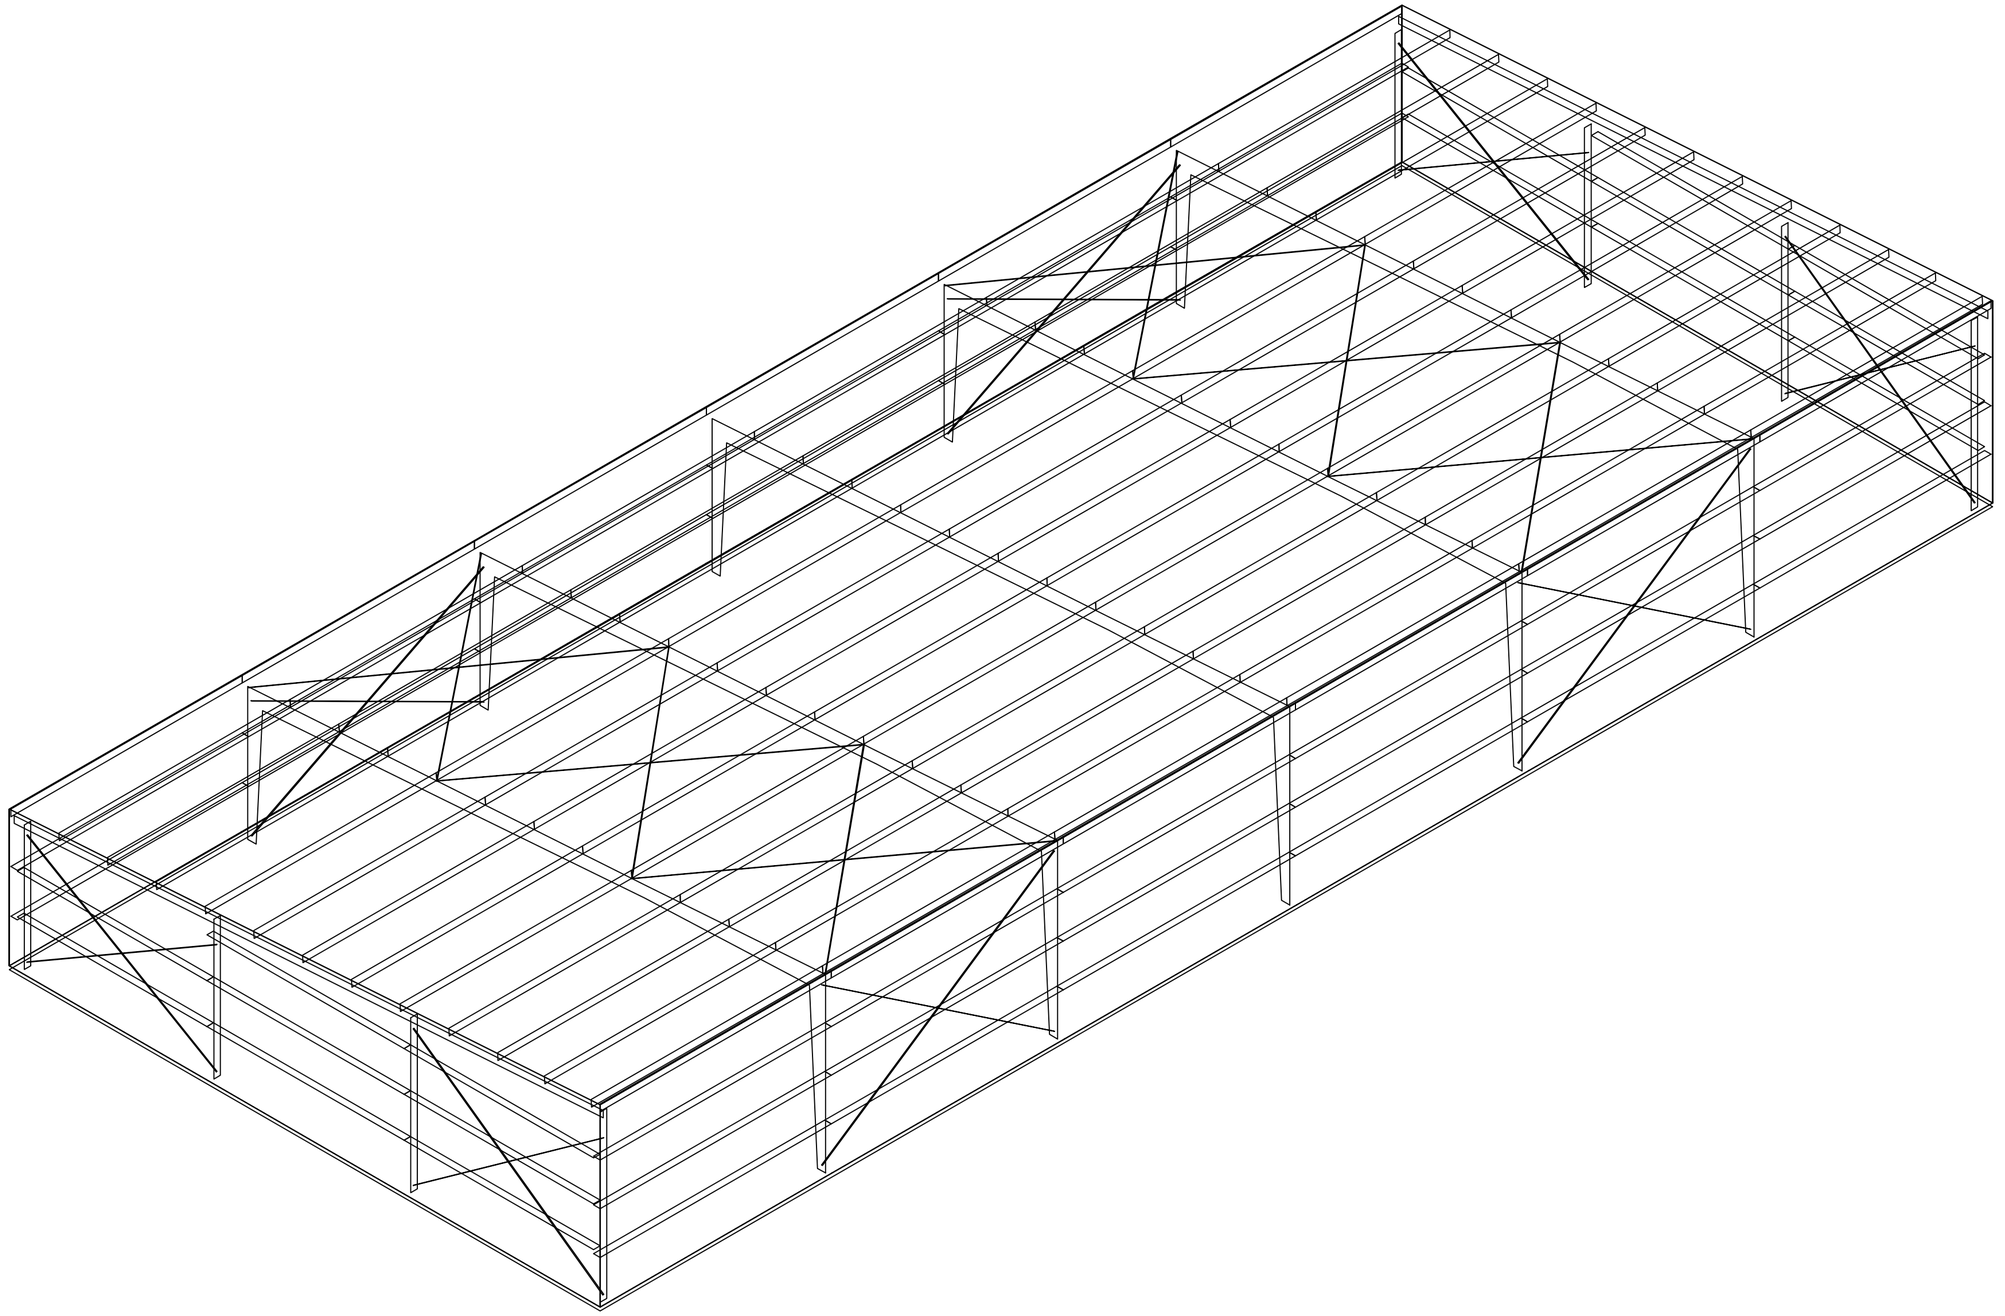

ARCHITECT ZUBAIR AHMED ZAFAR ALI	PROJECT MANAGER TANVEER AHMED	CLIENT _____	PROJECT CONSTRUCTION OF PRE-ENGINEERED SHED 141' X 59.5'	DRAWN MUHMMAD SAEED	ACCO ARCHITECTURE & CONSTRUCTION
ADDRESS _____	No. / ISSUED / DATE 1. PROPOSED DRAWING	CONSULTANT : AHMED CONSTRUCTION COMPANY OFFICE NO.2,3RD FLOOR BIG CITY PLAZA, GULBERG-iii,Lahore 0322-8000190	DRAWING 3D VIEW	PLOTTED DATE 26-November-2025 SCALE SCALED TO FIT	DWG. NO. 01

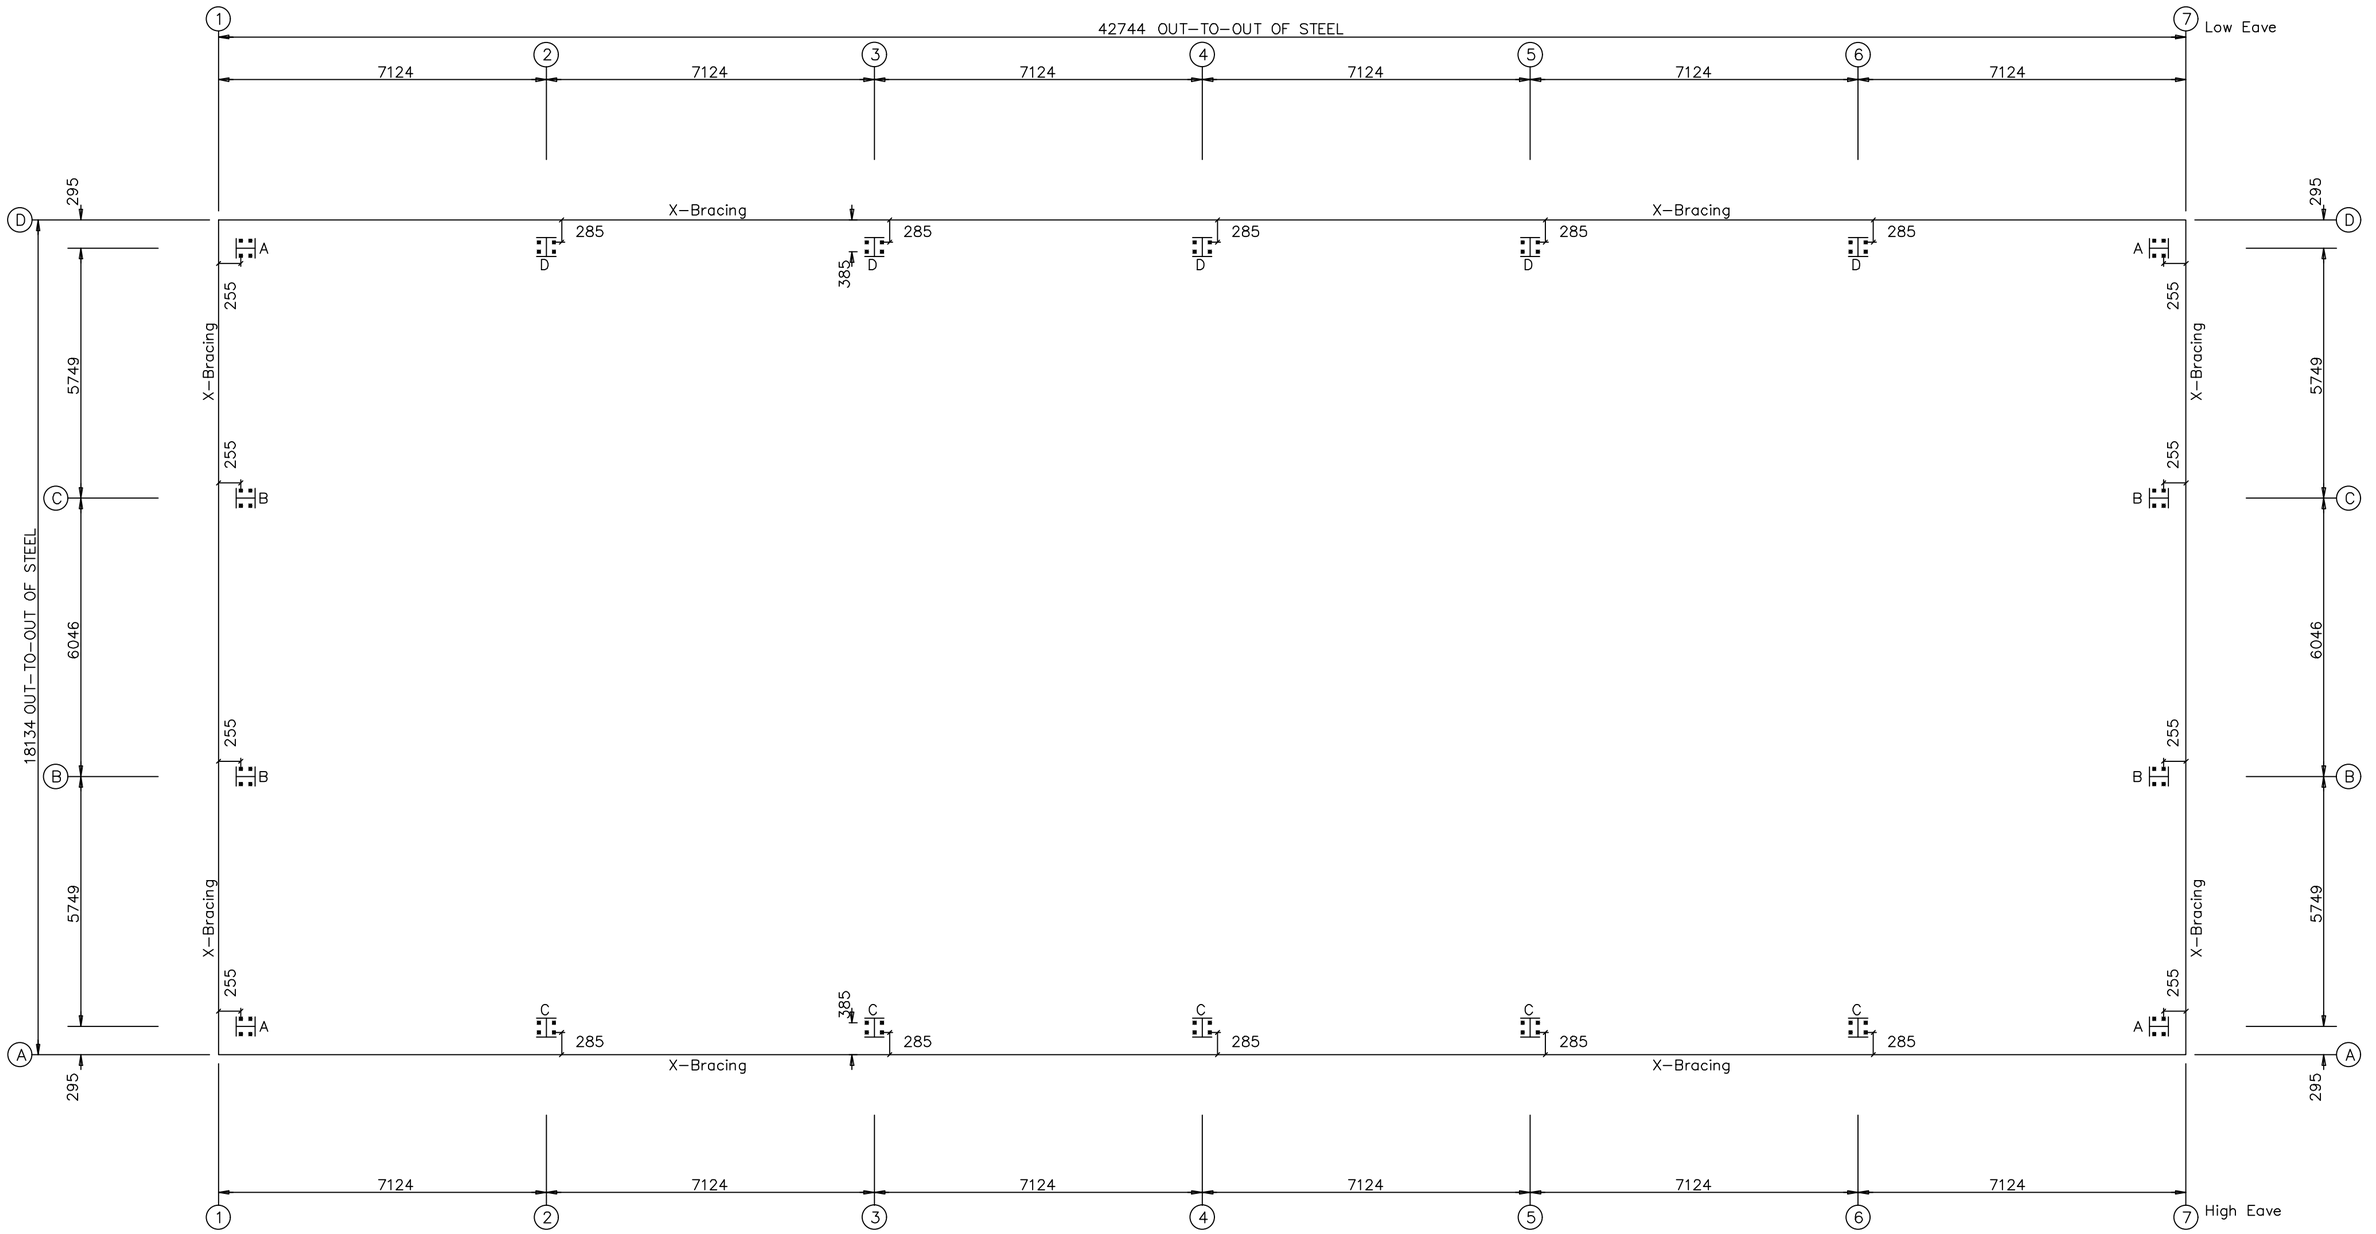


ANCHOR BOLT PLAN

NOTE: All Base Plates @ 0 (U.N.)

ARCHITECT ZUBAIR AHMED ZAFAR ALI	PROJECT MANAGER TANVEER AHMED	CLIENT _____	PROJECT CONSTRUCTION OF PRE-ENGINEERED SHED 141' X 59.5'
ADDRESS _____	No. / ISSUED / DATE 1. PROPOSED DRAWING	CONSULTANT : AHMED CONSTRUCTION COMPANY OFFICE NO.2,3RD FLOOR BIG CITY PLAZA, GULBERG-iii,Lahore 0322-8000190	DRAWING ANCHOR BOLT PLAN

DRAWN	MUHMMAD SAEED
PLOTTED DATE	26-November-2025
SCALE	SCALED TO FIT
DWG. NO.	02

ACCO
ARCHITECTURE & CONSTRUCTION

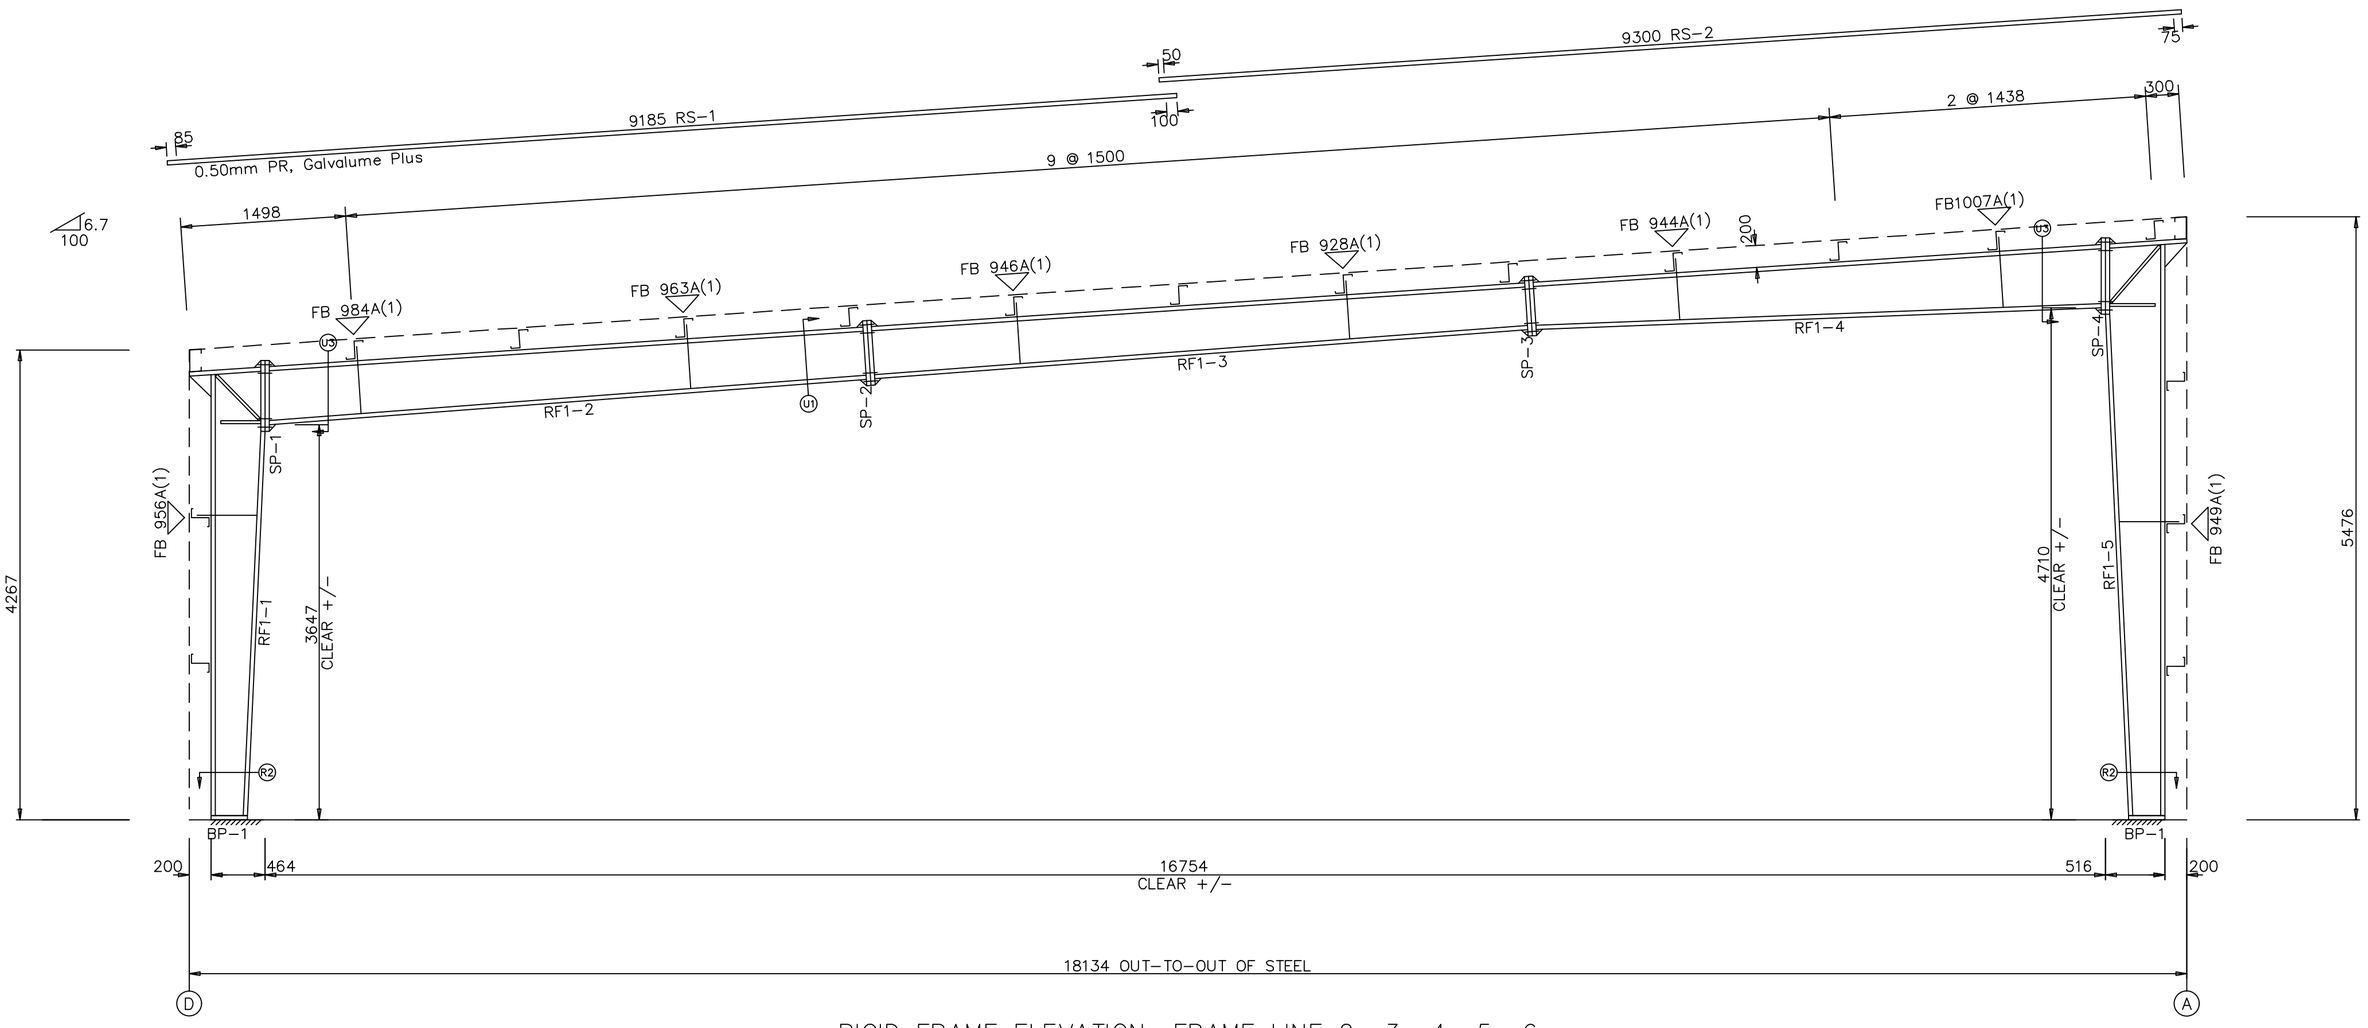


RIGID FRAME ELEVATION: FRAME LINE 2 3 4 5 6

ARCHITECT ZUBAIR AHMED ZAFAR ALI	PROJECT MANAGER TANVEER AHMED	CLIENT _____	PROJECT CONSTRUCTION OF PRE-ENGINEERED SHED 141' X 59.5'
ADDRESS _____	No. / ISSUED / DATE 1. PROPOSED DRAWING	CONSULTANT : AHMED CONSTRUCTION COMPANY OFFICE NO.2,3RD FLOOR BIG CITY PLAZA, GULBERG-iii,Lahore 0322-8000190	DRAWING RIGID FRAME ELEVATION

DRAWN	MUHMMAD SAEED
PLOTTED DATE	26-November-2025
SCALE	SCALED TO FIT
DWG. NO.	03

ACCO
ARCHITECTURE & CONSTRUCTION

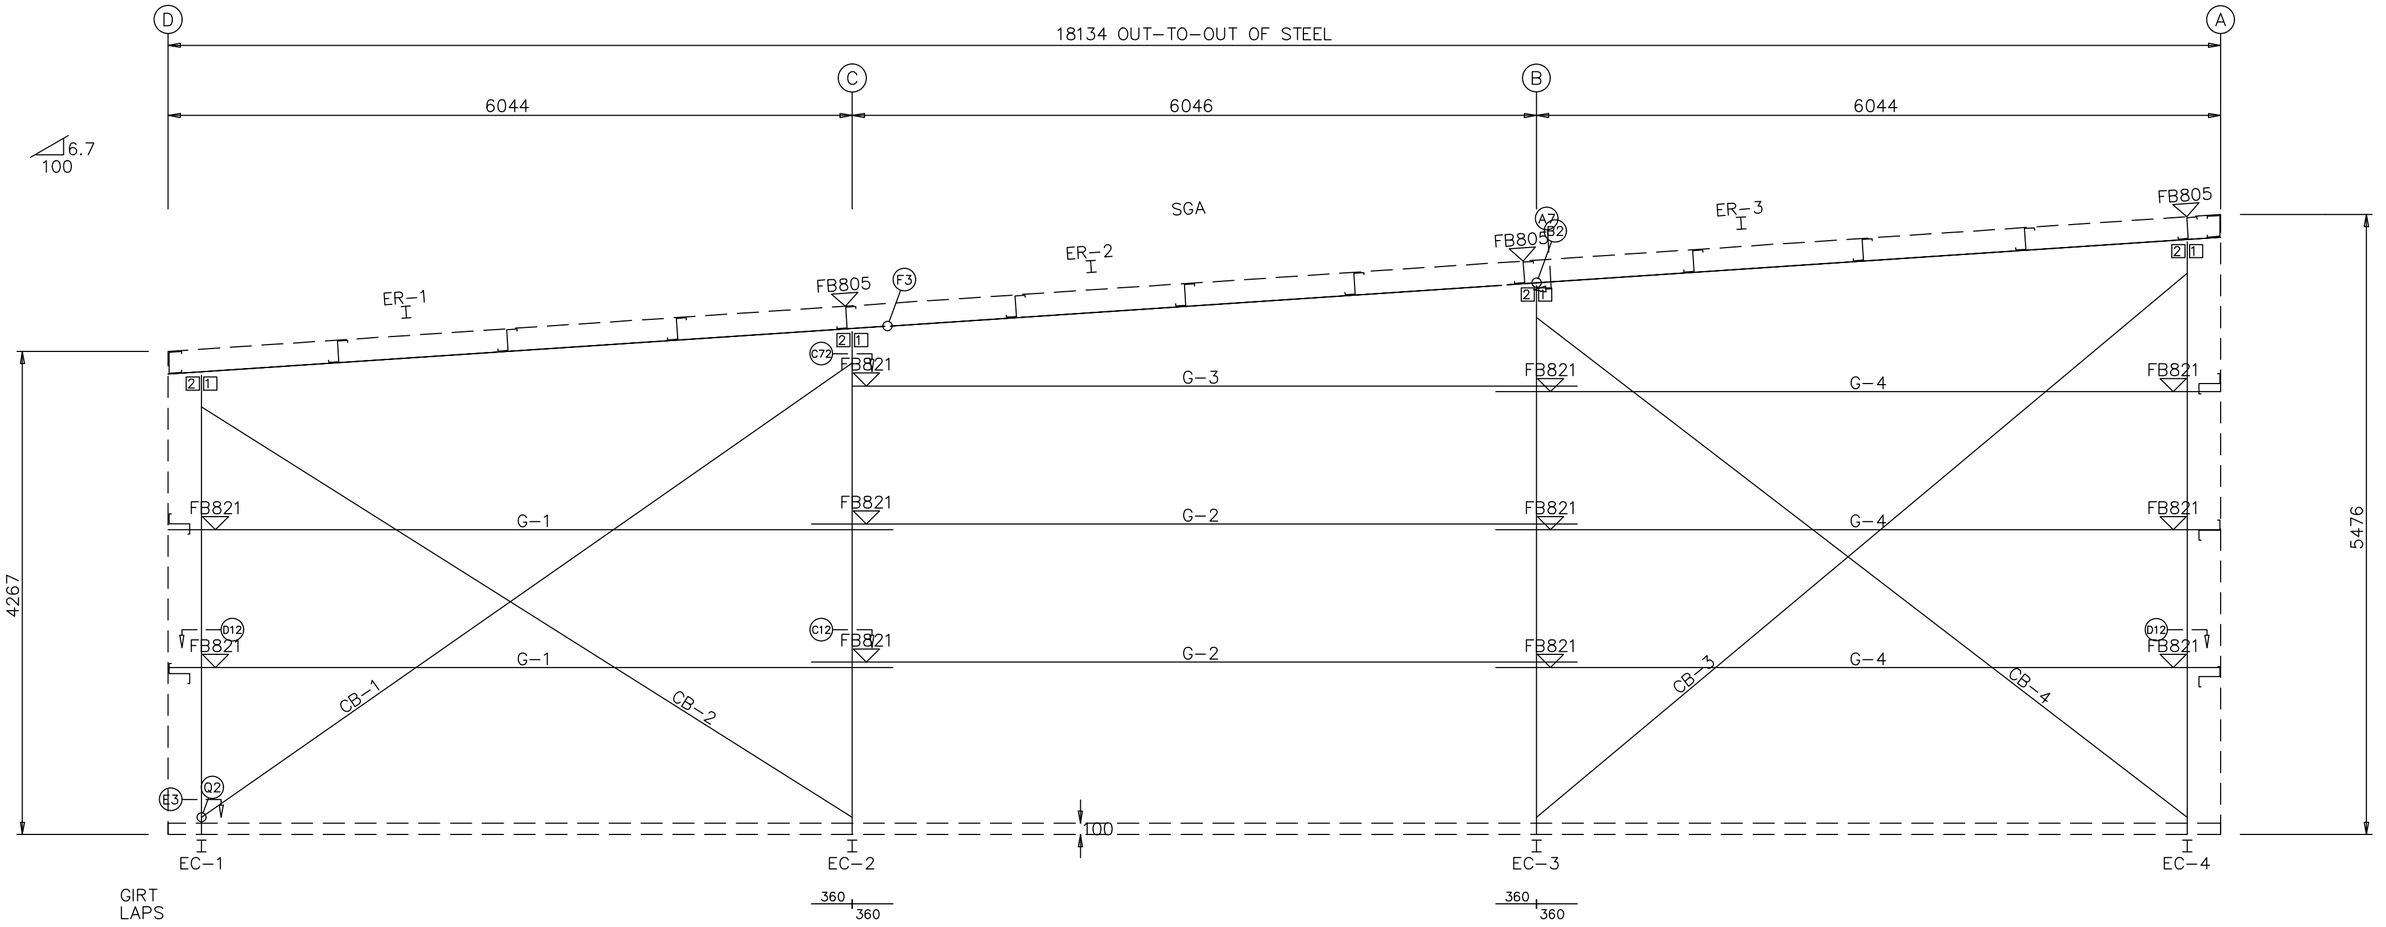


ENDWALL FRAMING: FRAME LINE 1

ARCHITECT ZUBAIR AHMED ZAFAR ALI	PROJECT MANAGER TANVEER AHMED	CLIENT _____	PROJECT CONSTRUCTION OF PRE-ENGINEERED SHED 141' X 59.5'
ADDRESS _____	No. / ISSUED / DATE 1. PROPOSED DRAWING	CONSULTANT : AHMED CONSTRUCTION COMPANY OFFICE NO.2,3RD FLOOR BIG CITY PLAZA, GULBERG-iii,Lahore 0322-8000190	DRAWING END WALL FRAMING

DRAWN	MUHMMAD SAEED
PLOTTED DATE	26-November-2025
SCALE	SCALED TO FIT
DWG. NO.	04


ACCO
ARCHITECTURE & CONSTRUCTION

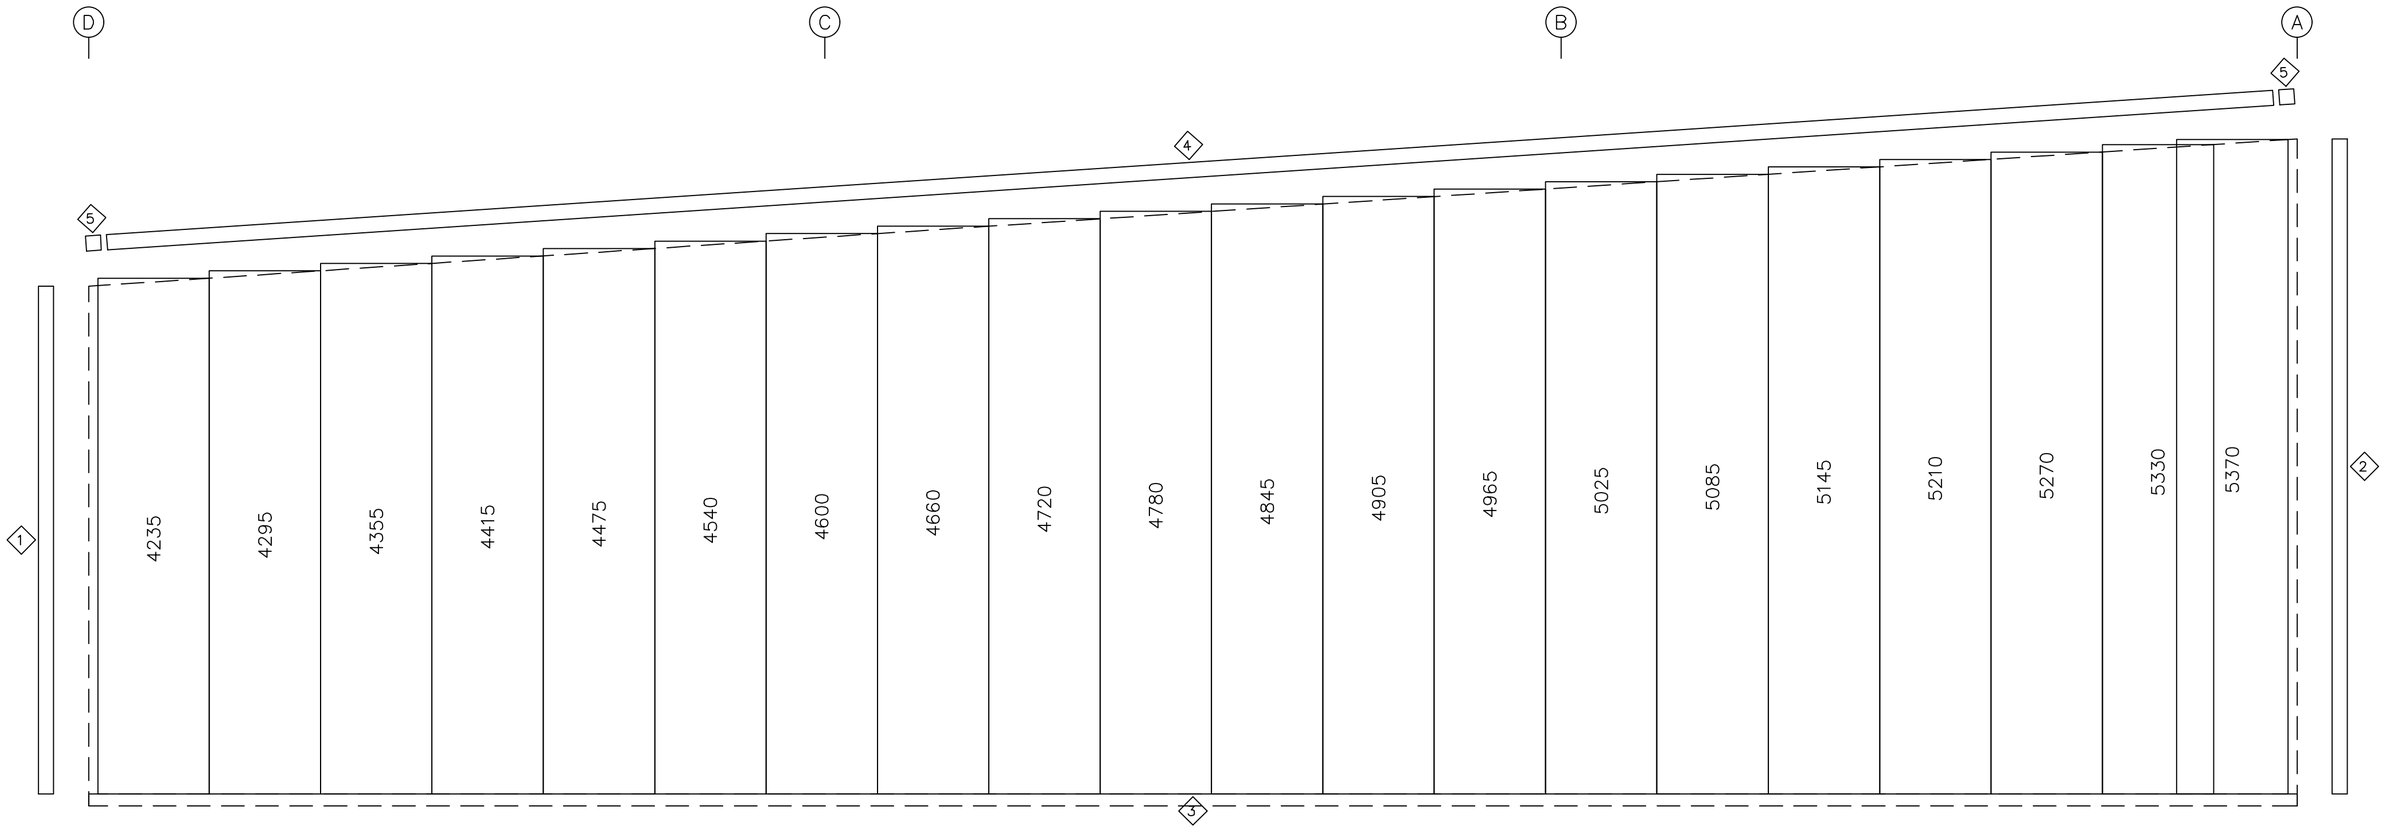

ENDWALL SHEETING & TRIM: FRAME LINE 1

PANELS: 0.50mm PR – Beige RAL1001

ARCHITECT ZUBAIR AHMED ZAFAR ALI	PROJECT MANAGER TANVEER AHMED	CLIENT _____	PROJECT CONSTRUCTION OF PRE-ENGINEERED SHED 141' X 59.5'	DRAWN MUHMMAD SAEED	ACCO ARCHITECTURE & CONSTRUCTION
ADDRESS _____	No. / ISSUED / DATE 1. PROPOSED DRAWING	CONSULTANT : AHMED CONSTRUCTION COMPANY OFFICE NO.2,3RD FLOOR BIG CITY PLAZA, GULBERG-iii,Lahore 0322-8000190	DRAWING ENDWALL SHEETING & TRIM	PLOTTED DATE 26-November-2025 SCALE SCALED TO FIT	DWG. NO. 05

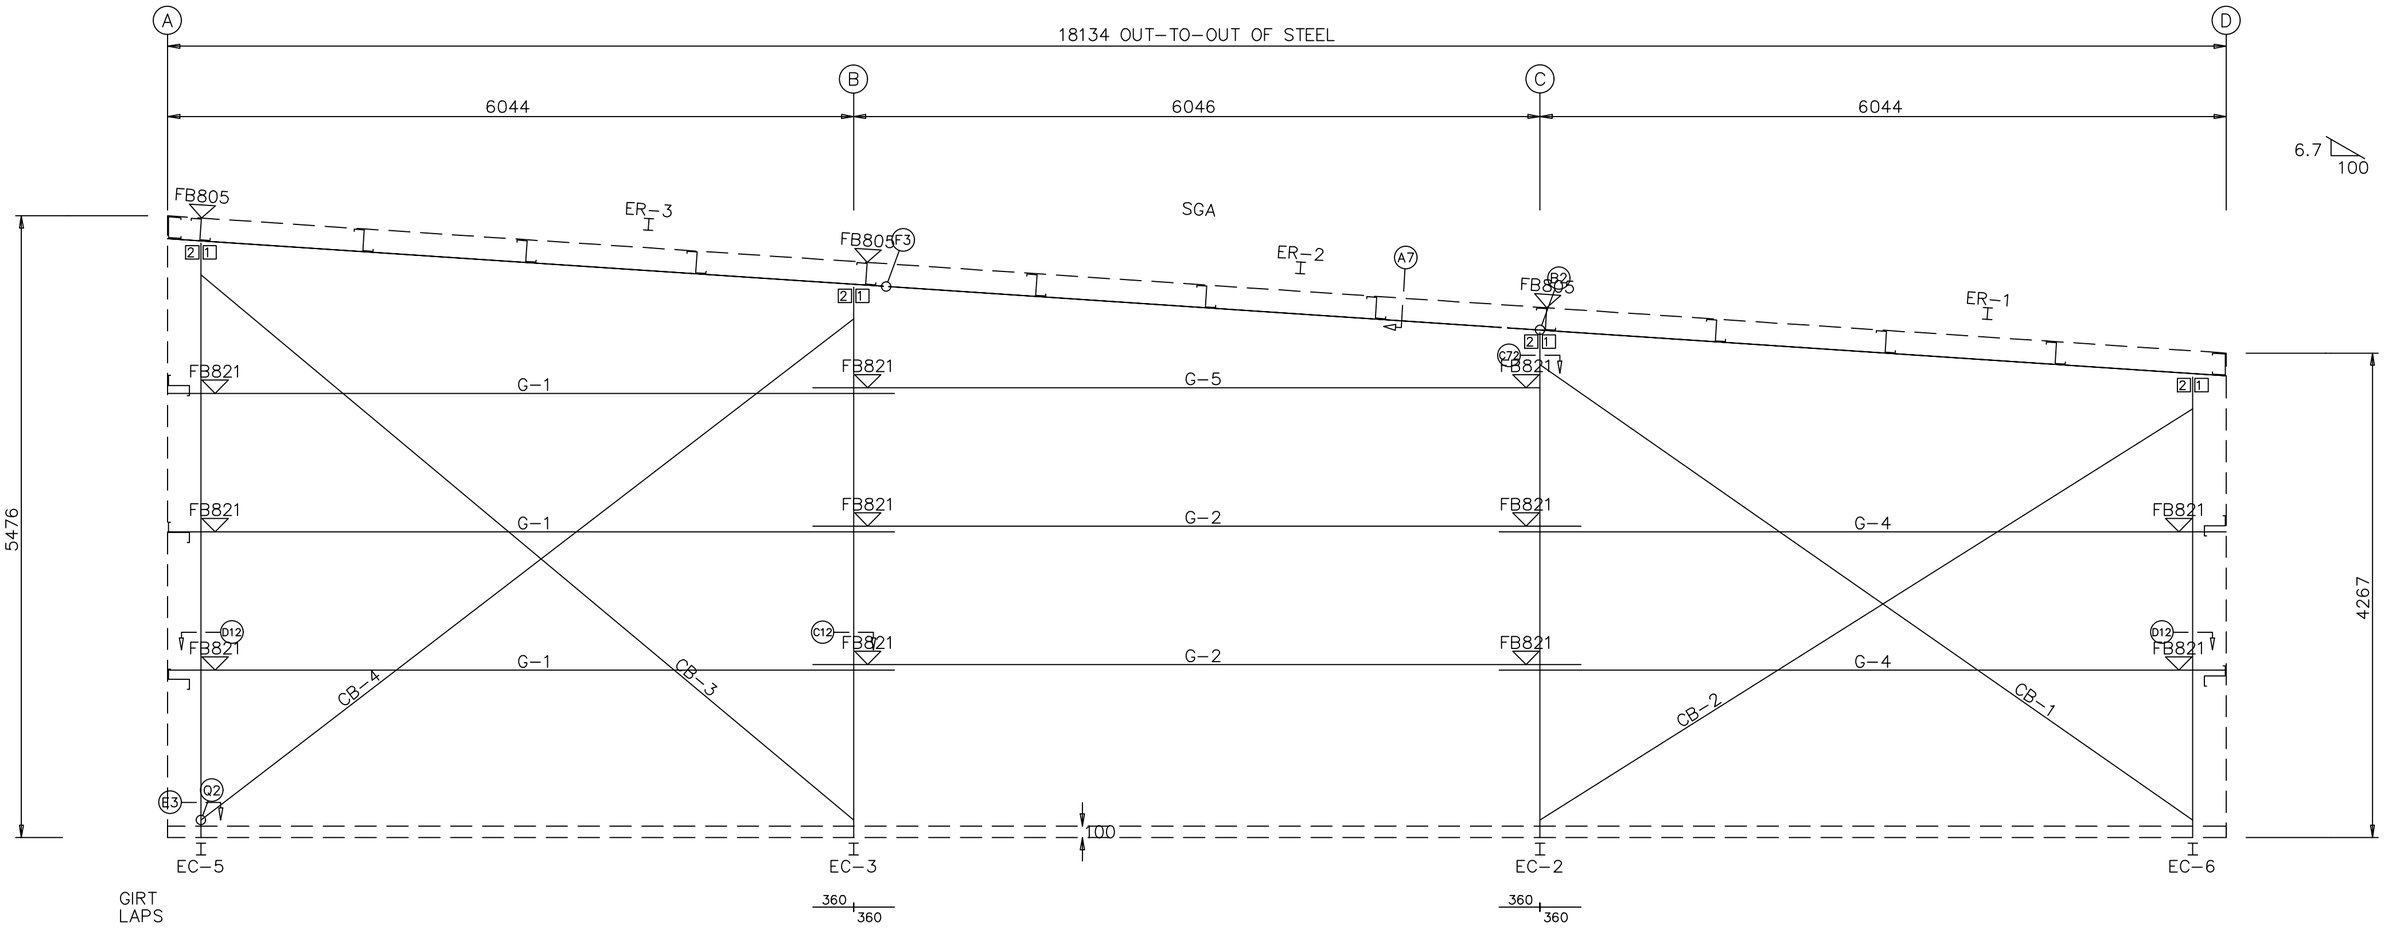


ENDWALL FRAMING: FRAME LINE 7

ARCHITECT ZUBAIR AHMED ZAFAR ALI	PROJECT MANAGER TANVEER AHMED	CLIENT _____	PROJECT CONSTRUCTION OF PRE-ENGINEERED SHED 141' X 59.5'
ADDRESS _____	No. / ISSUED / DATE 1. PROPOSED DRAWING	CONSULTANT : AHMED CONSTRUCTION COMPANY OFFICE NO.2,3RD FLOOR BIG CITY PLAZA, GULBERG-iii,Lahore 0322-8000190	DRAWING ENDWALL FRAMING

DRAWN	MUHMMAD SAEED
PLOTTED DATE	26-November-2025
SCALE	SCALED TO FIT
DWG. NO.	06


ACCO
ARCHITECTURE & CONSTRUCTION

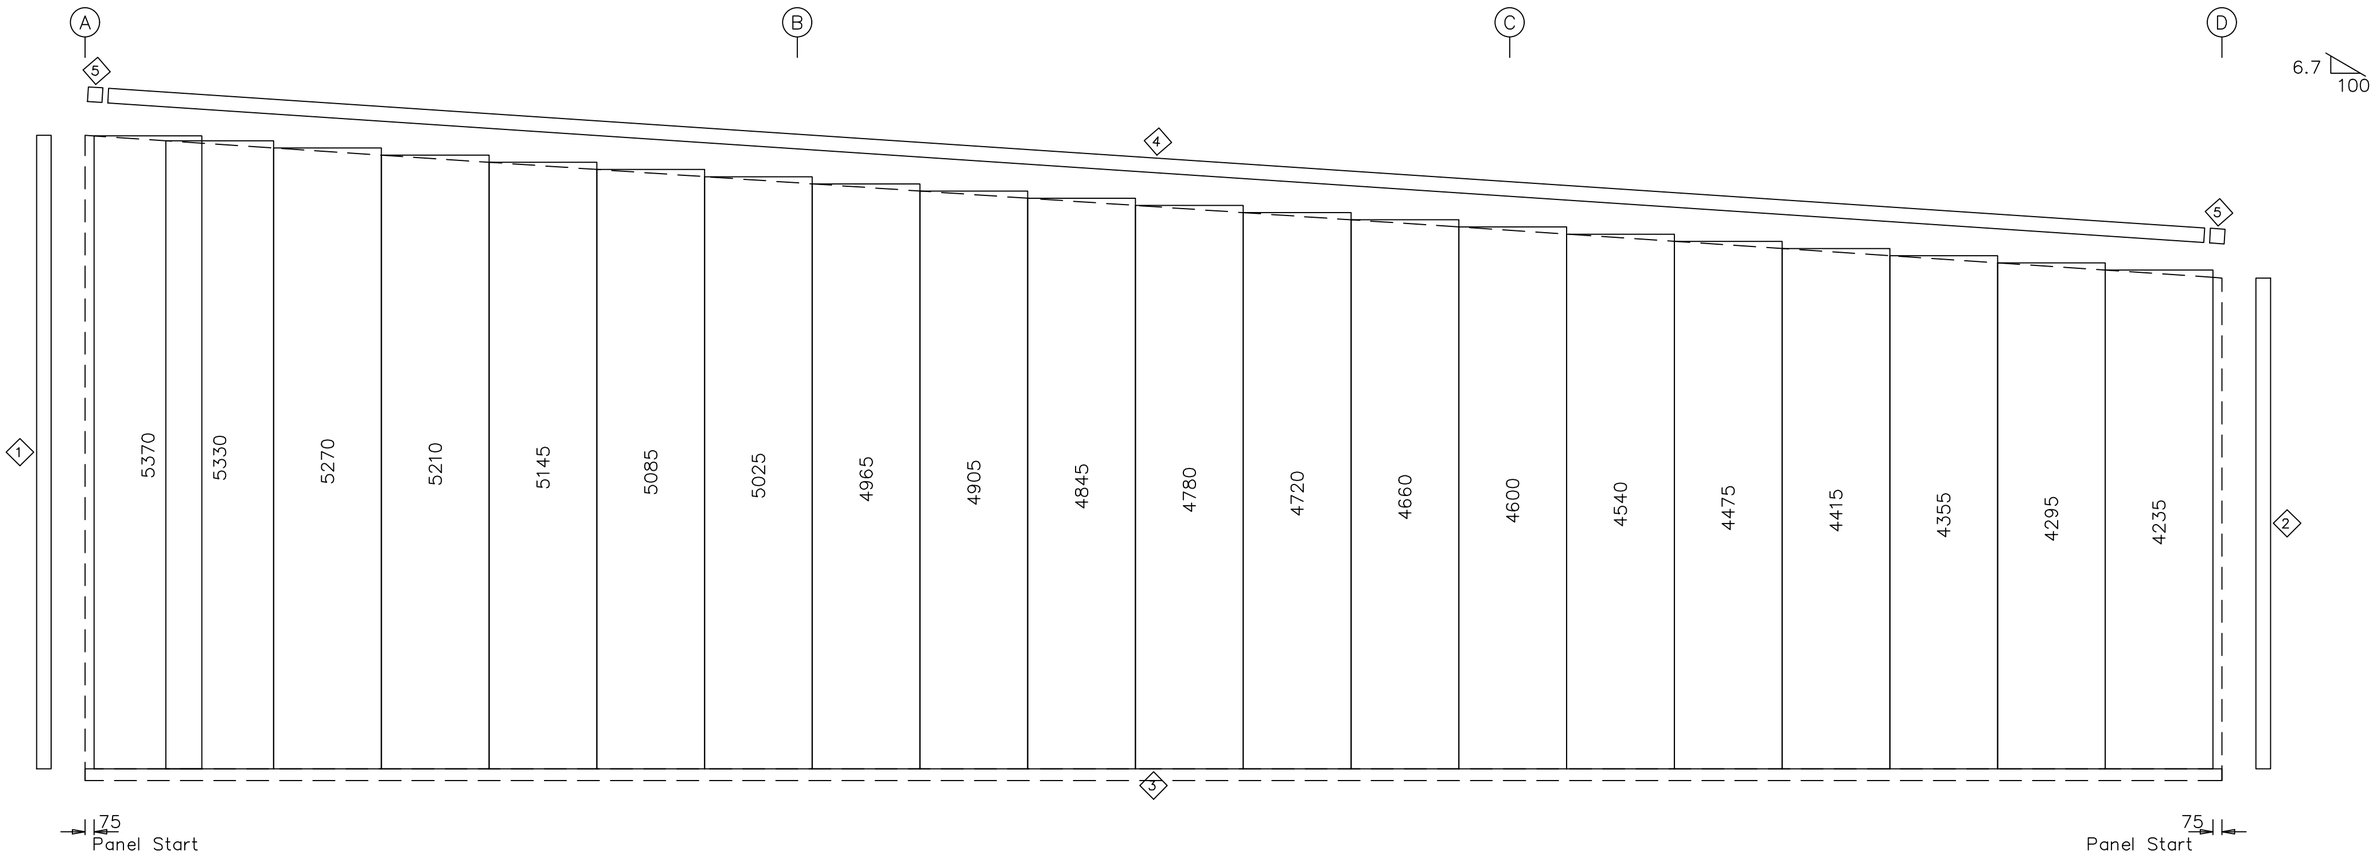

ENDWALL SHEETING & TRIM: FRAME LINE 7

PANELS: 0.50mm PR – Beige RAL1001

ARCHITECT ZUBAIR AHMED ZAFAR ALI	PROJECT MANAGER TANVEER AHMED	CLIENT _____	PROJECT CONSTRUCTION OF PRE-ENGINEERED SHED 141' X 59.5'	DRAWN MUHMMAD SAEED	ACCO ARCHITECTURE & CONSTRUCTION
ADDRESS _____	No. / ISSUED / DATE 1. PROPOSED DRAWING	CONSULTANT : AHMED CONSTRUCTION COMPANY OFFICE NO.2,3RD FLOOR BIG CITY PLAZA, GULBERG-iii,Lahore 0322-8000190	DRAWING ENDWALL SHEETING & TRIM	PLOTTED DATE 26-November-2025 SCALE SCALED TO FIT	DWG. NO. 07

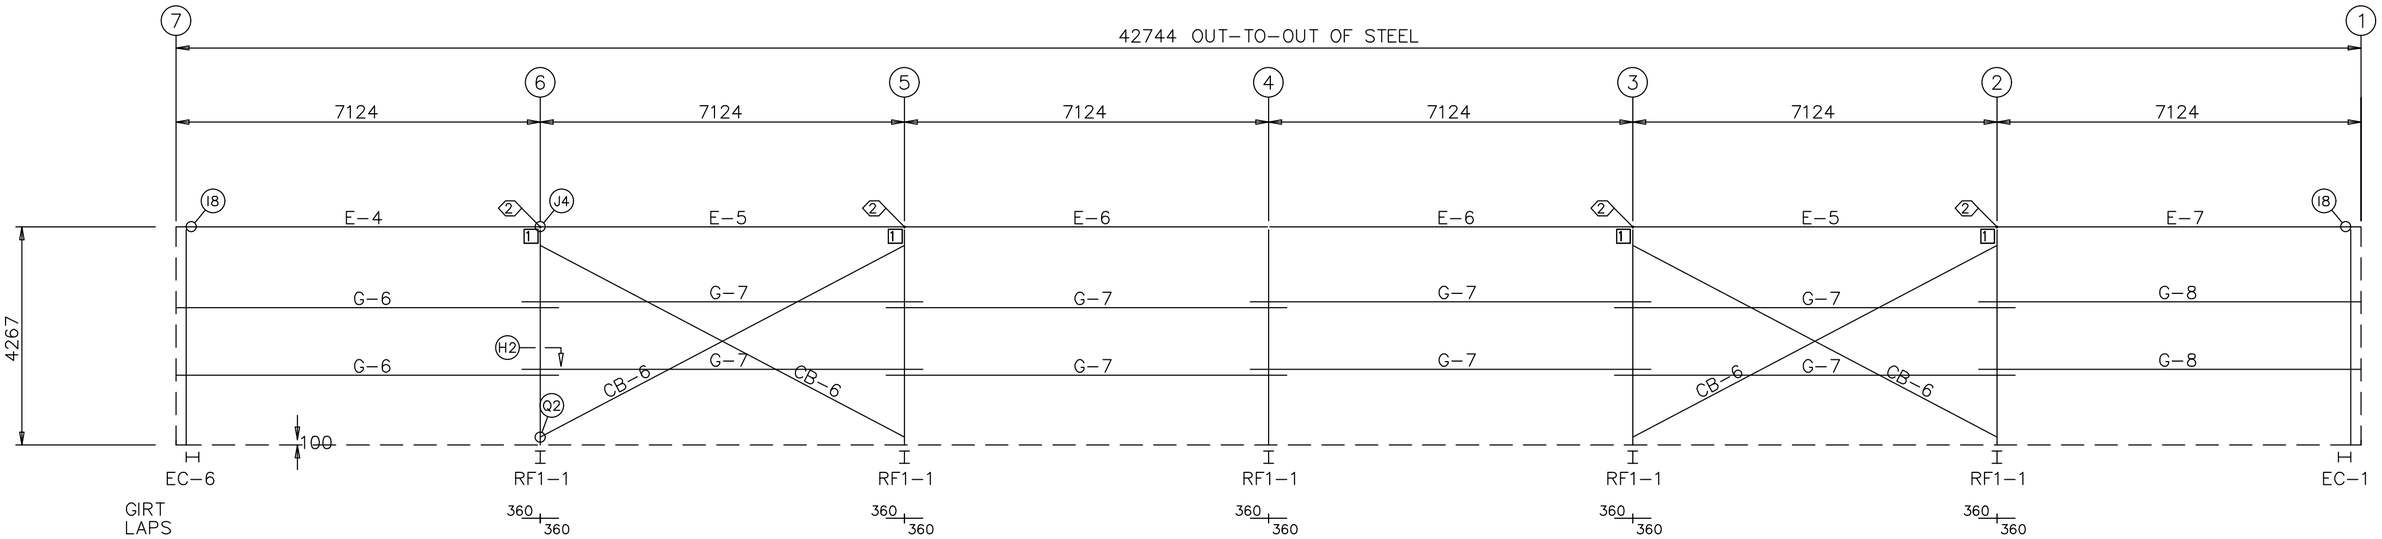


SIDEWALL FRAMING: FRAME LINE D

ARCHITECT ZUBAIR AHMED ZAFAR ALI	PROJECT MANAGER TANVEER AHMED	CLIENT _____	PROJECT CONSTRUCTION OF PRE-ENGINEERED SHED 141' X 59.5'
ADDRESS _____	No. / ISSUED / DATE 1. PROPOSED DRAWING	CONSULTANT : AHMED CONSTRUCTION COMPANY OFFICE NO.2,3RD FLOOR BIG CITY PLAZA, GULBERG-iii,Lahore 0322-8000190	DRAWING SIDEWALL FRAMING

DRAWN	MUHMMAD SAEED
PLOTTED DATE	26-November-2025
SCALE	SCALED TO FIT
DWG. NO.	08

ACCO
ARCHITECTURE & CONSTRUCTION

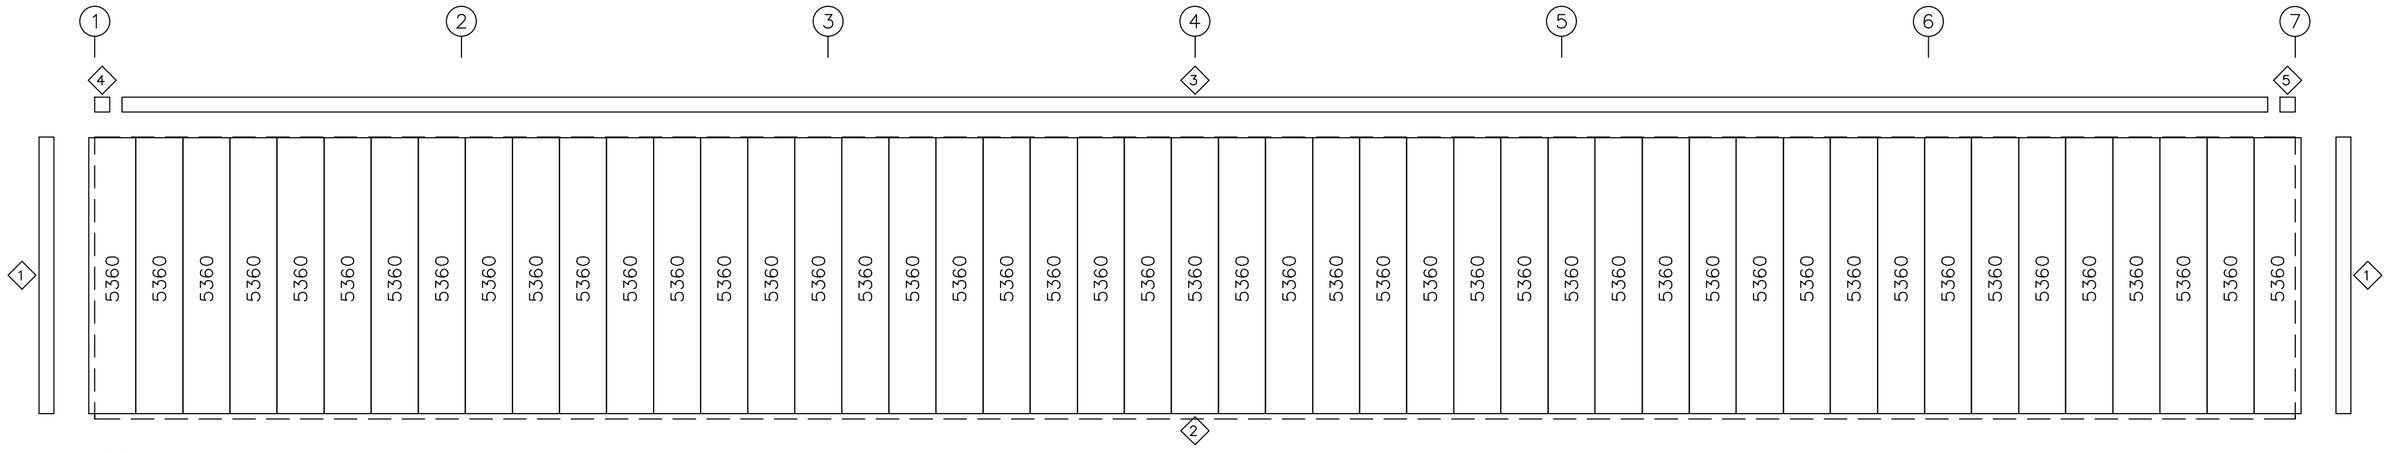


SIDEWALL SHEETING & TRIM: FRAME LINE A

PANELS: 0.50mm PR – Beige RAL1001

ARCHITECT: ZUBAIR AHMED, ZAFAR ALI	PROJECT MANAGER: TANVEER AHMED	CLIENT: _____
ADDRESS: _____	CONSULTANT : AHMED CONSTRUCTION COMPANY, OFFICE NO.2,3RD FLOOR BIG CITY PLAZA, GULBERG-iii,Lahore 0322-8000190	PROJECT: CONSTRUCTION OF PRE-ENGINEERED SHED 141' X 59.5'
	DRAWING: SIDEWALL SHEETING & TRIM	DRAWN: MUHMMAD SAEED
		PLOTTED DATE: 26-November-2025
		SCALE: SCALED TO FIT
		ACCO ARCHITECTURE & CONSTRUCTION
		DWG. NO. 09

No.	ISSUED	DATE
1.	PROPOSED DRAWING	

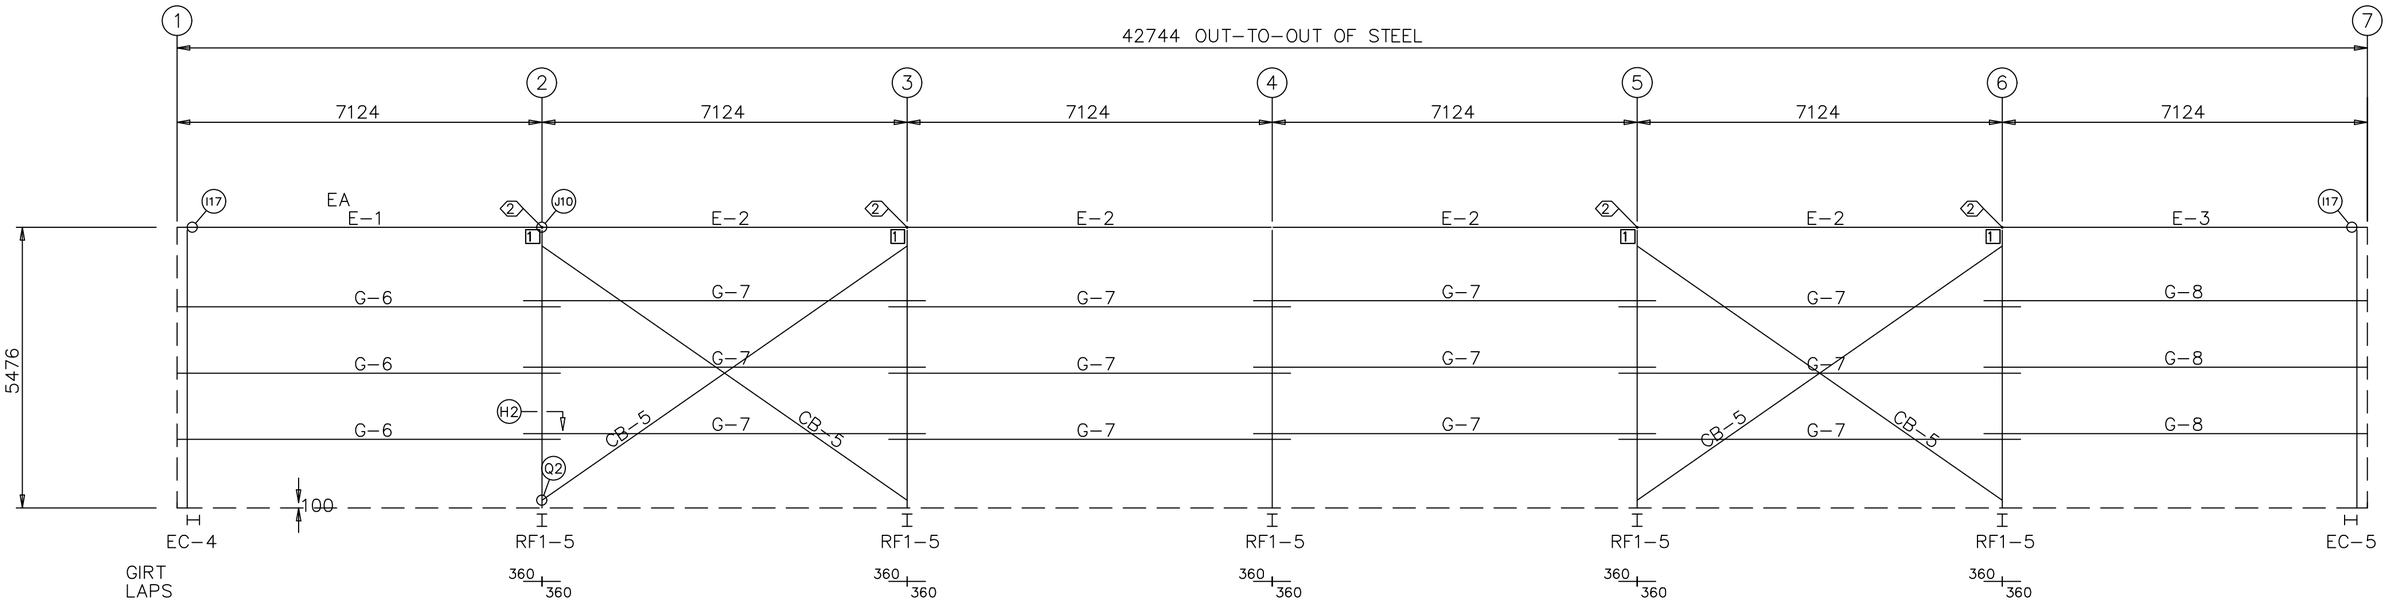


SIDEWALL FRAMING: FRAME LINE A

ARCHITECT ZUBAIR AHMED ZAFAR ALI	PROJECT MANAGER TANVEER AHMED	CLIENT _____	PROJECT CONSTRUCTION OF PRE-ENGINEERED SHED 141' X 59.5'
ADDRESS _____	No. / ISSUED / DATE 1. PROPOSED DRAWING	CONSULTANT : AHMED CONSTRUCTION COMPANY OFFICE NO.2,3RD FLOOR BIG CITY PLAZA, GULBERG-iii,Lahore 0322-8000190	DRAWING SIDEWALL FRAMING

DRAWN	MUHMMAD SAEED
PLOTTED DATE	26-November-2025
SCALE	SCALED TO FIT
DWG. NO.	10

ACCO
ARCHITECTURE & CONSTRUCTION

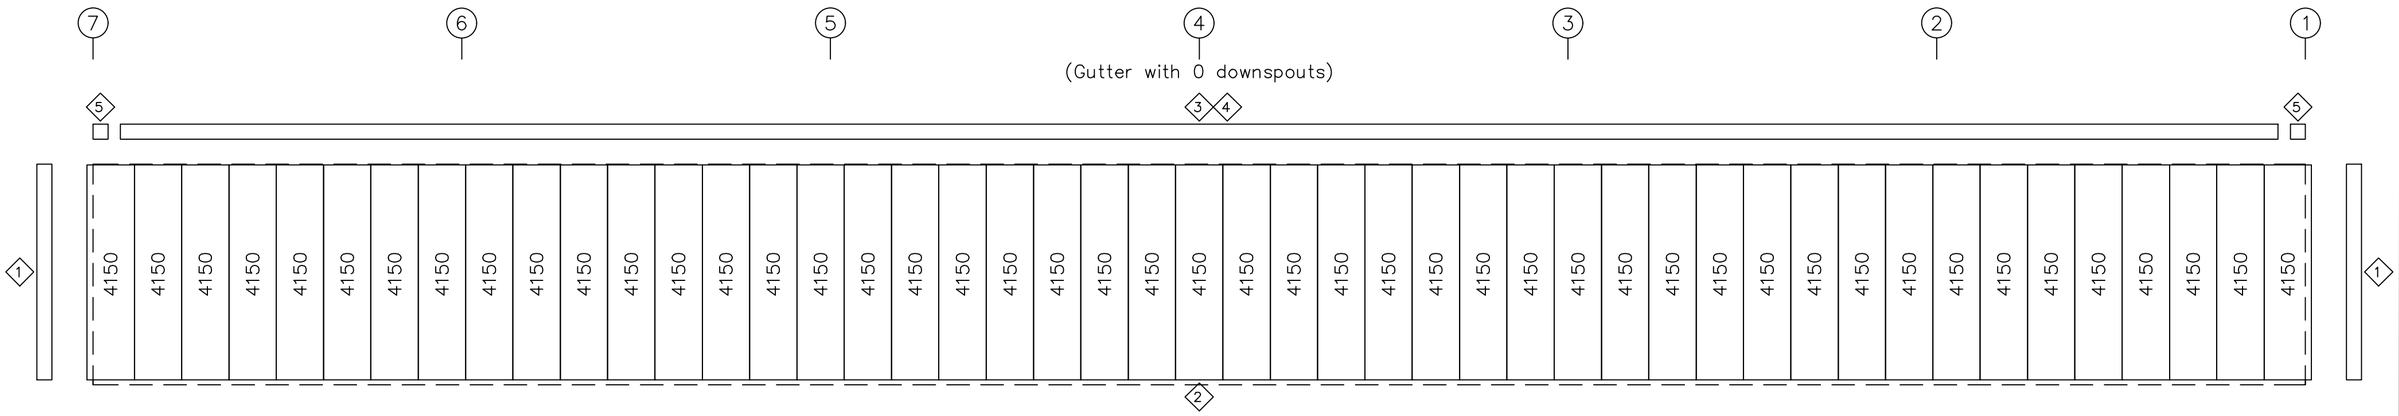


SIDEWALL SHEETING & TRIM: FRAME LINE D

PANELS: 0.50mm PR – Beige RAL1001

ARCHITECT: ZUBAIR AHMED, ZAFAR ALI	PROJECT MANAGER: TANVEER AHMED	CLIENT: _____
ADDRESS: _____	CONSULTANT : AHMED CONSTRUCTION COMPANY, OFFICE NO.2,3RD FLOOR BIG CITY PLAZA, GULBERG-iii,Lahore 0322-8000190	PROJECT: CONSTRUCTION OF PRE-ENGINEERED SHED 141' X 59.5'
	DRAWING: SIDEWALL SHEETING & TRIM	DRAWN: MUHMMAD SAEED
		PLOTTED DATE: 26-November-2025
		SCALE: SCALED TO FIT
		ACCO ARCHITECTURE & CONSTRUCTION
		DWG. NO. 11

No.	ISSUED	DATE
1.	PROPOSED DRAWING	

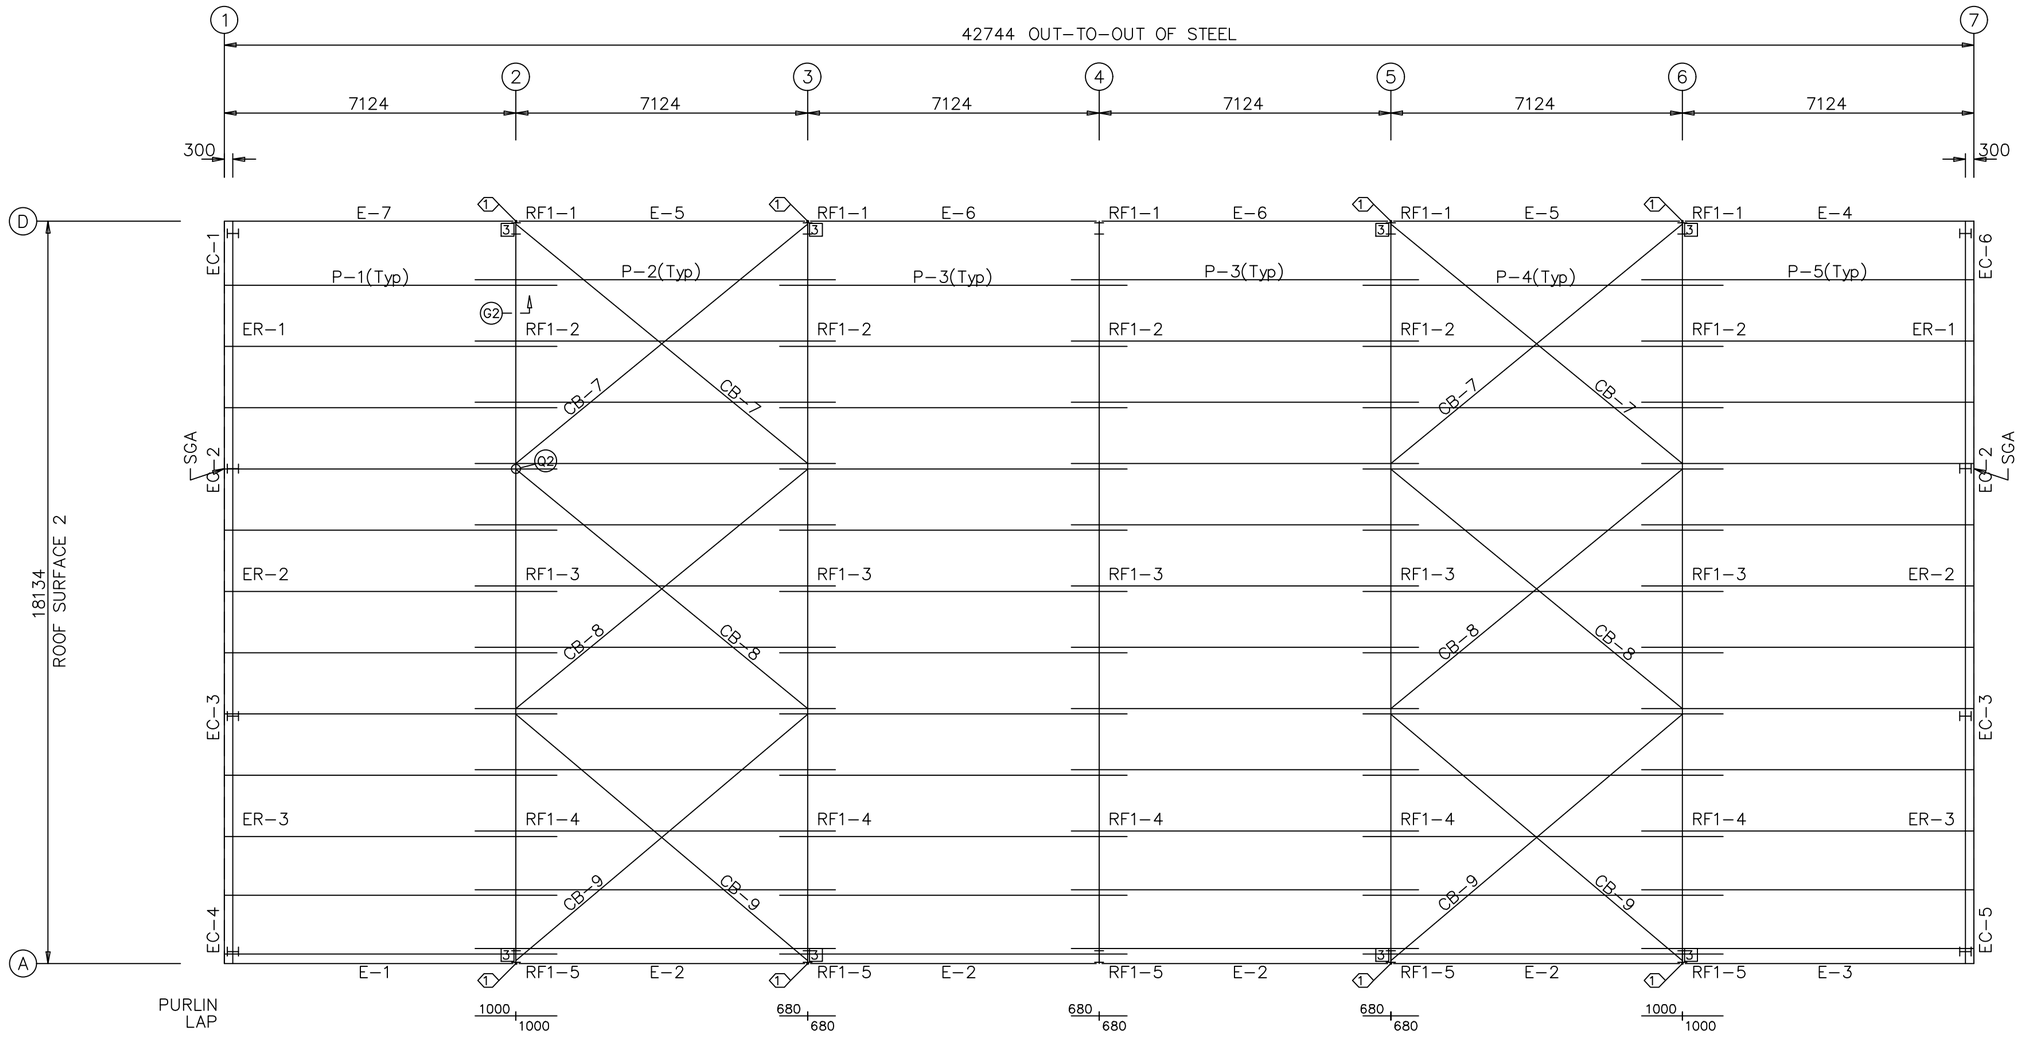

ROOF FRAMING PLAN

ROOF SHEETING

PANELS: 0.50mm PR Galvalume Plus

ARCHITECT: ZUBAIR AHMED, ZAFAR ALI	PROJECT MANAGER: TANVEER AHMED	CLIENT: _____	PROJECT: CONSTRUCTION OF PRE-ENGINEERED SHED 141' X 59.5'
ADDRESS: _____	CONSULTANT : AHMED CONSTRUCTION COMPANY, OFFICE NO.2,3RD FLOOR BIG CITY PLAZA, GULBERG-iii,Lahore 0322-8000190		DRAWING: ROOF FRAMING PLAN

No.	ISSUED	DATE
1.	PROPOSED DRAWING	


DRAWN: MUHMMAD SAEED

PLOTTED DATE: 26-November-2025

SCALE: SCALED TO FIT

ACCO
ARCHITECTURE & CONSTRUCTION

DWG. NO. 12

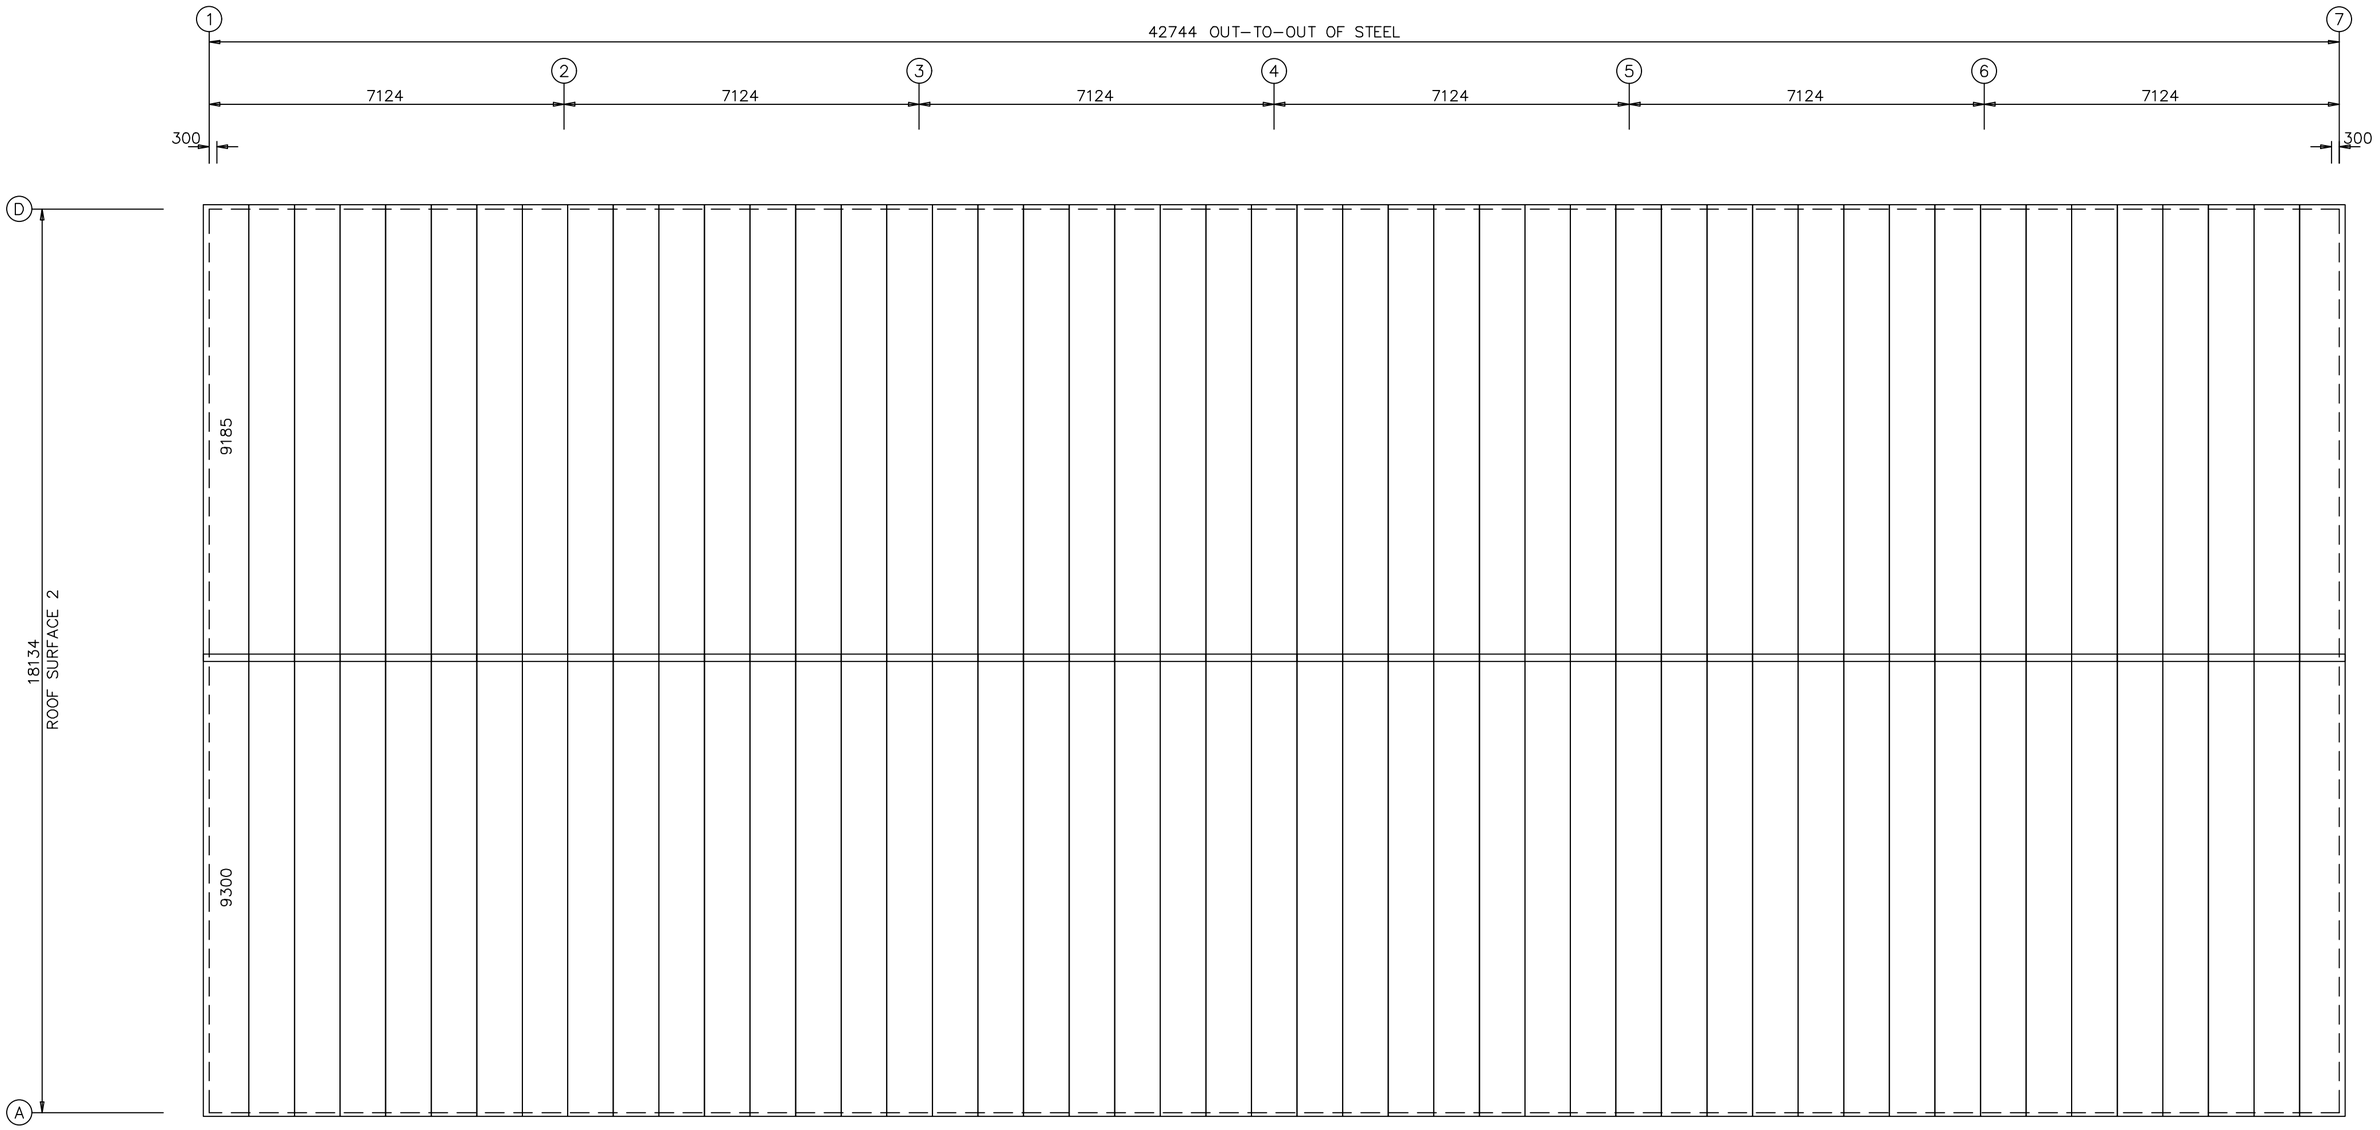

ROOF SHEETING PLAN

PANELS: 0.50mm PR – Galvalume Plus

ARCHITECT ZUBAIR AHMED ZAFAR ALI	PROJECT MANAGER TANVEER AHMED	CLIENT _____	PROJECT CONSTRUCTION OF PRE-ENGINEERED SHED 141' X 59.5'	DRAWN MUHMMAD SAEED	ACCO ARCHITECTURE & CONSTRUCTION
ADDRESS _____	No. / ISSUED / DATE 1. PROPOSED DRAWING	CONSULTANT : AHMED CONSTRUCTION COMPANY OFFICE NO.2,3RD FLOOR BIG CITY PLAZA, GULBERG-iii,Lahore 0322-8000190	DRAWING ROOF SHEETING PLAN	PLOTTED DATE 26-November-2025 SCALE SCALED TO FIT	DWG. NO. 13
