To,
Mr. Almas Ambreen Sahab
Lahore, Pakistan

Date: December 03, 2025
Ref#: ACCO/PEB/1081

SUBJECT: - **QUOTATION FOR CONSTRUCTION OF PRE-ENGINEERED FLOOR BUILDING IN LAHORE**

السلام علیکم
We are pleased to submit our best quote for subject work as follows: -

Sr.#	Item Description	Area (MTR)	Rate (Rs.)	Amount
1	Construction, supply and installation of a prefabricated steel structure shed for **Fuel** Complete in all respect. Wall: 5 Meter sheet wall after 3 Meter Brick Wall Height Approx. 8 Meter	4,000	10,760/-	43,040,000/-
2	Construction, supply and installation of a prefabricated steel structure shed for **Boiler** Complete in all respect. Height Approx. 16 Meter	1,000	17,431/-	60,471,000/-
	Total Amount			**6,928,000/-**

Terms & Conditions:


1. This quotation excludes all taxes.
2. Complication Time 45 days
3. 50% Advance before starting the Project, 35% on material on site and remaining 15% on completion.
4. Provision of storage facilities for our goods and equipment, where necessary, shall be client responsibility.
5. Electricity & water supply will be provided by the client.
6. This quotation is valid for 30 days from above mentioned date.
7. Civil Work is not included.

We will be obliged for your cooperation in this regard.
Thanks & Regards.
Truly yours,

Tanveer Ahmed
Director
+92-322-8000190

Product description

1. Building System

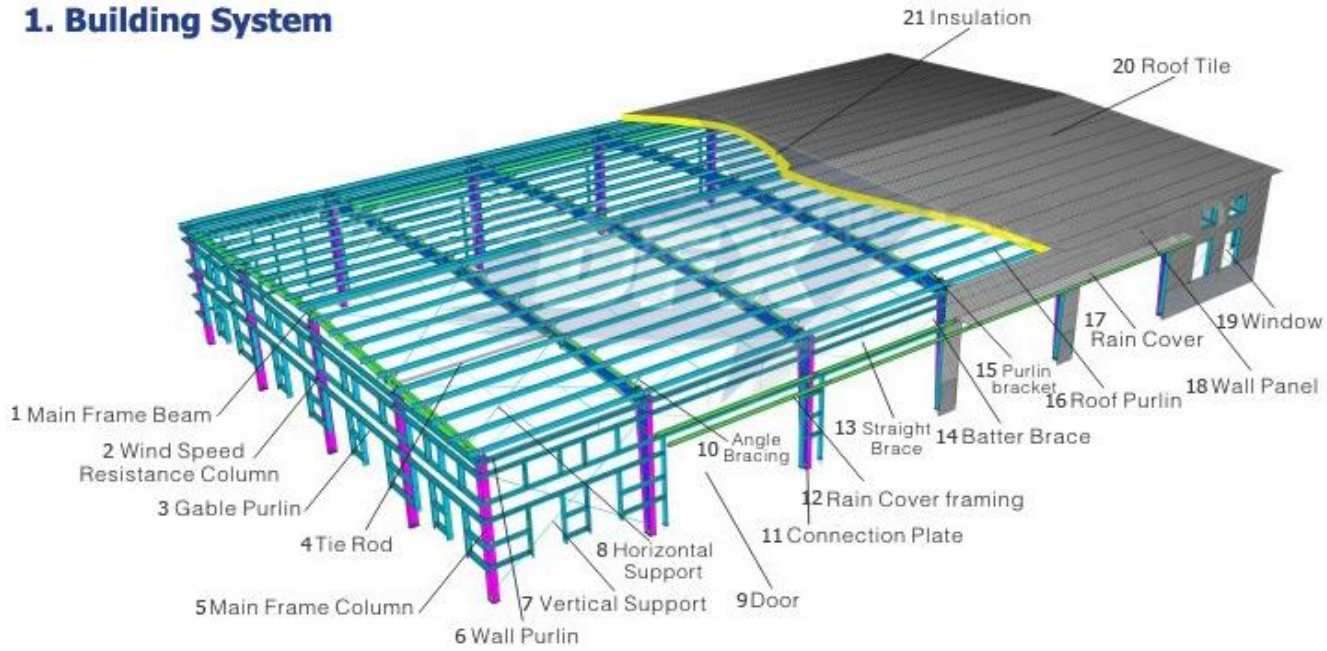

2. Specification

Items		Specification
Main Steel Frame	Column	5 mm and 6 mm
	Beam	5 mm and 6 mm
Secondary Frame	Purlin	1.5 mm
	Knee brace	12 mm
	Tie Rod	50 mm x 50 mm angle
	Brace	Sag Rod
	Vertical and Horizontal Support	Q235 Angle Steel, Round Bar or Steel Pipe
Maintenance system	Roof Panel	0.45 mm sheet PPGI (Pre-Painted Galvanized Iron)
	Wall Panel	0.45 mm sheet PPGI (Pre-Painted Galvanized Iron)
Accessories	Window	Nil
	Door	Nil
	Rainspout	MS Sheet
Live load on Roof		0.57 (kN/m2) (Color steel panel surrounded)
Live load on Frame		0.57 (kN/m2)

Wind Resistance (km/hr)	160 (Exposure C) / 140 km per hour
Seismic Zone	2-B
Structure Usage	Up to 50 years
Finishing Options	Vast array of colors and textures available
Paint Options	Alkyd painting, two primary painting, two finish painting (gray paint, red paint, white paint, epoxy zinc etc.) Or Galvanized.

3. Detailed Images



RELATED PRODUCTS



+92 322 8000 190 UAN: +923 111 749 849 info@acco.com.pk

Office 2nd, 3rd Floor, Bigcity Plaza, Gulberg-III, Lahore, Pakistan
www.acco.com.pk
